

UgIFT Asset Verification Report

Field findings, service gaps and recommended actions

Client

Ministry of Finance, Planning and Economic Development

Reporting date

27 September 2026

National institutions and local governments

Central, Eastern, Northern and Western regions

Contents

Executive summary	8
1 Introduction and background.....	9
1.1 Introduction.....	9
1.2 Background to the verification	9
1.3 Justification.....	9
1.4 Objectives of the assignment	9
1.5 Scope of work.....	9
2 Approach and methodology.....	10
2.1 Preparation.....	10
2.2 What teams checked	10
2.3 Fieldwork and itinerary.....	10
2.4 Quality assurance	10
2.5 Bringing the findings together	11
2.6 How the findings are presented	11
3 Project context	12
3.1 Programme background and design.....	12
3.2 Programme components	12
3.3 Programme objectives.....	12
3.4 Delivery position at programme closure	12
4 Findings	13
4.1 Facilities expected and what was found	13
4.2 National institutions	18
4.3 Regional findings	21
4.4 Condition and use of assets.....	46
4.5 Asset management practices, gaps and actions	47
4.6 UgIFT support to service delivery	50
4.7 Summary of findings.....	52
5 Recommendations	53
5.1 Restore safe operation	53
5.2 Complete works and bring stored assets into use.....	53
5.3 Equip staff to operate and maintain assets	53
5.4 Strengthen identification and custody	53
5.5 Fund and monitor maintenance	53
5.6 Plan for continued service delivery	53
6 Conclusion	54
Appendices.....	55
Appendix A Full summary count schedule	55
Appendix B Asset totals by report category and register class.....	56
Appendix C Condition tables behind the charts	57
Appendix D Recorded value and net book value schedules	59
Appendix E Use and asset identification schedules.....	61
Appendix F Master-list reconciliation and ground-return identities	62
Appendix G Asset information for institutional handover.....	66
Appendix H Evidence supporting the findings.....	66

List of tables

Table 1: Local government field itinerary.....	10
Table 2: Programme outputs at closure	12
Table 3: Facilities on the verification master list	13
Table 4: Facilities requiring completion or preparation for use	14
Table 5: Facility reconciliation outcomes	15
Table 6: Expected facilities and the outcomes established during verification.....	16
Table 7: Examples encountered outside the master-list names	17
Table 8: Asset identification at the listed national ministries and agencies.....	18
Table 9: Central region: findings and recommended actions.....	21
Table 10: Central assets and identification by category.....	22
Table 11: Eastern region: findings and recommended actions	27
Table 12: Eastern assets and identification by category	28
Table 13: Northern region: findings and recommended actions	34
Table 14: Northern assets and identification by category.....	35
Table 15: Western region: findings and recommended actions	41
Table 16: Western assets and identification by category.....	42
Table 17: Priority actions to protect assets and restore service	49
Table 18: Whole programme and regional summary counts	55
Table 19: Assets by report category and region.....	56
Table 20: Assets by register class and region	56
Table 21: Condition classifications by report category.....	57
Table 22: Condition classifications by sub-region	58
Table 23: Recorded value and net book value by region	60
Table 24: National ministry and agency value schedule	60
Table 25: Use flags and recorded reasons by report category	62
Table 26: Identification entries by region	62
Table 27: Master-list entries accounted for through reconciliation.....	62
Table 28: Ground-return identities outside master-list names	65
Table 29: Asset information prepared for handover	66

List of figures

Figure 1: All 629 master-list entries were accounted for	13
Figure 2: Unfinished school block at Got Apwoyo Seed Secondary School, Nwoya District (Acholi)	15
Figure 3: Building works at a seed secondary school, Kiboga District (Buganda)	15
Figure 4: School block awaiting completion at Butungama Seed Secondary School, Ntoroko District (Tooro)	15
Figure 5: School buildings and courtyard at a seed secondary school, Buvuma District (Buganda)	23
Figure 6: Raised water storage tank at a seed secondary school, Buvuma District (Buganda)	23
Figure 7: Boxed pulse oximeters at a health centre, Makindye-Ssabagabo Municipal Council (Buganda)	23
Figure 8: Programme and school engraving on a chair at Budde Seed Secondary School, Butambala District (Buganda)	23
Figure 9: Desks and chairs bearing asset identification at Budde Seed Secondary School, Butambala District (Buganda)	23
Figure 10: Laboratory benches and sinks at Bweema Seed Secondary School, Buvuma District (Buganda)	23
Figure 11: Classroom desks at Bweema Seed Secondary School, Buvuma District (Buganda)	24
Figure 12: Sanitation block at Bweema Seed Secondary School, Buvuma District (Buganda)	24
Figure 13: Water tank and enclosed service structures at Bweema Seed Secondary School, Buvuma District (Buganda)	24
Figure 14: Science laboratory tables and stools at a seed secondary school, Kalangala District (Buganda)	24
Figure 15: School blocks at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)	24
Figure 16: Library shelves and reading tables at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)	24
Figure 17: Anatomical teaching model at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)	25
Figure 18: Laboratory glassware and equipment at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)	25
Figure 19: Oxygen cylinders at Kibiri HC III, Makindye-Ssabagabo Municipality (Buganda)	25
Figure 20: Wooden waiting bench at Kibiri HC III, Makindye-Ssabagabo Municipal Council (Buganda)	25
Figure 21: Sanitation block with external handwashing basins at Kibiri HC III, Makindye-Ssabagabo Municipal Council (Buganda)	25
Figure 22: Waste disposal structure at Kibiri HC III, Makindye-Ssabagabo Municipal Council (Buganda)	25
Figure 23: Infant radiant warmer at a health centre, Makindye-Ssabagabo Municipal Council (Buganda)	26
Figure 24: Office desk and other furniture at Lwamata Town Council Seed Secondary School, Kiboga District (Buganda)	26
Figure 25: Laboratory tables at Lwamata Town Council Seed Secondary School, Kiboga District (Buganda)	26
Figure 26: Library shelving at Lwamata Town Council Seed Secondary School, Kiboga District (Buganda)	26
Figure 27: ICT laboratory interior under construction at Kitawoi Seed Secondary School, Kween District (Sebei)	28
Figure 28: Unfinished laboratory building at a health centre, Sironko District (Bugisu)	28
Figure 29: Empty computer laboratory at a seed secondary school, Kween District (Sebei)	29
Figure 30: Computer sets stacked in a store at Bumufuni Seed Secondary School, Bulambuli District (Bugisu)	29
Figure 31: Pedal suction unit in packaging at Majanji HC III, Busia District (Bukedi)	29
Figure 32: Cracked health centre block above collapsed ground, Bulambuli District (Bugisu)	29
Figure 33: Stained and peeling ceiling at a health centre, Sironko District (Bugisu)	30
Figure 34: Water tank on a cracked base at a seed secondary school, Kibuku District (Bukedi)	30
Figure 35: Broken desk frame at a seed secondary school, Namisindwa District (Bugisu)	30
Figure 36: UglFT engraving on a health centre bench, Bududa District (Bugisu)	30
Figure 37: Engraving on a wheelchair armrest at Bumugibole HC III, Bulambuli District (Bugisu)	30
Figure 38: Institutional engraving on equipment at Moyok HC III, Kween District (Sebei)	30
Figure 39: Autoclave at Atar HC III, Kween District (Sebei)	31
Figure 40: Solar batteries and control equipment at Atar HC III, Kween District (Sebei)	31
Figure 41: Kangaroo care chair at Atar HC III, Kween District (Sebei)	31
Figure 42: Solar batteries at Bunangaka HC III, Bulambuli District (Bugisu)	31
Figure 43: Infant weighing scale at Buwembe HC III, Busia District (Bukedi)	31
Figure 44: Autoclave above a gas cylinder at Buwembe HC III, Busia District (Bukedi)	31
Figure 45: Computer equipment in the school ICT room at Kabeywa Seed Secondary School, Kapchorwa District (Sebei)	32
Figure 46: Library shelving and tables at Kabeywa Seed Secondary School, Kapchorwa District (Sebei)	32
Figure 47: Water tanks on a steel tower at Kabweri HC III, Kibuku District (Bukedi)	32
Figure 48: Delivery bed with side rails at Kabweri HC III, Kibuku District (Bukedi)	32
Figure 49: Anatomical skeleton teaching model at Kamonkoli Seed Secondary School, Budaka District (Bukedi)	32
Figure 50: Delivery bed with a torn mattress cover at a health centre, Busia District (Bukedi)	32
Figure 51: Binocular microscope on a trolley at Namusita HC III, Budaka District (Bukedi)	32
Figure 52: Infant weighing scales at Namusita HC III, Budaka District (Bukedi)	33
Figure 53: Laboratory benches, stools and sinks at Nansanga Seed Secondary School, Budaka District (Bukedi)	33
Figure 54: Library shelving with books at Nansanga Seed Secondary School, Budaka District (Bukedi)	33
Figure 55: Desktop computers and classroom furniture at a seed secondary school, Busia District (Bukedi)	33
Figure 56: Building works and construction materials at Ndhew Seed Secondary School, Nebbi District (West Nile)	36
Figure 57: Unfinished classroom block at Sidok Seed Secondary School, Kaabong District (Karamoja)	36
Figure 58: Latrine block under construction at Sidok Seed Secondary School, Kaabong District (Karamoja)	36

Figure 59: Computer and library block interior with furniture and stored items at Iriiri Seed Secondary School, Napak District (Karamoja)	36
Figure 60: Stacked desks, chairs and stools at a seed secondary school, Napak District (Karamoja)	36
Figure 61: Damaged drip stand at a health centre, Moroto District (Karamoja)	36
Figure 62: Programme engraving on a weighing scale at Kalemungole HC III, Moroto District (Karamoja)	37
Figure 63: Programme engraving on a delivery bed at Kalemungole HC III, Moroto District (Karamoja)	37
Figure 64: Programme engraving on a table at Kamoru HC III, Kotido District (Karamoja)	37
Figure 65: Classroom furniture with school markings at Rupa Seed School, Moroto District (Karamoja)	37
Figure 66: Water tanks on a rendered plinth and steel tower at Alerek Seed Secondary School, Abim District (Karamoja)	37
Figure 67: Laboratory reagent containers at Alerek Seed Secondary School, Abim District (Karamoja)	37
Figure 68: Health centre building, Nwoya District (Acholi)	38
Figure 69: Section of the science laboratory exterior at Iriiri Seed Secondary School, Napak District (Karamoja)	38
Figure 70: Refrigerator bearing programme identification at Kalemungole HC III, Moroto District (Karamoja)	38
Figure 71: Solar panels at Kalemungole HC III, Moroto District (Karamoja)	38
Figure 72: Patient toilet block at Kalemungole HC III, Moroto District (Karamoja)	38
Figure 73: Oxygen concentrator at Kalemungole HC III, Moroto District (Karamoja)	38
Figure 74: Suction apparatus at Kalemungole HC III, Moroto District (Karamoja)	38
Figure 75: Wheelchair with programme marking at Kalemungole HC III, Moroto District (Karamoja)	39
Figure 76: Instrument trolley with delivery instruments at Kamoru HC III, Kotido District (Karamoja)	39
Figure 77: Microscope bearing local facility identification at Kamoru HC III, Kotido District (Karamoja)	39
Figure 78: Oxygen concentrator at Kamoru HC III, Kotido District (Karamoja)	39
Figure 79: Borehole apron and pipework at Katikekire Seed School, Moroto District (Karamoja)	39
Figure 80: Computer and library block at Lopei Seed Secondary School, Napak District (Karamoja)	39
Figure 81: Water storage tanks at Lopei Seed Secondary School, Napak District (Karamoja)	39
Figure 82: Buildings at a seed secondary school, Nwoya District (Acholi)	40
Figure 83: Water storage tanks at Rengen Seed School, Kotido District (Karamoja)	40
Figure 84: Rainwater tank beside a staff house at Rupa Seed School, Moroto District (Karamoja)	40
Figure 85: Laboratory supplies and an anatomical teaching model at Rupa Seed School, Moroto District (Karamoja)	40
Figure 86: Classroom block with earthworks in the foreground at Kihungya Seed Secondary School, Buliisa District (Bunyoro)	42
Figure 87: Biology laboratory under construction at a seed secondary school, Buliisa District (Bunyoro)	42
Figure 88: Unfinished laboratory interior at Kihungya Seed Secondary School, Buliisa District (Bunyoro)	43
Figure 89: Library interior under construction at Kihungya Seed Secondary School, Buliisa District (Bunyoro)	43
Figure 90: Laboratory benches with cupboard doors detached at King Solomon Seed Secondary School, Kagadi District (Bunyoro)	43
Figure 91: Laboratory stools and other school furniture in storage, Ntoroko District (Tooro)	43
Figure 92: Clinical equipment packed among cartons at a health centre, Hoima City (Bunyoro)	43
Figure 93: Stacked classroom furniture at King Solomon Seed Secondary School, Kagadi District (Bunyoro)	43
Figure 94: Boxed projector and other equipment at King Solomon Seed Secondary School, Kagadi District (Bunyoro)	44
Figure 95: Hospital beds and screens stacked in storage at a health centre, Kagadi District (Bunyoro)	44
Figure 96: Flood-affected older health facility at Butiaba, Buliisa District (Bunyoro)	44
Figure 97: School engraving on wooden furniture at King Solomon Seed Secondary School, Kagadi District (Bunyoro)	44
Figure 98: Programme engraving on a table at Kyabasara HC III, Kagadi District (Bunyoro)	44
Figure 99: Blood pressure apparatus on a mobile stand at Butiaba HC III, Buliisa District (Bunyoro)	45
Figure 100: Office chairs at Butiaba HC III, Buliisa District (Bunyoro)	45
Figure 101: Medical-waste bins and ward beds at Butiaba HC III, Buliisa District (Bunyoro)	45
Figure 102: Laboratory centrifuge at Butiaba HC III, Buliisa District (Bunyoro)	45
Figure 103: Delivery bed and clinical furniture at a health centre, Kabarole District (Tooro)	45
Figure 104: Water tank on a masonry support at King Solomon Seed Secondary School, Kagadi District (Bunyoro)	45
Figure 105: Elevated water tank on a steel tower at King Solomon Seed Secondary School, Kagadi District (Bunyoro)	45
Figure 106: Classroom desks at King Solomon Seed Secondary School, Kagadi District (Bunyoro)	46
Figure 107: Gas cylinders and pipework at King Solomon Seed Secondary School, Kagadi District (Bunyoro)	46
Figure 108: Latrine block and paved access at Kyabasara HC III, Kagadi District (Bunyoro)	46
Figure 109: Kangaroo care chair at Kyabasara HC III, Kagadi District (Bunyoro)	46
Figure 110: Power house at Kyabasara HC III, Kagadi District (Bunyoro)	46
Figure 111: Classroom desks at a seed secondary school, Ntoroko District (Tooro)	46
Figure 112: Most eligible assets lacked a recorded mark	47
Figure 113: UgIFT identification on a desk at a seed school, Tororo District (Bukedi)	48
Figure 114: Boxed computers and related equipment in a seed school store, Nwoya District (Acholi)	49
Figure 115: Adult weighing scale with a height meter and waiting benches at Iruhura HC III, Kabarole District (Tooro)	51
Figure 116: Maternity block entrance and access ramp at Kamuli HC III, Tororo District (Bukedi)	51
Figure 117: Health centre building at Kibiri HC III, Makindye-Ssabagabo Municipal Council (Buganda)	51
Figure 118: Health centre buildings and covered walkway at Kihuukya HC III, Hoima City (Bunyoro)	51

Figure 119: Binocular microscope at Kihuukya HC III, Hoima City (Bunyoro).....	51
Figure 120: Classroom furnished with desks and a whiteboard at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)	51
Figure 121: Books displayed on library shelves at Sibanga Seed School, Manafwa District (Bugisu)	52
Figure 122: ICT laboratory block and entrance ramp at Sisiyi Seed Secondary School, Bulambuli District (Bugisu)	52
Figure 123: School furniture forms the largest asset category	57
Figure 124: The Functional classification predominates across sub-regions.....	58
Figure 125: Eastern holds the largest regional recorded value	59
Figure 126: MoFPED and MoES hold the largest ministry recorded values	60
Figure 127: Recorded use is concentrated in school furniture.....	61

List of acronyms

CIP	Capital work in progress
ID	Identifier
PDF	Portable Document Format
GOU	Government of Uganda
FY	Financial year
HC	Health centre
ICT	Information and communications technology
IDA	International Development Association
IFMIS	Integrated Financial Management Information System
KCCA	Kampala Capital City Authority
LGFC	Local Government Finance Commission
MAAIF	Ministry of Agriculture, Animal Industry and Fisheries
MDA	Ministry, department or agency
MoES	Ministry of Education and Sports
MoFPED	Ministry of Finance, Planning and Economic Development
MoGLSD	Ministry of Gender, Labour and Social Development
MoH	Ministry of Health
MoLG	Ministry of Local Government
MoLHUD	Ministry of Lands, Housing and Urban Development
MoPS	Ministry of Public Service
MoWE	Ministry of Water and Environment
MoWT	Ministry of Works and Transport
NEMA	National Environment Management Authority
OAG	Office of the Auditor General
OPM	Office of the Prime Minister
PPDA	Public Procurement and Disposal of Public Assets Authority
REAP	Resource Enhancement and Accountability Programme
UBTS	Uganda Blood Transfusion Services
UgIFT	Uganda Intergovernmental Fiscal Transfer
UGX	Uganda shillings
USD	United States dollars

Executive summary

The verification found that UgIFT buildings and equipment were supporting local services, while unfinished works, power constraints, damage and delayed installation prevented some assets from serving their intended purpose. Health staff described improved access to maternity and antenatal care. Schools described better teaching facilities and wider access to secondary education. The main follow-up is to put unused assets into service and sustain those already working.

The verification and reconciliation accounted for 629 master-list entries: 371 health centres and 258 schools. Outcomes included operating names, replacement facilities, relocated assets and sites not constructed. Section 4.1 explains how the institutions were accounted for.

Construction and service readiness need attention together. Got Apwoyo Seed Secondary School in Nwoya had not been commissioned and its computer equipment remained at district headquarters. At Ndhew and Mamba seed schools in Nebbi, unfinished buildings delayed installation. At Atego in the same district, computers were already working in older rooms while construction continued.

Power and repairs were immediate constraints. Lungulu Seed Secondary School in Nwoya held computers in storage pending a suitable power connection. Pamaka Health Centre III in Nebbi could not use oxygen equipment because of power constraints, and Busaale Health Centre III in Kayunga needed roof, door and solar repairs. Among assets recorded as out of use, 2,569 had damage, fault or repair remarks, while 483 were stored and described as good or new.

Asset identification also needs follow-up. Among 218,715 movable assets eligible for a physical mark, 49,836 had an identification entry, including 20,973 with UgIFT marking. Buildings and land are identified through site, ownership and handover records. The findings at Lungulu included equipment without identification marks. Districts should combine marking with custody and allocation decisions, particularly where equipment has moved between facilities.

The proposed priorities are to make unsafe items safe, restore essential equipment, complete works and utilities, and install usable stored assets. Facility managers should lead routine checks and minor repairs, supported by district engineers, health and education officers and the relevant technical teams. The action schedule proposes owners, timing and evidence that each action has been completed.

1 Introduction and background

1.1 Introduction

UgIFT invested in facilities and equipment to bring education and health services closer to communities and strengthen the institutions that support them. This verification examined where those assets were, how they were being used and what was needed to keep them working. The findings focus on facilities, equipment, custody, maintenance and the services available to the public.

1.2 Background to the verification

The programme ended on 31 December 2025. The Ministry of Finance, Planning and Economic Development commissioned the verification to support closure and the continued use of programme assets. The exercise covered national institutions, government seed secondary schools and health facilities upgraded from Health Centre II to Health Centre III.

1.3 Justification

Buildings and equipment need staff, utilities, maintenance and clear responsibility for their care. The verification provided a basis for handover and identified practical actions to bring unused assets into service, repair damaged items and protect assets already in use.

1.4 Objectives of the assignment

The assignment was to identify and locate programme assets, check their condition and use, assess how institutions cared for them and recommend action where assets were damaged or unserviceable. It also prepared asset information for government reporting and the Integrated Financial Management Information System (IFMIS).

1.5 Scope of work

Teams reviewed institutional asset information, inspected facilities and equipment, and spoke with the officers responsible for their use and care. The scope included buildings, furniture, medical equipment, computers, vehicles and motorcycles. Small office items such as staplers and punches and disposable school laboratory items were excluded from physical inspection.

2 Approach and methodology

The assignment followed 3 phases: preparation, field verification, and consolidation and reporting.

2.1 Preparation

The entry meeting on 29 May 2026 agreed the scope, approach and work plan. A pilot at Buloba Health Centre III and Sumbwe Seed School in Wakiso District tested the tools and visit arrangements. Teams planned visits with Accounting Officers, district health and education officers, finance staff, head teachers and health centre in-charges.

2.2 What teams checked

At each institution, the team checked the assets present, their location, identification markings, condition and use. Interviews covered repairs, servicing, breakdowns, storage, operating constraints and service benefits. Photographs documented selected assets and facilities.

2.3 Fieldwork and itinerary

National verification began on 24 July 2026 and included 10 working days of collection and repeat visits. Training for the local government teams took place on 20 and 21 August 2026. Local government fieldwork ran from 24 August to 7 September 2026, with 10 working days of collection.

The Consultant deployed 33 teams of 2 to 3 people, comprising 80 research assistants, supported by 6 supervisors and a team leader, across 176 local governments. Teams first met the local government leadership, reviewed the planned investments, visited the facilities and discussed the findings with the responsible officers.

National visits covered the ministries responsible for finance, works and transport, education, agriculture, health, water and environment, gender, public service, lands and housing, and local government. They also covered the Office of the Prime Minister, Local Government Finance Commission, National Environment Management Authority, Public Procurement and Disposal of Public Assets Authority, and Office of the Auditor General.

Table 1: Local government field itinerary

Day	Activity	Work undertaken
1	Arrival and entry	Register the visit at the Accounting Officer's office and hold the entry meeting with finance and administration.
1	Document review	Review UgIFT documents and the asset register.
2	Physical verification	Inspect identified assets in offices, health centres and schools.
2	Service interviews	Discuss functionality, maintenance and sustainability with institution and facility management.
2	Follow up and debrief	Complete follow up checks, debrief the responsible officers and finalise verification.

Table 1 sets out the sequence followed during local government visits.

2.4 Quality assurance

Regional supervisors checked daily field activity and reviewed the completed tools. The central technical team carried out spot checks and helped resolve operational questions. Teams compared institutional asset information with the items and explanations provided during visits, while supervisors referred matters requiring clarification to the team leader and field coordinator.

2.5 Bringing the findings together

The analysis brought the facility findings, interviews and asset counts together by region, institution and type of asset. Master-list names were reconciled with operating names, replacements and receiving facilities. Section 4.1 explains those outcomes, while the later sections examine use, condition, marking, maintenance and service delivery.

2.6 How the findings are presented

The findings bring together physical inspection, discussions with facility managers, photographs and the asset inventory. They distinguish assets that were available for service from equipment awaiting installation, items requiring repair and facilities requiring completion. Recommendations address the practical steps needed to put these assets to use and maintain them.

The inventory counts each asset once. School furniture, computer and support equipment, health equipment, maternity equipment, clinical furniture and buildings are presented separately. Regional summaries follow the local government location, with Rwenzori and Tooro presented together. The appendices provide the detailed counts, condition classifications and accounting basis.

3 Project context

3.1 Programme background and design

UgIFT began in financial year 2017/18 to improve the financing and delivery of local government services. Initial support focused on education and health. Later support extended the programme to water and environment and agricultural micro scale irrigation, including services for refugees and host communities.

3.2 Programme components

The programme supported a fairer system of grants to local governments, new secondary schools in underserved subcounties, and construction and upgrading of health facilities. School investments included classrooms, laboratories, administration blocks, sanitation and teachers' housing. Health investments included buildings, equipment, staff accommodation and sanitation.

It also supported local government planning, budgeting, procurement and infrastructure management, together with performance assessment and technical support. National institutions received equipment and transport to support programme administration and oversight.

3.3 Programme objectives

The programme sought more adequate and predictable support, fairer allocation of resources and stronger oversight of local services. Its intended result was wider access to education, health, water and irrigation services and better management of the facilities and resources used to provide them.

3.4 Delivery position at programme closure

At closure, 196 of the 259 seed schools in the programme output account were complete and 189 were operational. The health output account showed 354 of 373 upgrades and new constructions complete. These closure figures show the delivery position before the later verification visits; section 4 describes the facilities and assets found during those visits.

Table 2: Programme outputs at closure

Sector	Outputs
Education	196 of 259 seed schools complete; 189 operational.
Health	354 of 373 health facility upgrades and new constructions complete.
Water and environment	758 piped water systems; 5,398 point water sources; 7,082 water supply systems rehabilitated; 325 designs completed; 256 sanitation facilities.
Micro scale irrigation	More than 6,235 irrigation systems installed, covering 4,843 hectares; 632 demonstration sites in 135 local governments.
Refugee host services	51 primary schools and 35 health facilities transitioned into local government services.
Blood banks	Arua and Hoima regional blood banks completed and commissioned; Soroti Regional Blood Bank rehabilitated.

Table 2 describes the position at programme closure. The September 2026 field findings are presented separately below.

4 Findings

4.1 Facilities expected and what was found

The exercise accounted for 629 entries on the verification master list: 258 schools and 371 health centres. Follow-up established which facilities retained their original names, which had replacements or relocated assets, and which listed institutions had not received programme support. These distinctions matter because a name on the list does not, by itself, demonstrate that the intended facility and its assets are available for service.


The findings identified 10 entries reported nonexistent or not constructed, four replacements, 30 name corrections, three institutions outside UgIFT, three cases of relocated assets and five existing facilities without UgIFT assets. The cases below explain the differences and the action needed. Identity corrections should be settled alongside decisions on incomplete works, custody, handover and operational readiness so that the programme account reflects where services and assets are actually located.

Table 3: Facilities on the verification master list

Region	Health centres	Schools	Total
Central	62	37	99
Eastern	93	76	169
Northern	92	74	166
Western	124	71	195
Total	371	258	629

Table 3 gives the facility list against which the teams carried out verification and reconciliation. Every master-list facility was accounted for through verification or reconciliation.

All 629 master-list entries were accounted for

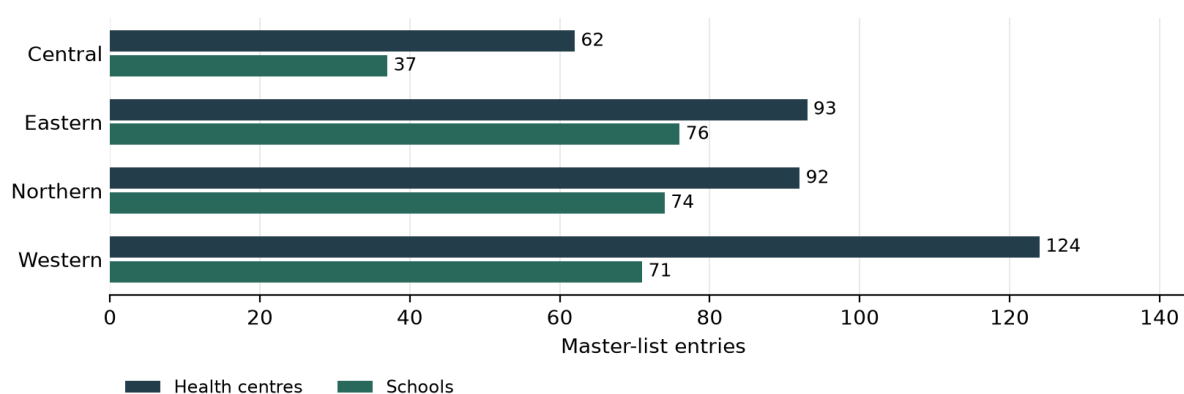

Counts include facilities accounted for through reconciliation.

Figure 1: All 629 master-list entries were accounted for

4.1.1 Construction and readiness for service

Table 4: Facilities requiring completion or preparation for use

Location	Expected position and field finding	Gap or service implication	Recommended action
Got Apwoyo Seed Secondary School, Nwoya	Expected: Got Apwoyo was intended to provide secondary education with completed buildings and installed ICT equipment. Found: The team found construction continuing and the school uncommissioned. Its ICT package remained at Nwoya District headquarters, while delivered furniture and structures had not been brought into use.	The assets were not yet supporting teaching at the intended school, and custody was divided between the district and the site.	Nwoya District and the Ministry of Education should set a completion and handover plan, check the stored equipment, and arrange installation, testing and signed transfer when the school is ready.
Bukibologoto Health Centre, Bulambuli	Expected: Bukibologoto was listed as complete and was intended to provide care from the constructed health facility. Found: The team found that mudslides had damaged the works before completion. A corner was undermined and a wall cracked. Care was being provided at Simu subcounty offices, with equipment held in district stores.	The planned facility was unavailable for its intended use, and the temporary service and storage arrangements needed a lasting solution.	Bulambuli District and the Ministry of Health should obtain an engineering assessment, decide on repair or relocation, inventory the equipment and provide for continuing care.
Kyangwali Seed Secondary School, Kikuube	Expected: Kyangwali school needed completed works, electricity, security and handover to use its assets fully. Found: The team recorded continuing construction. The school reported a lack of electricity and an incomplete perimeter fence, and the facility had not been handed over.	Finishing the buildings alone would not make the school ready: power, security and responsibility for the assets also remained unresolved.	Kikuube District, the Ministry of Education and the contractor should close these requirements through one readiness plan, followed by joint testing and handover. The plan should name who will operate, safeguard and maintain the assets.
Sidok Seed Secondary School, Kaabong	Expected: Sidok school needed completed buildings and checked equipment before the investment could support full operations. Found: The team found blocks, a kitchen and toilets under construction, with termite workings on the plaster of two blocks. The school consignment remained unopened and its contents had not been counted.	Both unfinished works and unchecked equipment prevented a complete assessment of readiness for use.	Kaabong District should secure completion and treatment of the affected works, then arrange a witnessed opening, count and condition check of the equipment. Accepted items should be recorded, assigned to custodians and issued for use.
Buwagogo Seed Secondary School, Manafwa	Expected: Buwagogo school was intended to use its supplied ICT equipment for teaching. Found: The team found the March 2024 ICT consignment still boxed in the store, with contractor installation pending and commissioning delayed.	Delivery had not translated into operational ICT capacity. Equipment continued to require secure custody while installation remained outstanding.	Manafwa District and the Ministry of Education should agree an installation and commissioning date with the contractor, reconcile the stored equipment against delivery records and test it before acceptance. The handover should assign responsibility for operation, maintenance and reporting of faults.



Figure 2: Unfinished school block at Got Apwoyo Seed Secondary School, Nwoya District (Acholi)



Figure 3: Building works at a seed secondary school, Kiboga District (Buganda)



Figure 4: School block awaiting completion at Butungama Seed Secondary School, Ntoroko District (Tooro)

4.1.2 Facilities that differed from the programme list

Table 5: Facility reconciliation outcomes

Outcome	Entries
Does not exist or was not constructed under the programme	10
Replaced by another facility	4
Operates under another name	30
Not a UgIFT beneficiary	3
Assets relocated to another facility or held at district	3
Exists with no UgIFT assets	5

Table 5 groups 55 reconciled entries. These include naming and replacement decisions for facilities that also had verification evidence; the 55 entries are not a separate count of unvisited facilities. Appendix F gives the outcome for each entry.

Table 6: Expected facilities and the outcomes established during verification

Location	Expected position and field finding	Gap or service implication	Recommended action
Olok Health Centre, Pader	Expected: Olok was listed as a completed health facility intended to serve its catchment in Pader. Found: The district health officer confirmed to the verification team that Olok Health Centre had not been constructed and did not exist in the district.	The completed entry could not be matched to the intended facility. The reason for non-construction requires a documented resolution.	Pader District and the Ministry of Health should reconcile the approved project, construction and payment records, correct the beneficiary schedule and decide how the intended health-service need will be met.
Busia Eastern Division health-centre entry, Busia Municipal Council	Expected: The beneficiary schedule should identify the particular health facility supported in Busia Municipality. Found: Reconciliation confirmed that no health facility called Busia Eastern Division existed. A separate return identified Sofia Health Centre III within Eastern Division.	An administrative division had been used as a facility name. The available confirmation did not identify Sofia as its replacement or establish that the two names referred to the same beneficiary.	The municipality and Ministry of Health should resolve the original beneficiary identity and document the programme status of Sofia before linking or changing the two entries.
Ngomoromo, Oweko, Musandama and Loinya health centres, Lamwo, Nebbi, Ntoroko and Maracha	Expected: The beneficiary schedule should name the facility that received each planned investment. Found: Supervisors confirmed that Pangira replaced Ngomoromo in Lamwo, Pamaka replaced Oweko in Nebbi, Butungama replaced Musandama in Ntoroko, and Liko replaced Loinya in Maracha. Liko was already listed separately.	The programme account needs to link each original entry to its confirmed replacement to prevent duplicate counting and identify the service location.	The districts and Ministry of Health should attach the replacement decisions, link the original projects to their recipients and retain one active facility identity for each recipient.
Alangi, Ther-uru and Abanga, Zombo	Expected: Asset locations and custodians should agree with the facilities holding and using the equipment. Found: The supervisor confirmed that Alangi, Ther-uru and Abanga existed, but their UgIFT assets had moved respectively to Amwonyo Health Centre, Atyak Health Centre and Kango Seed Secondary School.	The original beneficiary names no longer described where the assets were held. Custody, location and the service arrangements at the original sites needed to be made clear.	Zombo District should reconcile transfer approvals and signed receipts with both sets of inventories, name the current custodians and confirm how the original catchments are served.
Alira Health Centre and Kiziranfumbi Seed Secondary School, Oyam and Kikuube	Expected: The programme beneficiary schedule should include institutions supported under UgIFT. Found: The later Oyam clarification confirmed that Alira Health Centre existed but was not among the facilities upgraded under UgIFT. The supervisor also confirmed that Kiziranfumbi Seed Secondary School in Kikuube was outside the programme.	The list confused the existence of an institution with its eligibility as a UgIFT beneficiary. Alira had initially been reported absent, but that account was corrected.	The local governments and sector ministries should approve the scope corrections, remove the institutions from the active UgIFT schedule and preserve the reasons for the changes.

Location	Expected position and field finding	Gap or service implication	Recommended action
Pandwong Health Centre; Bumbaire, Kyamuhunga and Kashenshero schools; Rwamujojo Health Centre, Kitgum Municipal Council, Bushenyi, Mitooma and Sheema Municipal Council	Expected: Each listed beneficiary should have a supported account of the programme assistance it received. Found: Supervisors confirmed that Pandwong Health Centre, Bumbaire and Kyamuhunga schools, Kashenshero school and Rwamujojo Health Centre existed but had not benefited from UglIFT assets.	Their appearance on the beneficiary list did not establish delivery. The cause of the difference between the list and the reported benefits needs to be resolved.	The responsible districts, municipalities and sector ministries should check beneficiary approvals and delivery records, then correct the schedule or record an approved outstanding delivery with an accountable officer and follow-up date.
Bussi/Zinga and Dabani/Buwumba, Wakiso and Busia	Expected: Each facility should have one stable identity, with local and former names linked to it. Found: Bussi was confirmed to be the village name for the already-listed Zinga Health Centre in Wakiso. In Busia, the Buwumba return was reconciled to the master entry named Dabani.	Different names could make one facility appear to be two, distort coverage and separate its asset history from the correct institution.	The districts should adopt the confirmed operating names, retain the old names as aliases and link the beneficiary, project and asset information to one facility identifier. Zinga should be counted once.

4.1.3 Facilities and names encountered outside the master list

Teams submitted information under 24 facility names that had no confirmed match to the verification master list. Follow-up expressly confirmed Rukoki General Hospital, Silumira Health Centre III and Bukuuku Community Seed Secondary School as additional programme beneficiaries. Their inclusion in the approved programme account should be regularised.

The remaining names should be resolved through the same checks of facility identity, programme approval and asset custody. Some entries came from combined returns, and Onywako was expressly reported without a physical inspection. All 24 return names are shown separately from the 629 master-list entries while the outstanding identity and scope decisions are completed.

Table 7: Examples encountered outside the master-list names

Location	Expected position and field finding	Gap or service implication	Recommended action
Rukoki General Hospital, Kasese Municipality	Expected: Confirmed beneficiaries should be included in the programme account. Found: The supervisor confirmed that Rukoki General Hospital was a UglIFT beneficiary in Kasese Municipality, although it was absent from the master list used for verification.	The programme list omitted a confirmed recipient.	The Ministry of Health and municipality should approve the beneficiary entry and link its asset information to a stable facility identifier.
Silumira Health Centre III, Kakumiro	Expected: The beneficiary schedule should include supported health facilities. Found: The supervisor confirmed that Silumira Health Centre III had benefited in Kakumiro but was not on the master list.	The facility was missing from the list used to plan and account for verification.	Kakumiro District and the Ministry of Health should approve the addition and connect the beneficiary decision to the facility asset inventory.

Location	Expected position and field finding	Gap or service implication	Recommended action
Bukuuku Community Seed Secondary School, Fort Portal City	Expected: Confirmed seed-school beneficiaries should appear in the programme account, with assets handed over for full use. Found: Bukuuku was confirmed as an additional beneficiary. The team recorded improved science and computer teaching following laboratory construction, while some asset handover remained pending.	The school was omitted from the master list and handover was incomplete.	The city and Ministry of Education should regularise the beneficiary entry and complete joint handover of the outstanding assets.

4.2 National institutions

National institutions held 15,793 assets, including office equipment, vehicles and assets in hospitals and blood banks. The main management questions were whether assets remained in use, could be identified and had clear responsibility for custody and maintenance. Detailed valuation schedules are provided in Appendix D.

Table 8: Asset identification at the listed national ministries and agencies

Institution	Assets	Eligible	Marked	Unmarked
MoFPED	458	458	282	176
MoWT	88	88	79	9
MoES	1,371	1,371	395	976
MAAIF	1,975	1,975	1,162	813
MoH	264	264	46	218
OPM	10	10	10	0
MoWE	2,939	2,939	2,897	42
MoGLSD	10	10	8	2
NEMA	6	6	1	5
PPDA	5	5	5	0
OAG	20	20	20	0
MoLG	13	13	8	5
MoLHUD	26	26	12	14

Table 8 identifies movable assets requiring a physical mark. Buildings and land are identified through property and site records. Each equipment mark should link to the asset number, institution and current custodian.

Accounting Officers should complete the outstanding marking, keep custody and location details current, and include serviceable equipment in routine maintenance. Damaged items require technical assessment and a decision on repair or disposal.

4.2.1 Ministry of Finance, Planning and Economic Development

MoFPED held 194 ICT items, 145 other assets, 99 furniture and fittings and 20 transport assets.

Expected: Staff computers should support their workload, and portable equipment should remain identifiable and accountable. Found: Most computers were working, but some keyboards and power-backup units had failed, and some older computers were freezing. Laptop losses were supported by police letters. The team also reported difficulty obtaining some laptops for engraving.

Gap: Equipment reliability, follow-up of lost assets and completion of identification each required a specific management response. Recommended action: The ministry should assess the failed accessories and freezing computers, follow up the reported laptop losses, and arrange a supervised exercise to identify and mark all remaining portable equipment.

Expected: Furniture should remain assigned to a location and custodian when offices move. Found: When programme staff moved to premises already furnished, their earlier furniture was left in the old building. Some remained in store, while staff said other items had gone to different offices.

Gap: The move had split the furniture between storage and other offices, requiring confirmation of its present custody and use. Recommended action: The ministry should inspect the old store and recipient offices, confirm the condition and custodian of each item, and approve reuse or other appropriate treatment of furniture no longer required.

4.2.2 Ministry of Works and Transport

MoWT held 60 ICT items, 27 other assets and 1 transport asset.

Repairs and servicing of the Toyota Hilux pickup were handled by MoFPED. The custody and maintenance arrangements should remain clear during handover.

Expected: Installed office and conferencing equipment should support the secretariat and carry a traceable asset identity. Found: The secretariat reported that the installed photocopier supported its daily work. The video-conferencing system was installed and functioning, but it had not been engraved or included in the asset list presented for verification.

Gap: An operational system still required clear identification and custody. Recommended action: The ministry should identify the conferencing system and its components, assign a custodian, and apply a suitable durable identifier without damaging the equipment.

4.2.3 Ministry of Education and Sports

MoES held 1,371 ICT items.

4.2.4 Ministry of Agriculture, Animal Industry and Fisheries

MAAIF held 1,138 ICT items and 837 other assets.

The ministry had working laptops and printers carrying programme asset identifiers. Keeping those identifiers linked to the equipment and its custodian will support continued accountability after programme closure. Routine condition checks should identify new faults and keep usable equipment in service.

4.2.5 Ministry of Health

MoH held 200 other assets, 39 ICT items and 25 transport assets.

Expected: Office equipment in use should be identifiable by a durable asset mark. Found: Two heavy-duty printers, one at the Industrial Area engineering office and one at headquarters, were in use and in good condition but unengraved. One headquarters laptop was also recorded without engraving.

Gap: Working equipment at separate offices still lacked the marking needed for straightforward physical identification. Recommended action: The ministry should mark these items, link the marks to their serial numbers and office locations, and obtain custody confirmation from the receiving units.

4.2.6 Office of the Prime Minister

OPM held 10 ICT items.

Damaged laptops were out of use. The institution should assess repair needs and return serviceable equipment to use.

Expected: Computers should have enough capacity for the work assigned to their users. Found: Users reported that the capacity of the HP Envy i3 laptops was below the volume of work handled, although the machines were described as being in fair condition.

Gap: A usable laptop could still be poorly matched to the workload of its user. Recommended action: The office should assess the requirements of the affected users and decide whether upgrading, reallocating or replacing the laptops would provide suitable capacity.

4.2.7 Ministry of Water and Environment

MoWE held 2,735 ICT items and 204 other assets.

Expected: Portable tablets should carry an asset identifier and have an assigned custodian. Found: Ten Apple tablets were recorded without engraving.

Gap: Portable equipment required an identification method that would allow each unit to be traced to its user and location. Recommended action: The ministry should apply suitable durable identifiers, link them to serial numbers, and confirm custody before the next physical check.

4.2.8 Ministry of Gender, Labour and Social Development

MoGLSD held 10 ICT items.

Laptops serving Finance and Administration were functional and engraved. Two tablets, one for Finance and Administration and the other for Youth and Children Affairs, were functional but unengraved. The ministry should mark the tablets and link their identifiers to the units and officers responsible for them.

4.2.9 National Environment Management Authority

NEMA held 6 ICT items.

Expected: Computers and shared office equipment should remain identifiable wherever they are used. Found: Four Lenovo laptops serving the executive office and environmental audit, together with a heavy-duty printer, were recorded as functional but not engraved.

Gap: The equipment could support work, but lacked a durable identifying mark. Recommended action: The authority should mark the five items, record their serial numbers and custodians, and include them in regular physical checks.

4.2.10 Public Procurement and Disposal of Public Assets Authority

PPDA held 3 other assets and 2 ICT items.

The authority had functioning laptops, a tablet and a printer assigned to its legal and strategy/planning units. These items carried programme identifiers. The authority should keep the identifiers linked to current custodians and update custody whenever equipment moves between units.

4.2.11 Office of the Auditor General

OAG held 18 ICT items and 2 transport assets.

The office had working laptops, printers and two pickup vehicles. The pickups had changed registration numbers. The office should retain the link between the earlier and current registrations, the chassis numbers and the assigned custodians so that each vehicle remains traceable.

4.2.12 Ministry of Local Government

MoLG held 12 ICT items and 1 transport asset.

The District Administration unit had a working pickup, photocopier and computer equipment. Two laptops and a desktop set, including its keyboard and mouse, lacked engraving. The ministry should mark the unengraved equipment and confirm its location and custodian while keeping the working assets in service.

4.2.13 Ministry of Lands, Housing and Urban Development

MoLHUD held 24 transport assets and 2 other assets.

4.2.14 Other national holdings

Hospital holdings and assets of the Uganda Blood Transfusion Services (UBTS), Kampala Capital City Authority (KCCA) and the MODV vote are included in the national inventory. Their quantities and values are retained in the appendices. Custody, identification and maintenance responsibilities should remain with the institution that holds and uses each asset.

4.3 Regional findings

4.3.1 Central region

The Central region master list covered 62 health centres and 37 schools. The asset inventory covered 28,192 items. Among 27,251 movable assets eligible for marking, 6,086 had an identification entry and 21,165 had none recorded. Buildings and land are identified through property and site records.

What was found

Central region showed both service gains and repair needs. At Lukale Health Centre III in Buvuma, staff said the maternity ward enabled women to give birth locally instead of crossing water and gave them greater privacy. At Musiitwa Seed Secondary School in Kayunga, new facilities improved access to secondary education, and the irrigation system supported practical teaching and food production.

Busaale Health Centre III in Kayunga used Primary Health Care funds for maintenance and reviewed asset condition quarterly. The maternity roof was leaking, door hinges needed repair and the solar system required a replacement battery. At Musiitwa, furniture and fittings were checked each term, but broken items remained out of use until the school could fund repairs.

The immediate actions are to repair Busaale's roof, doors and solar system and clear the furniture repair backlog at Musiitwa. The school also reported attendance pressures linked to long walking distances and pupils' involvement in petty trade. School management and the district education office should address these alongside the physical improvements.

Gaps and actions

Table 9: Central region: findings and recommended actions

Location	Expected position and field finding	Gap or service implication	Recommended action
Busaale Health Centre III, Kayunga	The facility used Primary Health Care funds for maintenance and kept a quarterly condition record.	The maternity roof leaked, door hinges were damaged and the solar battery needed replacement.	Cost and complete the roof, door and battery repairs, then confirm that the affected rooms and solar system are working.
Musiitwa Seed Secondary School, Kayunga	The school checked furniture and fittings each term and repaired them when funds allowed.	Broken furniture remained out of use while funding was arranged.	Prepare a termly repair list and fund repairs in order of their effect on teaching and safety.

Location	Expected position and field finding	Gap or service implication	Recommended action
Musiitwa Seed Secondary School, Kayunga	The school improved access to secondary education and used irrigation equipment for teaching and food production.	Long walking distances and pupils' engagement in petty trade affected attendance.	Maintain the practical teaching equipment and work with parents and the district education office on attendance barriers.
Lukale Health Centre III, Buvuma	Staff reported that the maternity ward allowed women to give birth locally and with greater privacy.	Benefit to sustain.	Protect the service through routine care of the maternity building and equipment.
Kijuna Health Centre III, Kassanda	Expected: Patient equipment and basic utilities should be available when care is needed. Found: The wheelchairs were not functional, and a failed water pump left the facility with inadequate water. Inadequate power also prevented full use of electronic equipment.	The facility faced separate constraints on patient movement, water supply and equipment use.	Kassanda District should arrange technical assessment and repair of the wheelchairs and pump, restore a dependable power supply and test the affected equipment before returning it to use.
Kikandwa Health Centre III, Kassanda	Expected: The health facility should provide powered equipment, durable buildings and secure custody of its assets. Found: Electronic equipment could not be used because reliable electricity and solar power were unavailable. Storage for damaged assets was inadequate, the facility lacked a perimeter fence, and defects were observed in flooring and skirting.	Power, secure storage and correction of building defects remained necessary for full and safe use.	Kassanda District should agree a joint power, security and defects plan, provide secure temporary storage, and have technical staff verify repairs and equipment operation.
Kyasansuwa Health Centre III, Kassanda	Expected: Computer equipment should support administration and reporting, while floors and bathrooms should remain usable and easy to maintain. Found: The facility reported three computers completely damaged following unstable power and surges. Poor floor finishes and defective staff bathroom levels were also observed.	Unstable electricity threatened the remaining electronics, while defective finishes and drainage needed correction.	Kassanda District should stabilise and protect the electrical supply, assess the three computers for repair or replacement, and correct the floor and bathroom defects under technical supervision.

Table 10: Central assets and identification by category

Asset category	Assets	Eligible	Marked	Unmarked
Clinical equipment	3,926	3,926	763	3,163
Clinical furniture	2,965	2,965	1,047	1,918
Other assets	3,522	3,521	363	3,158
Health centre ICT equipment	32	32	1	31
Maternity ward equipment	1,372	1,372	472	900
Building blocks	940	-	-	-
School computers and related equipment	1,365	1,365	334	1,031
School support equipment	76	76	10	66
Other ICT equipment	80	80	2	78
School furniture	13,911	13,911	3,092	10,819

Asset category	Assets	Eligible	Marked	Unmarked
Vehicles and motorcycles	3	3	2	1

Table 10 shows the assets covered and the outstanding identification work by category. A dash means physical marking does not apply. Sub-region counts and condition classifications are in the appendices.

Field photographs from Central



Figure 5: School buildings and courtyard at a seed secondary school, Buvuma District (Buganda)



Figure 6: Raised water storage tank at a seed secondary school, Buvuma District (Buganda)



Figure 7: Boxed pulse oximeters at a health centre, Makindye-Ssabagabo Municipal Council (Buganda)



Figure 8: Programme and school engraving on a chair at Budde Seed Secondary School, Butambala District (Buganda)



Figure 9: Desks and chairs bearing asset identification at Budde Seed Secondary School, Butambala District (Buganda)



Figure 10: Laboratory benches and sinks at Bweema Seed Secondary School, Buvuma District (Buganda)



Figure 11: Classroom desks at Bweema Seed Secondary School, Buvuma District (Buganda)



Figure 12: Sanitation block at Bweema Seed Secondary School, Buvuma District (Buganda)



Figure 13: Water tank and enclosed service structures at Bweema Seed Secondary School, Buvuma District (Buganda)



Figure 14: Science laboratory tables and stools at a seed secondary school, Kalangala District (Buganda)



Figure 15: School blocks at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)



Figure 16: Library shelves and reading tables at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)




Figure 17: Anatomical teaching model at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)



Figure 18: Laboratory glassware and equipment at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)



Figure 19: Oxygen cylinders at Kibiri HC III, Makindye-Ssabagabo Municipality (Buganda)



Figure 20: Wooden waiting bench at Kibiri HC III, Makindye-Ssabagabo Municipal Council (Buganda)



Figure 21: Sanitation block with external handwashing basins at Kibiri HC III, Makindye-Ssabagabo Municipal Council (Buganda)



Figure 22: Waste disposal structure at Kibiri HC III, Makindye-Ssabagabo Municipal Council (Buganda)



Figure 23: Infant radiant warmer at a health centre, Makindye-Ssabagabo Municipal Council (Buganda)



Figure 24: Office desk and other furniture at Lwamata Town Council Seed Secondary School, Kiboga District (Buganda)



Figure 25: Laboratory tables at Lwamata Town Council Seed Secondary School, Kiboga District (Buganda)



Figure 26: Library shelving at Lwamata Town Council Seed Secondary School, Kiboga District (Buganda)

4.3.2 Eastern region

The Eastern region master list covered 93 health centres and 76 schools. The asset inventory covered 84,681 items. Among 82,099 movable assets eligible for marking, 19,830 had an identification entry and 62,269 had none recorded. Buildings and land are identified through property and site records.

What was found

At Kagumba Health Centre III in Kamuli, staff linked the new maternity ward to increased use of delivery and antenatal services. The facility kept an asset condition book, but staff identified pressure on housing and a need for outpatient, laboratory, storage and kitchen space. These needs should be assessed against the services now provided at the facility.

Repairs had returned broken furniture to use at Kagumba Seed Secondary School during the second term. In contrast, Sikuda Seed Secondary School in Busia had broken desks and a cracked laboratory stool that was still being used. At Bubago Health Centre in Kamuli, staff needed training to operate and maintain an oxygen concentrator.

Equipment from Bumunji, Buwembe and Majanji health centres in Busia had been transferred to Masafu Hospital. The district should confirm the continuing service need at each location and keep responsibility for

the transferred equipment clear. Repairing unsafe furniture and training the oxygen equipment users are immediate priorities.

Gaps and actions

Table 11: Eastern region: findings and recommended actions

Location	Expected position and field finding	Gap or service implication	Recommended action
Kagumba Health Centre III, Kamuli	Staff reported increased maternity and antenatal service use, and the facility kept an asset condition book.	Staff housing was under pressure; outpatient, laboratory, storage and kitchen space were identified as needs.	Assess the supporting space against patient demand and include the agreed works in the district health investment plan.
Kagumba Seed Secondary School, Kamuli	The school reported that broken furniture had been repaired during the second term.	Practice to sustain.	Continue condition checks and scheduled furniture repairs before each term.
Sikuda Seed Secondary School, Busia	Broken desks and a cracked laboratory stool were found.	The cracked stool was still in use.	Withdraw unsafe furniture from use and repair or replace it before returning it to classrooms or laboratories.
Bubago Health Centre, Kamuli	Staff identified difficulty operating and maintaining an oxygen concentrator.	Equipment use depended on stronger user and basic maintenance skills.	Arrange practical user training and a technical check, then demonstrate operation with the staff responsible for the equipment.
Bumunji, Buwembe and Majanji health centres; Masafu Hospital, Busia	Equipment had been transferred from the health centres to Masafu Hospital.	Allocation and custody require confirmation.	Confirm the receiving custodian, location and service need, and retain signed transfer and receipt documentation.
Nansanga Seed Secondary School, Budaka	Expected: The supplied desktop computers should be installed and available for teaching. Found: The school lacked reliable power, and twenty-seven of its twenty-eight desktops remained packed.	Most of the supplied computer capacity had not reached classroom use because a basic operating requirement was unresolved.	Budaka District and the school should settle the power connection or suitable alternative, arrange installation and testing, and confirm the number of computers available to learners.
Muhula Seed Secondary School, Butaleja	Expected: The school should receive completed buildings and tested equipment before formal handover and operation. Found: The contractor had not handed over the school, and it was not operating. Buildings showed cracks, an air conditioner remained boxed with a missing fan, and the installed water pump was not working.	Construction completion, equipment completeness and successful testing had not come together to make the school ready.	Butaleja District and the Ministry of Education and Sports should agree a defects and handover schedule with the contractor, rectify the works, complete the equipment and witness operational tests before handover.
Sop Sop Health Centre III, Tororo	Expected: Delivered equipment should be accompanied by the skills and accessories needed to use it. Found: The facility reported that much of its equipment remained in store because staff did not know how to operate it. Oxygen equipment had arrived without cylinders. Tuberculosis testing and maternity services had nevertheless improved.	Equipment delivery had not been matched consistently with user training and a complete operating package.	Tororo District and the Ministry of Health should arrange practical training at the facility, confirm the required oxygen components, and check that trained staff can safely use each released item.

Location	Expected position and field finding	Gap or service implication	Recommended action
Bunamono Health Centre III, Bududa	Expected: The installed water system should supply the staff houses, and supplied clinical equipment should be ready for use. Found: The water tank was not working and the solar pump was not connected, leaving the staff houses without water. A supplied laboratory stand remained boxed because staff could not assemble it, and a glucometer lacked test strips.	The facility needed installation, demonstration and consumables to turn delivered assets into usable services.	Bududa District should complete and test the water connection, arrange assembly and user demonstration for the laboratory stand, and establish a supply of compatible glucometer strips.

Table 12: Eastern assets and identification by category

Asset category	Assets	Eligible	Marked	Unmarked
Clinical equipment	8,249	8,249	764	7,485
Clinical furniture	6,877	6,877	936	5,941
Other assets	13,526	13,521	1,406	12,115
Health centre ICT equipment	107	107	4	103
Maternity ward equipment	1,753	1,753	110	1,643
Building blocks	2,577	-	-	-
School furniture	46,351	46,351	15,529	30,822
School computers and related equipment	4,462	4,462	983	3,479
School support equipment	423	423	81	342
Other ICT equipment	347	347	12	335
Vehicles and motorcycles	9	9	5	4

Table 12 shows the assets covered and the outstanding identification work by category. A dash means physical marking does not apply. Sub-region counts and condition classifications are in the appendices.

Field photographs from Eastern



Figure 27: ICT laboratory interior under construction at Kitawoi Seed Secondary School, Kween District (Sebei)



Figure 28: Unfinished laboratory building at a health centre, Sironko District (Bugisu)



Figure 29: Empty computer laboratory at a seed secondary school, Kween District (Sebei)



Figure 30: Computer sets stacked in a store at Bumufuni Seed Secondary School, Bulambuli District (Bugisu)



Figure 31: Pedal suction unit in packaging at Majanji HC III, Busia District (Bukedi)



Figure 32: Cracked health centre block above collapsed ground, Bulambuli District (Bugisu)



Figure 33: Stained and peeling ceiling at a health centre, Sironko District (Bugisu)



Figure 34: Water tank on a cracked base at a seed secondary school, Kibuku District (Bukedi)



Figure 35: Broken desk frame at a seed secondary school, Namisindwa District (Bugisu)



Figure 36: UglIFT engraving on a health centre bench, Bududa District (Bugisu)



Figure 37: Engraving on a wheelchair armrest at Bumugibole HC III, Bulambuli District (Bugisu)



Figure 38: Institutional engraving on equipment at Moyok HC III, Kween District (Sebei)



Figure 39: Autoclave at Atar HC III, Kween District (Sebei)



Figure 40: Solar batteries and control equipment at Atar HC III, Kween District (Sebei)



Figure 41: Kangaroo care chair at Atar HC III, Kween District (Sebei)



Figure 42: Solar batteries at Bunangaka HC III, Bulambuli District (Bugisu)



Figure 43: Infant weighing scale at Buwembe HC III, Busia District (Bukedi)



Figure 44: Autoclave above a gas cylinder at Buwembe HC III, Busia District (Bukedi)



Figure 45: Computer equipment in the school ICT room at Kabeywa Seed Secondary School, Kapchorwa District (Sebei)



Figure 46: Library shelving and tables at Kabeywa Seed Secondary School, Kapchorwa District (Sebei)



Figure 47: Water tanks on a steel tower at Kabweri HC III, Kibuku District (Bukedi)



Figure 48: Delivery bed with side rails at Kabweri HC III, Kibuku District (Bukedi)



Figure 49: Anatomical skeleton teaching model at Kamonkoli Seed Secondary School, Budaka District (Bukedi)



Figure 50: Delivery bed with a torn mattress cover at a health centre, Busia District (Bukedi)



Figure 51: Binocular microscope on a trolley at Namusita HC III, Budaka District (Bukedi)



Figure 52: Infant weighing scales at Namusita HC III, Budaka District (Bukedi)



Figure 53: Laboratory benches, stools and sinks at Nansanga Seed Secondary School, Budaka District (Bukedi)



Figure 54: Library shelving with books at Nansanga Seed Secondary School, Budaka District (Bukedi)



Figure 55: Desktop computers and classroom furniture at a seed secondary school, Busia District (Bukedi)

4.3.3 Northern region

The Northern region master list covered 92 health centres and 74 schools. The asset inventory covered 52,303 items. Among 50,912 movable assets eligible for marking, 12,037 had an identification entry and 38,875 had none recorded. Buildings and land are identified through property and site records.

What was found

Unfinished construction delayed the use of delivered equipment at several schools. Got Apwoyo Seed Secondary School in Nwoya had not been commissioned; furniture was on site and computer equipment remained at district headquarters. At Ndhew and Mamba Seed Schools in Nebbi, unfinished buildings also delayed installation, with science equipment held at district headquarters. Mamba was using older structures to accommodate its computers.

Conditions differed within Nebbi. Atego Seed School was still under construction, but its computers were connected and working in older rooms. Staff reported power surges. This calls for completion of the planned facilities and a stable electricity supply while protecting the equipment already in use.

Power also restricted use of completed facilities. Lungulu Seed Secondary School in Nwoya kept computers and related equipment in storage pending a suitable power connection; the stored equipment included defective desktop units requiring separate attention. At Pamaka Health Centre III in Nebbi, a nonfunctional solar system and power constraints prevented use of oxygen equipment. Rupa Seed School in Moroto hired a generator for practical lessons and used the library and computer laboratory block as dormitories.

Some equipment had yet to be brought into use. Neonatal respiratory equipment at Kalemungole Health Centre III in Moroto remained in an unopened carton and treatment trolleys were still wrapped. Equipment intended for Todora Health Centre III in Nwoya had been sent to Paraa during construction and had not all been transferred back. Each case needs a clear decision on installation, allocation and custody.

Todora referred major medical equipment repairs through the District Health Officer to the Gulu Regional Referral Hospital technical team. Lungulu funded minor repairs from school revenue and sought district

technical support. Its assets also required engraving. At Pamaka, staff reported greater community confidence and patient attendance, alongside pressure on staffing.

Gaps and actions

Table 13: Northern region: findings and recommended actions

Location	Expected position and field finding	Gap or service implication	Recommended action
Got Apwoyo Seed Secondary School, Nwoya	The school was under construction and had not been commissioned. Delivered furniture was on site and computer equipment was held at district headquarters.	Incomplete buildings prevented commissioning and installation.	Agree a costed completion and handover plan, then move and install the equipment when the rooms and utilities are ready.
Ndhew Seed School, Nebbi	Buildings were incomplete, with computer and science equipment held at district headquarters and furniture not yet installed.	Delivery of equipment had not translated into an equipped school.	Complete the outstanding works and sanitation facilities and coordinate furniture and equipment installation with handover.
Mamba Seed School, Nebbi	Construction was incomplete. Computers were temporarily accommodated in older structures, while science equipment remained at district headquarters.	The planned laboratory and computer spaces were not ready for full installation.	Complete and commission the buildings, install the equipment and confirm safe operation before formal handover.
Atego Seed School, Nebbi	Computers were connected and working in older rooms while construction continued.	Staff reported power surges and the planned facilities were not fully commissioned.	Stabilise the power supply, protect the installed computers and finish the remaining works.
Lungulu Seed Secondary School, Nwoya	The school funded minor repairs and kept breakdown information, but computers remained in storage pending power.	The stored equipment included defective desktop units, and the assets were not engraved.	Provide a suitable power connection, repair defective units, install the usable equipment and apply asset identification markings.
Todora and Paraa Health Centres III, Nwoya	Todora used the regional technical maintenance team, while some equipment originally intended for Todora remained at Paraa after redirection during construction.	Equipment location and final allocation required a district decision.	Confirm the service need at both facilities, formally allocate or transfer the equipment and update the named custodians.
Pamaka Health Centre III, Nebbi	Staff reported increased attendance and community confidence.	The solar system was not working, oxygen equipment could not be used because of power constraints, and staffing was under pressure.	Restore reliable power and demonstrate oxygen equipment operation; review staffing against patient demand.
Kalemungole Health Centre III, Moroto	Neonatal respiratory equipment remained in an unopened carton and treatment trolleys were still wrapped.	Delivered items had not been brought into routine use.	Check the equipment, confirm the room and staff requirements, and arrange installation and user orientation.
Rupa Seed School, Moroto	The school hired a generator for practical lessons and used its library and computer laboratory block as dormitories.	The intended learning spaces and a permanent power connection were unavailable for their planned use.	Agree a room-use plan and power solution that restores the library and computer laboratory functions.

Location	Expected position and field finding	Gap or service implication	Recommended action
Alwi Seed Secondary School, Pakwach	Expected: The computer laboratory and security equipment should support teaching and school operation. Found: The school reported power surges. Nine monitors and ten system units were not working, as were the server power-backup unit and twenty other power-backup units. Only one of thirteen security cameras was functional.	The loss of working computer stations and power protection reduced the usable laboratory capacity and left much of the camera system unavailable.	Pakwach District and the school should first assess the electrical supply and protection, then repair or replace failed equipment and test the whole laboratory and camera system before acceptance.
Wadelai Seed Secondary School, Pakwach	Expected: The school should be able to use its computer laboratory reliably and keep water storage structures safe. Found: Twenty desktop computers were recorded as working and in use, but the school reported a solar fault that interrupted use of electrical equipment. One water-tank stand was broken and presented a threat to students.	Usable equipment remained dependent on an unreliable power supply, and the damaged tank support required immediate attention.	The school and Pakwach District should restrict access around the damaged tank support pending an engineering assessment, repair the support, and restore and test the solar system.

Table 14: Northern assets and identification by category

Asset category	Assets	Eligible	Marked	Unmarked
Clinical equipment	6,016	6,016	444	5,572
Clinical furniture	5,795	5,795	1,164	4,631
Other assets	4,080	4,080	208	3,872
Maternity ward equipment	2,215	2,215	28	2,187
Building blocks	1,391	-	-	-
Health centre ICT equipment	205	205	137	68
School furniture	29,910	29,910	9,145	20,765
School computers and related equipment	2,383	2,383	874	1,509
Other ICT equipment	102	102	12	90
School support equipment	201	201	23	178
Vehicles and motorcycles	5	5	2	3

Table 14 shows the assets covered and the outstanding identification work by category. A dash means physical marking does not apply. Sub-region counts and condition classifications are in the appendices.

Field photographs from Northern



Figure 56: Building works and construction materials at Ndhew Seed Secondary School, Nebbi District (West Nile)



Figure 57: Unfinished classroom block at Sidok Seed Secondary School, Kaabong District (Karamoja)



Figure 58: Latrine block under construction at Sidok Seed Secondary School, Kaabong District (Karamoja)



Figure 59: Computer and library block interior with furniture and stored items at Iriiri Seed Secondary School, Napak District (Karamoja)



Figure 60: Stacked desks, chairs and stools at a seed secondary school, Napak District (Karamoja)



Figure 61: Damaged drip stand at a health centre, Moroto District (Karamoja)



Figure 62: Programme engraving on a weighing scale at Kalemungole HC III, Moroto District (Karamoja)



Figure 63: Programme engraving on a delivery bed at Kalemungole HC III, Moroto District (Karamoja)



Figure 64: Programme engraving on a table at Kamoru HC III, Kotido District (Karamoja)



Figure 65: Classroom furniture with school markings at Rupa Seed School, Moroto District (Karamoja)



Figure 66: Water tanks on a rendered plinth and steel tower at Alerek Seed Secondary School, Abim District (Karamoja)



Figure 67: Laboratory reagent containers at Alerek Seed Secondary School, Abim District (Karamoja)



Figure 68: Health centre building, Nwoya District (Acholi)



Figure 69: Section of the science laboratory exterior at Iriiri Seed Secondary School, Napak District (Karamoja)



Figure 70: Refrigerator bearing programme identification at Kalemungole HC III, Moroto District (Karamoja)



Figure 71: Solar panels at Kalemungole HC III, Moroto District (Karamoja)



Figure 72: Patient toilet block at Kalemungole HC III, Moroto District (Karamoja)



Figure 73: Oxygen concentrator at Kalemungole HC III, Moroto District (Karamoja)



Figure 74: Suction apparatus at Kalemungole HC III, Moroto District (Karamoja)



Figure 75: Wheelchair with programme marking at Kalemungole HC III, Moroto District (Karamoja)



Figure 76: Instrument trolley with delivery instruments at Kamoru HC III, Kotido District (Karamoja)



Figure 77: Microscope bearing local facility identification at Kamoru HC III, Kotido District (Karamoja)



Figure 78: Oxygen concentrator at Kamoru HC III, Kotido District (Karamoja)



Figure 79: Borehole apron and pipework at Katikekire Seed School, Moroto District (Karamoja)



Figure 80: Computer and library block at Lopei Seed Secondary School, Napak District (Karamoja)



Figure 81: Water storage tanks at Lopei Seed Secondary School, Napak District (Karamoja)



Figure 82: Buildings at a seed secondary school, Nwoya District (Acholi)



Figure 83: Water storage tanks at Rengen Seed School, Kotido District (Karamoja)



Figure 84: Rainwater tank beside a staff house at Rupa Seed School, Moroto District (Karamoja)



Figure 85: Laboratory supplies and an anatomical teaching model at Rupa Seed School, Moroto District (Karamoja)

4.3.4 Western region

The Western region master list covered 124 health centres and 71 schools. The asset inventory covered 44,164 items. Among 42,755 movable assets eligible for marking, 6,914 had an identification entry and 35,841 had none recorded. Buildings and land are identified through property and site records.

What was found

Repair needs affected buildings as well as equipment. At Nyamarunda Health Centre III in Kibaale, staff raised concerns about staff-quarter workmanship, electrical installation, drainage, water security and storage space. The facility recorded broken items, set them aside and referred them to the District Health Officer. A technical inspection should establish the repairs needed and their order of priority.

Avogera Health Centre III in Buliisa carried out some repairs locally and received support from Hoima Regional Referral Hospital. Items that could not be repaired remained in storage, and staff identified a need for technical skills, user orientation and more storage space. Kyankaramata Health Centre III in Kyenjojo funded minor repairs from Primary Health Care funds, but the cost of major repairs was a constraint.

There were practical maintenance arrangements to continue. Ngwedo Seed Secondary School in Buliisa engaged a caretaker monthly and used the Directorate of Industrial Training for furniture repairs. Bundimulangya Health Centre III in Bundibugyo referred maintenance needs to the District Health Officer, who sent a team; staff said the power house and solar installation supported continued operation.

Butungama Seed School in Ntoroko remained under construction. At Kigorobyia Seed Secondary School in Hoima, classrooms, the computer room and chemistry laboratory supported teaching, while staffing and study materials remained constraints. These findings call for completion of outstanding works and operating support alongside the assets already supplied.

Gaps and actions

Table 15: Western region: findings and recommended actions

Location	Expected position and field finding	Gap or service implication	Recommended action
Nyamarunda Health Centre III, Kibaale	The facility identified and set aside broken items and referred them to the District Health Officer.	Staff raised concerns about staff-quarter workmanship, electrical installation, drainage, water security and storage.	Carry out a joint engineering and health inspection, make unsafe installations safe and complete the agreed repairs.
Avogera Health Centre III, Buliisa	The facility carried out local repairs and received technical support from Hoima Regional Referral Hospital.	Items that could not be repaired remained stored; staff identified technical skills, user orientation and storage needs.	Assess the stored items for repair, give practical user training and agree a suitable storage arrangement.
Ngwedo Seed Secondary School, Buliisa	A caretaker attended monthly for repairs, and the Directorate of Industrial Training repaired furniture.	Practice to sustain.	Continue the repair schedule and record the items returned to use.
Bundimulangya Health Centre III, Bundibugyo	The District Health Officer arranged maintenance support, and staff said the power house and solar installation supported continued operation.	Practice to sustain.	Keep the technical referral arrangement active and include the power and solar systems in routine servicing.
Kyankaramata Health Centre III, Kyenjojo	Primary Health Care funds paid for minor repairs.	Major repair costs were a constraint.	Prepare costed technical referrals for major repairs and agree district funding and follow-up.
Kigorobya Seed Secondary School, Hoima	Equipped classrooms, the computer room and chemistry laboratory supported teaching; the school and ministry shared maintenance work.	Staffing and study materials constrained use of the improved facilities.	Review teaching staff and materials alongside the maintenance plan.
Butungama Seed School, Ntoroko	The school was still under construction at the time of the interview.	The construction works required completion.	Confirm the outstanding works with the district engineer and agree the completion and handover sequence.
Butiaba Health Centre III, Buliisa	The hydraulic delivery bed was not in use because staff needed operating guidance. Staff also reported difficulty obtaining test strips for the supplied glucometers.	Equipment use depended on practical training and access to compatible consumables.	Demonstrate safe operation of the delivery bed with its users and arrange a reliable supply of compatible glucometer strips.
Kihungya Seed Secondary School, Buliisa	Expected: The school investment should provide usable science and computer laboratories, staff accommodation, water and secure premises. Found: The science block, computer laboratory and library were still under construction, and staff quarters were incomplete. The school reported no electricity for computer sessions, no water for sanitation and no perimeter fence. Its administration block was already in use.	The school was partly in use while essential teaching spaces, utilities and security remained unfinished.	Buliisa District and the Ministry of Education and Sports should use one completion plan for the laboratories, staff housing, electricity, water and security, with separate testing and handover of each finished element.

Location	Expected position and field finding	Gap or service implication	Recommended action
Kihungya Health Centre III, Buliisa	Expected: Expanded buildings and equipment should support care at the health centre, with responsibility clear for any items kept elsewhere. Found: Staff reported more room for patients, easier working arrangements through staff accommodation, and electricity from the new solar power house. Buildings were in use. A gas stove, electric suction apparatus, laboratory stool and electric centrifuge were recorded at the subcounty rather than the health centre.	The building and power investment was supporting care, but the intended use and custody of equipment held away from the facility needed confirmation.	Buliisa District and facility management should preserve the working building and solar arrangements, confirm who holds the off-site equipment, and agree whether it should be deployed to the health centre or remain at its present location.

Table 16: Western assets and identification by category

Asset category	Assets	Eligible	Marked	Unmarked
Clinical equipment	6,365	6,365	729	5,636
Clinical furniture	4,524	4,524	805	3,719
Other assets	7,913	7,902	271	7,631
Health centre ICT equipment	79	79	7	72
Maternity ward equipment	2,098	2,098	900	1,198
Building blocks	1,398	-	-	-
School furniture	19,518	19,518	3,890	15,628
School support equipment	216	216	26	190
Other ICT equipment	58	58	3	55
School computers and related equipment	1,994	1,994	283	1,711
Vehicles and motorcycles	1	1	0	1

Table 16 shows the assets covered and the outstanding identification work by category. A dash means physical marking does not apply. Sub-region counts and condition classifications are in the appendices.

Field photographs from Western



Figure 86: Classroom block with earthworks in the foreground at Kihungya Seed Secondary School, Buliisa District (Bunyoro)



Figure 87: Biology laboratory under construction at a seed secondary school, Buliisa District (Bunyoro)



Figure 88: Unfinished laboratory interior at Kihungya Seed Secondary School, Buliisa District (Bunyoro)



Figure 89: Library interior under construction at Kihungya Seed Secondary School, Buliisa District (Bunyoro)



Figure 90: Laboratory benches with cupboard doors detached at King Solomon Seed Secondary School, Kagadi District (Bunyoro)

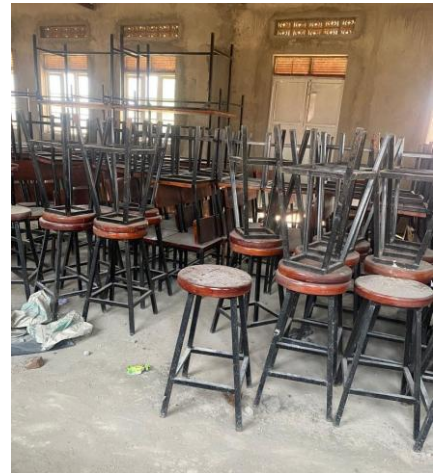


Figure 91: Laboratory stools and other school furniture in storage, Ntoroko District (Tooro)



Figure 92: Clinical equipment packed among cartons at a health centre, Hoima City (Bunyoro)



Figure 93: Stacked classroom furniture at King Solomon Seed Secondary School, Kagadi District (Bunyoro)



Figure 94: Boxed projector and other equipment at King Solomon Seed Secondary School, Kagadi District (Bunyoro)



Figure 95: Hospital beds and screens stacked in storage at a health centre, Kagadi District (Bunyoro)



Figure 96: Flood-affected older health facility at Butiaba, Buliisa District (Bunyoro)



Figure 97: School engraving on wooden furniture at King Solomon Seed Secondary School, Kagadi District (Bunyoro)



Figure 98: Programme engraving on a table at Kyabasara HC III, Kagadi District (Bunyoro)



Figure 99: Blood pressure apparatus on a mobile stand at Butiaba HC III, Buliisa District (Bunyoro)



Figure 100: Office chairs at Butiaba HC III, Buliisa District (Bunyoro)



Figure 101: Medical-waste bins and ward beds at Butiaba HC III, Buliisa District (Bunyoro)



Figure 102: Laboratory centrifuge at Butiaba HC III, Buliisa District (Bunyoro)



Figure 103: Delivery bed and clinical furniture at a health centre, Kabarole District (Tooro)



Figure 104: Water tank on a masonry support at King Solomon Seed Secondary School, Kagadi District (Bunyoro)



Figure 105: Elevated water tank on a steel tower at King Solomon Seed Secondary School, Kagadi District (Bunyoro)



Figure 106: Classroom desks at King Solomon Seed Secondary School, Kagadi District (Bunyoro)



Figure 107: Gas cylinders and pipework at King Solomon Seed Secondary School, Kagadi District (Bunyoro)



Figure 108: Latrine block and paved access at Kyabasara HC III, Kagadi District (Bunyoro)



Figure 109: Kangaroo care chair at Kyabasara HC III, Kagadi District (Bunyoro)



Figure 110: Power house at Kyabasara HC III, Kagadi District (Bunyoro)



Figure 111: Classroom desks at a seed secondary school, Ntoroko District (Tooro)

4.4 Condition and use of assets

4.4.1 Equipment in use and items awaiting action

The visits showed why availability, condition and use need to be considered together. At Lungulu Seed Secondary School, a power connection was needed before stored computers could be installed. At

Kalemungole Health Centre III, equipment remained boxed or wrapped. At Sikuda Seed Secondary School, a damaged stool was still being used.

Among assets recorded as out of use, 2,569 had damage, fault or repair remarks, while 483 were stored and described as good or new. These groups require different action: damaged items need technical assessment, while usable stored items need the conditions for safe installation and use.

4.4.2 Complete the setting in which equipment will work

At Got Apwoyo, Ndhew and Mamba seed schools, unfinished buildings delayed the use or installation of equipment. At Rupa Seed School, the library and computer laboratory block had been put to another use. Completion plans should bring buildings, electricity, furniture, equipment and staffing together so that handover leads to an operating service.

At Atego Seed School, equipment was already working in older rooms while construction continued. Completion should protect this use while the planned facilities are finished and the power supply is stabilised.

4.5 Asset management practices, gaps and actions

4.5.1 Identification and custody

Across the programme, 49,836 of 218,715 movable assets eligible for a physical mark had an identification entry (22.8%). Of these, 20,973 carried UgIFT marking and 28,863 carried another marking. Buildings and land are tracked by location, ownership and handover records instead. Lungulu Seed Secondary School provided a specific example of equipment requiring identification.

Marking should identify the asset and the institution responsible for it. Where assets have moved, custody needs to move with them: equipment from three Busia health centres had gone to Masafu Hospital, while equipment intended for Todora in Nwoya had gone to Paraa during construction. The district should confirm the continuing allocation and retain signed handover or transfer documentation.

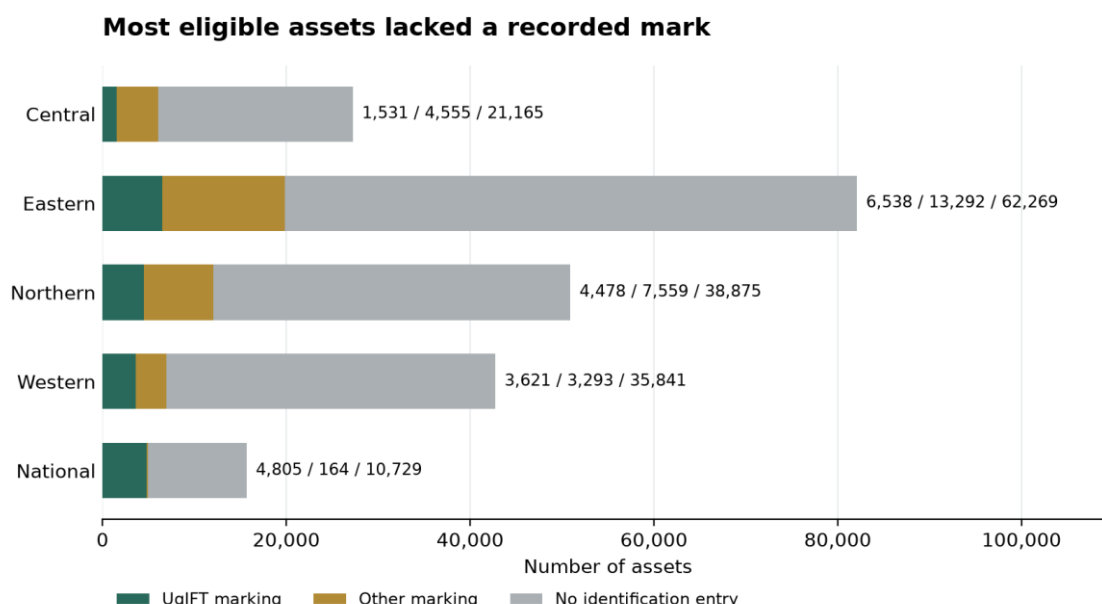


Figure 112: Most eligible assets lacked a recorded mark



Figure 113: UgIFT identification on a desk at a seed school, Tororo District (Bukedi)

4.5.2 Maintenance and repairs

Facilities used several practical arrangements. Busaale Health Centre III reviewed condition quarterly and used Primary Health Care funds for repairs. Kagumba Health Centre III kept a condition book, and Kagumba Seed Secondary School had repaired broken furniture during the second term. Ngwedo Seed Secondary School used a monthly caretaker visit and specialist furniture repair support.

Major medical equipment repairs depended on technical support beyond the facility. Todora worked through the District Health Officer and Gulu Regional Referral Hospital; Avogera received support from Hoima Regional Referral Hospital; Bundimulangya obtained a team through the District Health Officer. At Kyankaramata, the cost of major repairs constrained what the facility could do.

Each facility should keep a short list of items requiring action, the responsible person and the agreed completion date. District health and education offices should review unresolved repairs and arrange technical assistance. Completion should mean that the item has been checked and returned to safe use, or formally assigned another outcome.

4.5.3 Storage, installation and user skills

Stored equipment needs a plan for use. Lungulu needed power, Got Apwoyo needed completed buildings, and Avogera needed repair support for items it could not restore locally. Kalemungole had unopened and wrapped equipment requiring a check of readiness for installation and use.

Training should accompany installation. Bubago Health Centre identified limited capacity to operate and maintain an oxygen concentrator, while Avogera asked for user orientation and technical skills. Equipment should be handed over with a practical demonstration to the staff who will use it and a clear route for technical support.



Figure 114: Boxed computers and related equipment in a seed school store, Nwoya District (Acholi)

4.5.4 Priorities for follow-up

The first priority is to make unsafe items and installations safe and restore equipment needed for care and teaching. The next is to complete works, provide utilities and install assets that can then be used. Marking, custody checks and routine servicing should form part of the same follow-up, with responsibility assigned to the institution and its supervising office.

Future delivery plans should confirm the room, power, water, storage and staff requirements before equipment arrives. Facility managers should take part in that planning, as recommended at Kyankaramata and Avogera. The action schedule sets out proposed owners, timing and evidence of completion.

Priority action plan

The following timeframes are proposed from acceptance of this report. Accounting Officers should assign responsible staff and track each action to completion.

Table 17: Priority actions to protect assets and restore service

Priority	Action	Responsible institution	Proposed timing	Evidence of completion
1	Withdraw damaged furniture that presents a safety concern, inspect the electrical concerns at Nyamarunda, and assess the failed solar and oxygen equipment arrangements at Pamaka.	Facility managers, district health and education officers, district engineers and regional medical equipment technical teams	inspect within 30 days of report approval; complete minor corrective work within 60 days.	Unsafe items withdrawn; signed technical assessment; repair record and demonstration of safe operation.
2	Agree completion plans for Got Apwoyo, Ndhew, Mamba and Butungama seed schools. Coordinate the remaining works, utilities, furniture and equipment installation; protect ongoing equipment use at Atego.	District Accounting Officers, district engineers, district education officers, contractors and Ministry of Education and Sports	agree site-specific completion plans within 30 days; track progress monthly against the approved dates.	Outstanding-works schedule; approved completion dates; inspection and handover documents; classrooms or laboratories opened for their intended use.
3	Provide the power required at Lungulu, assess and install the boxed equipment at Kalemungole, and assess the repair needs of stored items at Avogera. Keep damaged and usable stored items on separate action lists.	District health and education officers, facility managers, electrical contractors and regional technical teams	confirm readiness and actions within 30 days; complete installation within 90 days where rooms and utilities are ready.	Equipment location check; power and installation sign-off; named custodian; practical demonstration and date first used.

Priority	Action	Responsible institution	Proposed timing	Evidence of completion
4	Repair the roof, doors and solar system at Busaale, arrange the major repair support needed at Kyankaramata and assess damaged laptops at the Office of the Prime Minister.	Facility managers, district health officers, district engineers and the responsible national institution asset managers	agree priority work within 30 days and complete funded repairs within 90 days.	Approved repair list; work orders; repairs checked and assets returned to use or assigned a formal disposal decision.
5	Provide practical operation and basic maintenance training for oxygen equipment users at Bubago and the staff requiring equipment orientation at Avogera.	District health officers, facility in-charges, suppliers and regional medical equipment technical teams	complete initial training within 60 days and review use after a further 30 days.	Training attendance by role; practical demonstration of equipment use; named technical support contact.
6	Mark eligible unengraved assets, starting with the identified Lungulu holdings, and confirm the final allocation of transferred equipment at Todora, Paraa and Masafu.	Institution asset managers, facility managers and district finance, health and education offices	confirm allocation within 30 days and complete priority marking and custody checks within 90 days.	Readable identification; item-to-custodian match; signed transfer or receipt and agreed final location.
7	Retain the functioning local and regional repair arrangements and prepare annual maintenance plans that separate minor repairs from specialist work. Review unresolved faults each quarter.	Facility managers, school governing bodies, district health and education officers and national institution Accounting Officers	prepare plans within 90 days, include costs in the next budget cycle and review quarterly.	Funded maintenance plan; fault list with responsible roles and due dates; service history and closed repair actions.
8	Review supporting clinical space and staffing at Kagumba and Pamaka, teaching staff and materials at Kigorobya, and attendance barriers at Musiitwa. Include operating needs in future asset planning.	District health and education officers, facility managers and the relevant sector ministries	complete service-needs reviews within 90 days and include agreed measures in the next planning and budget cycle.	Agreed staffing and space priorities; service or teaching plan; funded actions and periodic review of use.

4.6 UgIFT support to service delivery

4.6.1 Benefits described by facilities

Staff at Lukale Health Centre III in Buvuma said women could give birth locally instead of crossing water and had greater privacy. Kagumba Health Centre III in Kamuli reported greater use of maternity and antenatal services. At Pamaka Health Centre III in Nebbi, staff described increased attendance and community confidence.

Schools also described practical gains. Musiitwa Seed Secondary School used the irrigation system for teaching and food production and provided secondary education closer to surrounding communities. Kigorobya Seed Secondary School used its classrooms, computer room and chemistry laboratory to support teaching.

Other school visits showed the value of bringing teaching space closer to communities. Gyagenda Memorial Seed Secondary School in Bujumba reported better access to secondary education about 35 kilometres from Kalangala town. Sisiyi recorded its buildings, furniture and ICT in use. Sibanga reported shorter journeys for learners, although full handover was still pending.

Health centres gave equally practical examples. Kibiri Health Centre III had begun operations by 31 August 2026, while staff were still arranging some equipment. At Kihuukya, the renovated maternity block and walkways were recorded in use and a binocular microscope was seen functioning. Iruhura recorded adult weighing scales and waiting benches in use. Kamuli reported improved service delivery, alongside continuing staffing and accommodation needs.

Facilities and equipment supporting services



Figure 115: Adult weighing scale with a height meter and waiting benches at Iruhura HC III, Kabarole District (Tooro)



Figure 116: Maternity block entrance and access ramp at Kamuli HC III, Tororo District (Bukedi)



Figure 117: Health centre building at Kibiri HC III, Makindye-Ssabagabo Municipal Council (Buganda)



Figure 118: Health centre buildings and covered walkway at Kihuukya HC III, Hoima City (Bunyoro)



Figure 119: Binocular microscope at Kihuukya HC III, Hoima City (Bunyoro)



Figure 120: Classroom furnished with desks and a whiteboard at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)



Figure 121: Books displayed on library shelves at Sibanga Seed School, Manafwa District (Bugisu)



Figure 122: ICT laboratory block and entrance ramp at Sisiyi Seed Secondary School, Bulambuli District (Bugisu)

4.6.2 Constraints to the intended service

Equipment could not deliver its intended benefit where buildings, utilities or user skills were not ready. Power restricted oxygen equipment at Pamaka and computer installation at Lungulu. At Rupa, teaching spaces served as dormitories and practical lessons depended on a hired generator.

Demand also brought pressure on staff and space. Kagumba identified needs for staff housing and supporting clinical facilities. Pamaka reported staffing pressure, and Kigorobyia identified teaching staff and study-material constraints. Musiitwa's attendance concerns required attention alongside investment in buildings and equipment.

4.6.3 Actions to sustain the benefits

Districts and sector ministries should direct the first round of follow-up to actions that restore or expand a service using assets already supplied. These include reliable electricity, completion of classrooms and laboratories, repair of maternity buildings, practical equipment training and return of damaged furniture to safe use.

Facility managers should report progress in terms of use: rooms opened, equipment installed and demonstrated, repairs completed and staff able to operate the equipment. Future investment should provide for staffing, operating funds and maintenance alongside buildings and equipment.

4.7 Summary of findings

The field visits found facilities and equipment already supporting care, teaching and programme administration. They also found places where the intended service had not yet followed the investment: unfinished buildings, equipment kept in stores, power and water problems, and assets awaiting repair or installation. The photographs and facility examples show both the progress made and the work still needed at each site.

The next stage should be practical and site-specific. Districts and responsible institutions should finish and inspect outstanding works, make rooms and utilities ready, install and test equipment, and resolve defects before final handover. They should confirm where each movable asset is held and who looks after it. Buildings and land should be identified through site and property records; suitable equipment and furniture should carry clear identification linked to the inventory.

The reconciled facility list should guide decisions where planned locations differed from what teams found. Managers should assign owners, track completion and check that work restores usable services. Regular maintenance and an up-to-date inventory will help protect the benefits already reaching communities.

5 Recommendations

The next phase should turn the findings into actions that protect assets and improve care, teaching and programme administration. Accounting Officers should use the priority action plan in Table 17 to assign responsibility, agree resources and check completion.

5.1 Restore safe operation

Facility managers, district health and education officers, engineers and technical teams should prioritise unsafe furniture, electrical concerns and failed equipment needed for essential services. Withdraw unsafe items, obtain technical assessments and verify safe operation after repair. Keep damaged assets separate from usable assets awaiting installation so that each receives the appropriate action.

5.2 Complete works and bring stored assets into use

District Accounting Officers, engineers, health and education officers and contractors should coordinate outstanding buildings, utilities, furniture and equipment through site-specific completion plans. Installation should follow confirmation that rooms, power, water and security are ready. Protect services already operating during construction, and complete testing and signed handover before closing each action.

5.3 Equip staff to operate and maintain assets

District health officers, facility managers, suppliers and regional technical teams should provide practical training for staff who use specialist equipment, including oxygen equipment users at Bubago and staff requiring orientation at Avogera. Handover should include a demonstration, basic maintenance guidance and a named route for technical support.

5.4 Strengthen identification and custody

Institution asset managers and district finance, health and education offices should mark eligible movable assets and confirm their locations and custodians. Resolve the continuing allocation of equipment at Todora, Paraa and Masafu through signed transfer or receipt documentation. Maintain site, ownership and handover records for buildings and land.

5.5 Fund and monitor maintenance

Facility managers and supervising institutions should retain effective local repair arrangements and prepare annual maintenance plans that distinguish minor repairs from specialist work. Include costs in the next budget cycle, review unresolved faults quarterly and record whether each asset has returned to safe use or received another formal decision.

5.6 Plan for continued service delivery

Districts and sector ministries should review staffing, operating funds, clinical and teaching space, consumables and utilities alongside asset needs. Future deliveries should follow confirmation of facility readiness. Managers should report progress through rooms opened, assets installed, repairs completed and staff able to operate equipment, using Table 17's proposed timeframes and evidence of completion.

6 Conclusion

The report brings together information on 225,133 assets across health care, education and programme administration. All 629 facilities on the master list were accounted for through verification or reconciliation. Field observations and facility accounts show benefits including care closer to communities, improved teaching spaces and equipment supporting daily services.

The findings also show why delivery alone does not secure the intended benefit. Unfinished buildings, unreliable utilities, stored equipment, repair needs and limited user skills prevented some assets from being used as intended. These findings call for coordinated action at facility, district and national levels, with clear responsibility for completion, installation, custody and maintenance.

The priority is to protect services already operating and bring the remaining assets into safe, intended use. The recommendations and action plan provide a basis for that follow-up. Progress should be judged by functioning facilities, equipment in use, completed repairs and accountable custody. Sustained maintenance and provision for operating needs will help preserve the programme benefits for the communities it serves.

Appendices

Appendix A Full summary count schedule

The summary schedule brings the asset counts, facility coverage and reconciliation outcomes together. Each asset is counted once. The national column contains national institutional holdings, and the whole programme column includes all assets.

Table 18: Whole programme and regional summary counts

Measure	Central	Eastern	Northern	Western	National	Programme
Assets	28,192	84,681	52,303	44,164	15,793	225,133
Movable assets eligible for marking	27,251	82,099	50,912	42,755	15,698	218,715
Identification entry recorded	6,086	19,830	12,037	6,914	4,969	49,836
UgIFT marking recorded	1,531	6,538	4,478	3,621	4,805	20,973
Other marking recorded	4,555	13,292	7,559	3,293	164	28,863
No identification entry recorded	21,165	62,269	38,875	35,841	10,729	168,879
Use flag YES	27,028	78,939	49,052	40,821	15,773	211,613
Use flag NO with damage wording	89	1,536	524	417	3	2,569
Not in use, stored and explicitly good or new	2	300	66	115	0	483
Functional classification	27,028	78,939	49,052	40,821	15,773	211,613
Faulty classification	1,164	5,742	3,251	3,343	20	13,520
Facilities sharing or holding assets elsewhere	2	11	12	17	0	42
Ground-return identities outside master names	3	2	10	9	0	24
Does not exist or was not constructed under the programme	1	3	5	1	0	10
Replaced by another facility	0	0	3	1	0	4
Operates under another name	9	8	0	13	0	30
Not a UgIFT beneficiary	0	1	1	1	0	3
Assets relocated to another facility or held at district	0	0	3	0	0	3
Exists with no UgIFT assets	0	0	1	4	0	5
Health centre master-list entries	62	93	92	124	0	371
School master-list entries	37	76	74	71	0	258
Health centre assets	10,153	21,250	16,991	15,565	14	63,973
School assets	18,037	63,431	35,310	28,599	0	145,377
MDA assets	0	0	0	0	7,520	7,520
Hospital assets	0	0	0	0	8,101	8,101
Blood bank assets	0	0	0	0	158	158
Local government office assets	2	0	2	0	0	4

Table 18 gives the full summary schedule. Report-category and register-class totals continue in Appendix B. Reconciled operating names may also hold verification materials, so reconciliation reasons are not additive to master-list coverage.

Appendix B Asset totals by report category and register class

Table 19: Assets by report category and region

Report category	Central	Eastern	Northern	Western	National	Programme
Building blocks	940	2,577	1,391	1,398	95	6,401
Clinical equipment	3,926	8,249	6,016	6,365	0	24,556
Clinical furniture	2,965	6,877	5,795	4,524	0	20,161
Health centre ICT equipment	32	107	205	79	8	431
Maternity ward equipment	1,372	1,753	2,215	2,098	0	7,438
Other ICT equipment	80	347	102	58	5,719	6,306
Other assets	3,522	13,526	4,080	7,913	9,656	38,697
Other furniture	0	0	0	0	242	242
School computers and related equipment	1,365	4,462	2,383	1,994	0	10,204
School furniture	13,911	46,351	29,910	19,518	0	109,690
School support equipment	76	423	201	216	0	916
Vehicles and motorcycles	3	9	5	1	73	91

Table 19 reconciles the report categories to the programme asset count.

Table 20: Assets by register class and region

Register class	Central	Eastern	Northern	Western	National	Programme
Other recorded items	3,097	9,275	3,358	5,532	1,830	23,092
Computer Software	0	0	19	2	30	51
Cycles	1	4	2	0	47	54
Electrical Machinery	141	1,560	217	260	224	2,402
Furniture And Fittings	16,097	51,276	33,669	21,982	242	123,266
Heavy ICT Hardware	7	121	101	38	14	281
ICT Network Lines	0	12	16	3	0	31
Land	1	5	0	11	0	17
Light ICT Hardware	1,462	4,889	2,634	2,147	5,707	16,839
Light Vehicles	2	5	3	1	26	37
Med Lab Research Appliances	5,978	13,789	9,537	10,270	7,493	47,067
Musical Instruments	1	1	0	0	0	2
Non Residential Buildings	927	2,006	2,086	2,971	0	7,990
Office Equipment	0	0	0	0	7	7
Other ICT Equipment	82	329	156	160	6	733
Other Structures	147	562	192	213	95	1,209
Plant Machinery	45	202	24	72	72	415
Precision Optical Instruments	26	246	18	172	0	462
Residential Buildings	171	386	255	309	0	1,121
Road Furniture	2	1	0	0	0	3

Register class	Central	Eastern	Northern	Western	National	Programme
Roads And Bridges	2	4	2	3	0	11
Sports Equipment	3	3	10	14	0	30
Water Supply Systems	0	5	4	4	0	13

Table 20 preserves the register class distribution alongside the report categories.

Appendix C Condition tables behind the charts

The consolidated asset inventory classifies each asset as Functional or Faulty. Functional includes working, available, verified and new items together with the register's default classification; Faulty includes defective items and items recorded as stored or otherwise out of use. The percentages in this appendix describe these register classifications. The separate use analysis retains the stated reasons for damage and storage.

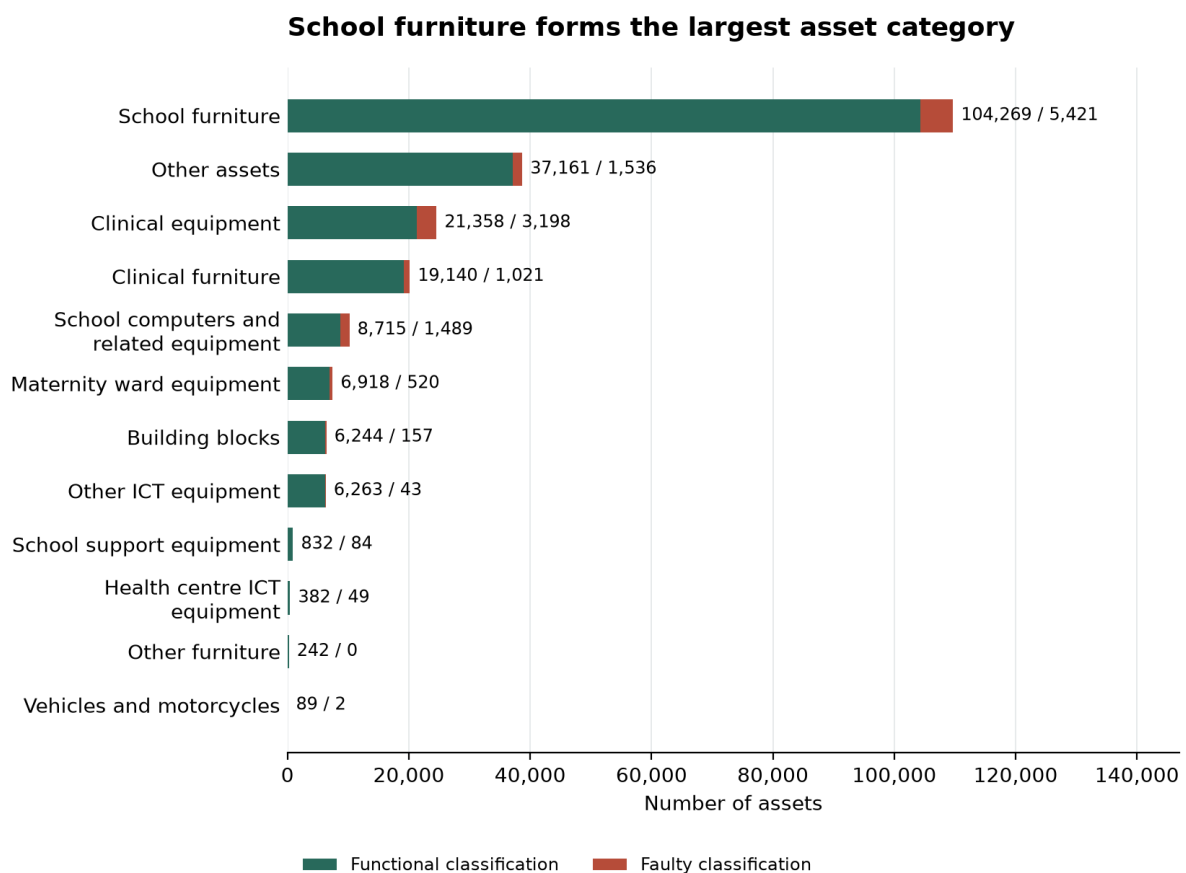


Figure 123: School furniture forms the largest asset category

Table 21: Condition classifications by report category

Category	Functional	Faulty	Total
Clinical equipment	21,358	3,198	24,556
Clinical furniture	19,140	1,021	20,161
Other assets	37,161	1,536	38,697
Health centre ICT equipment	382	49	431
Maternity ward equipment	6,918	520	7,438
Building blocks	6,244	157	6,401
School furniture	104,269	5,421	109,690

Category	Functional	Faulty	Total
School support equipment	832	84	916
Other ICT equipment	6,263	43	6,306
School computers and related equipment	8,715	1,489	10,204
Vehicles and motorcycles	89	2	91
Other furniture	242	0	242

Table 21 supplies the data for the corresponding condition chart in this appendix.

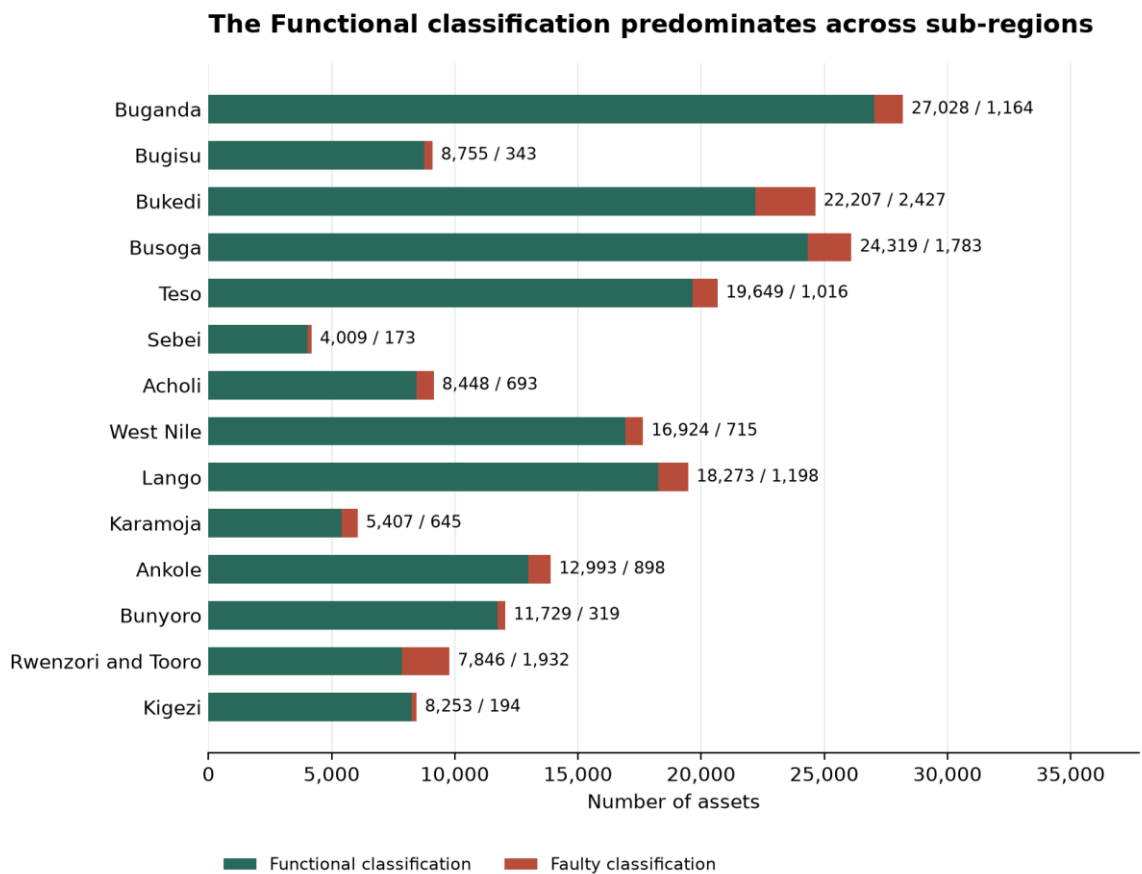


Figure 124: The Functional classification predominates across sub-regions

Table 22: Condition classifications by sub-region

Subregion	Functional	Faulty	Total
Buganda	27,028	1,164	28,192
Rwenzori and Tooro	7,846	1,932	9,778
Bunyoro	11,729	319	12,048
Busoga	24,319	1,783	26,102
West Nile	16,924	715	17,639
Acholi	8,448	693	9,141
Ankole	12,993	898	13,891
Lango	18,273	1,198	19,471
Teso	19,649	1,016	20,665

Subregion	Functional	Faulty	Total
Bukedi	22,207	2,427	24,634
Karamoja	5,407	645	6,052
Bugisu	8,755	343	9,098
Sebei	4,009	173	4,182
Kigezi	8,253	194	8,447

Table 22 supplies the data for the corresponding condition chart in this appendix.

Appendix D Recorded value and net book value schedules

The programme assets have a total recorded value of UGX 987,149,478,424, accumulated depreciation of UGX 177,442,659,553 and net book value of UGX 809,721,344,882 at 30 September 2026. These amounts support the financial handover and are presented separately from the field findings.

Recognition followed sections 3.2.1 and 3.3.3 of the Government of Uganda Asset Accounting Policies and Guidelines 2023. The asset register carries the unit values used in these schedules; amounts below UGX 10,000 are carried at zero.

The useful lives and commencement dates follow the register and the asset-class framework in Annex 1. Depreciation is straight line with nil residual value under sections 5.5 and 5.7; capital work in progress is not depreciated. Net book value is calculated for each asset as cost less accumulated depreciation, with a minimum of zero, before amounts are totalled.

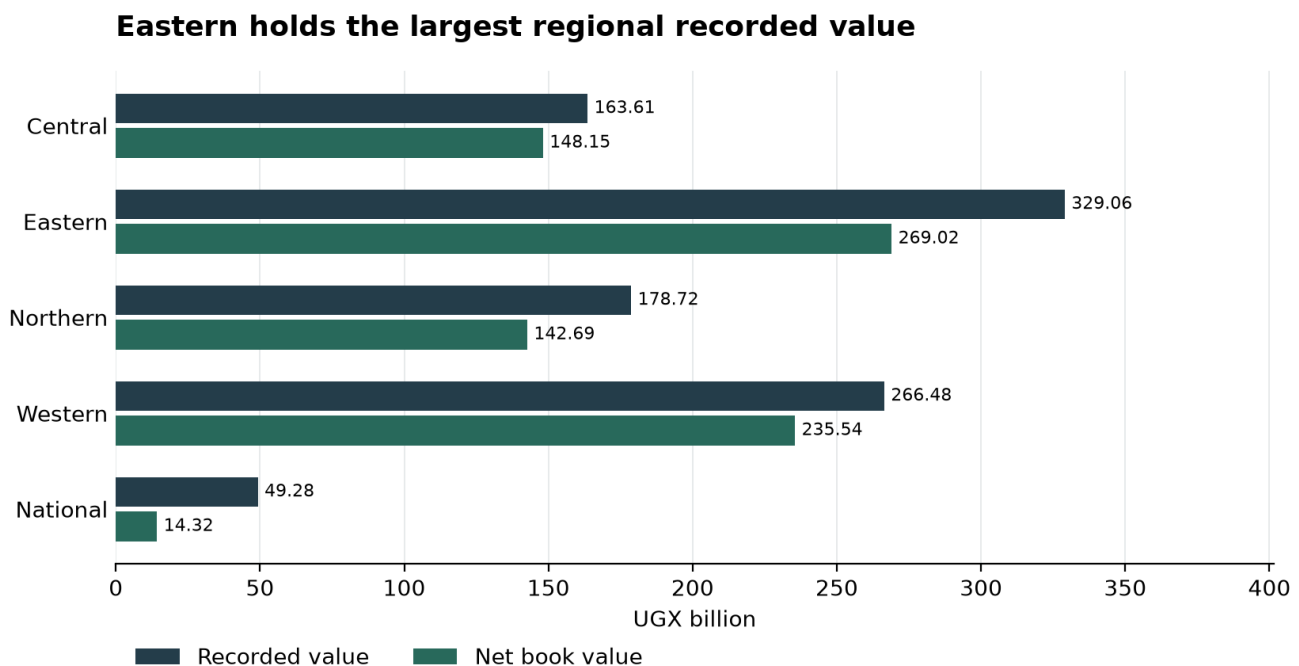


Figure 125: Eastern holds the largest regional recorded value

MoFPED and MoES hold the largest ministry recorded values

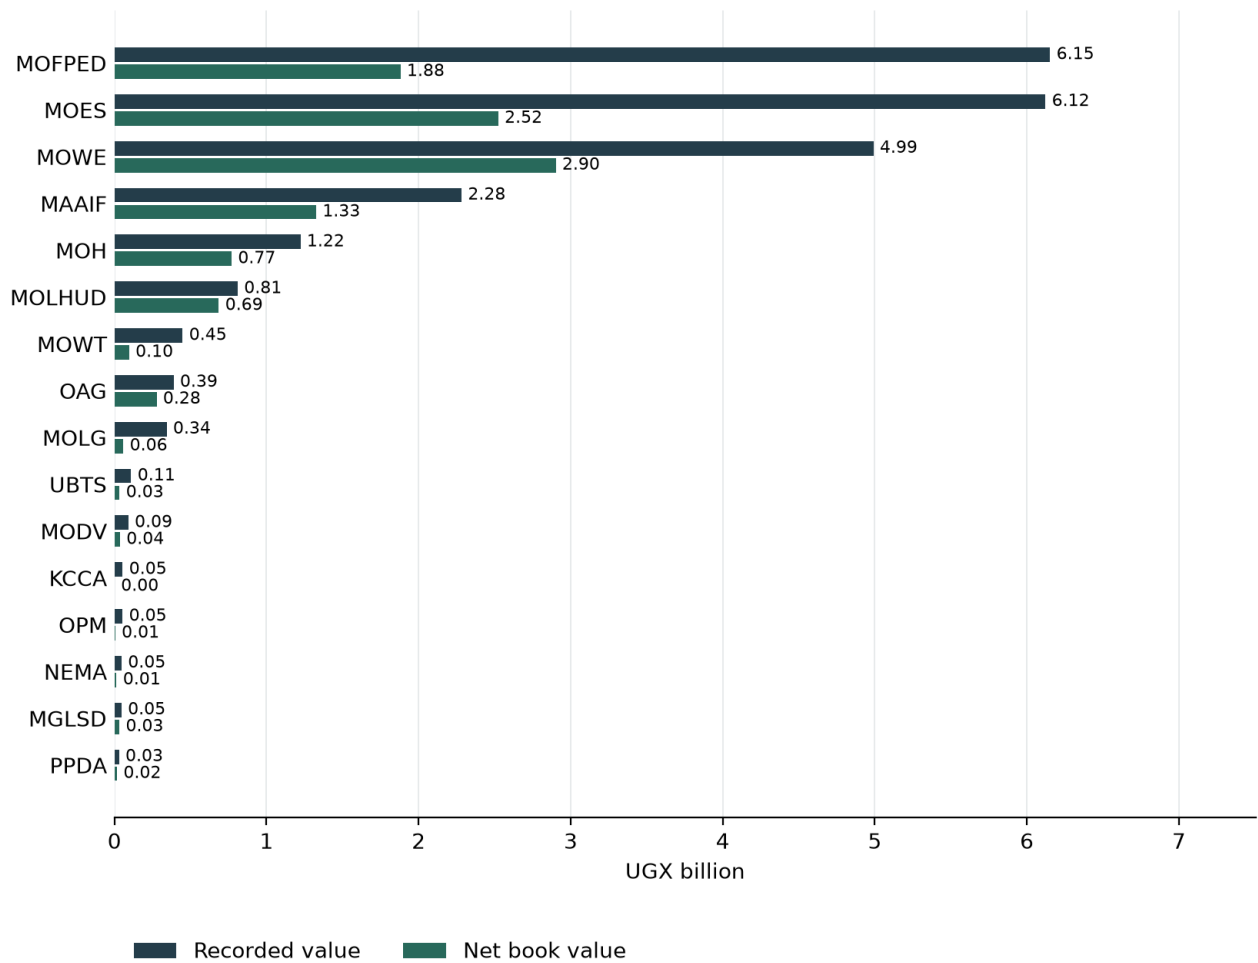


Figure 126: MoFPED and MoES hold the largest ministry recorded values

Table 23: Recorded value and net book value by region

Region	Recorded value UGX	Depreciation UGX	Net book value UGX
Central	163,614,333,983	15,463,880,138	148,150,453,845
Eastern	329,055,793,224	60,032,652,248	269,023,140,987
Northern	178,717,389,379	36,039,298,157	142,692,617,222
Western	266,481,129,152	30,945,966,264	235,535,162,888
National	49,280,832,686	34,960,862,746	14,319,969,940
Programme	987,149,478,424	177,442,659,553	809,721,344,882

Table 23 gives the data behind the regional value chart. The net book value floor applies to each individual asset before aggregation.

Table 24: National ministry and agency value schedule

Vote or group	Qty	Recorded value UGX	Depreciation UGX	Net book value UGX
MOFPED	458	6,152,854,000	4,272,041,257	1,880,812,743
MOES	1,371	6,122,415,903	3,598,574,311	2,523,841,592
MOWE	2,939	4,990,929,297	2,088,701,634	2,902,227,663
MAAIF	1,975	2,282,355,629	955,929,429	1,326,426,200

Vote or group	Qty	Recorded value UGX	Depreciation UGX	Net book value UGX
MOH	264	1,222,996,178	452,722,710	770,273,468
MOLHUD	26	810,399,998	124,320,000	686,079,998
MOWT	88	448,639,007	352,204,285	96,434,722
OAG	20	388,773,680	111,591,545	277,182,135
MOLG	13	343,320,450	284,804,160	58,516,290
UBTS	273	109,987,849	76,107,195	33,880,654
MODV	183	91,162,979	54,612,464	36,550,515
KCCA	51	54,024,515	53,024,515	1,000,000
OPM	10	53,535,300	48,181,770	5,353,530
NEMA	6	46,824,409	32,841,273	13,983,136
MGLSD	10	46,180,000	13,660,000	32,520,000
PPDA	5	30,153,500	13,066,516	17,086,984
Hospital holdings	8,101	26,086,279,992	22,428,479,682	3,657,800,310

Table 24 supplies the ministry and agency chart data and retains the national health groups in the account. Vote codes are the register identifiers.

Appendix E Use and asset identification schedules

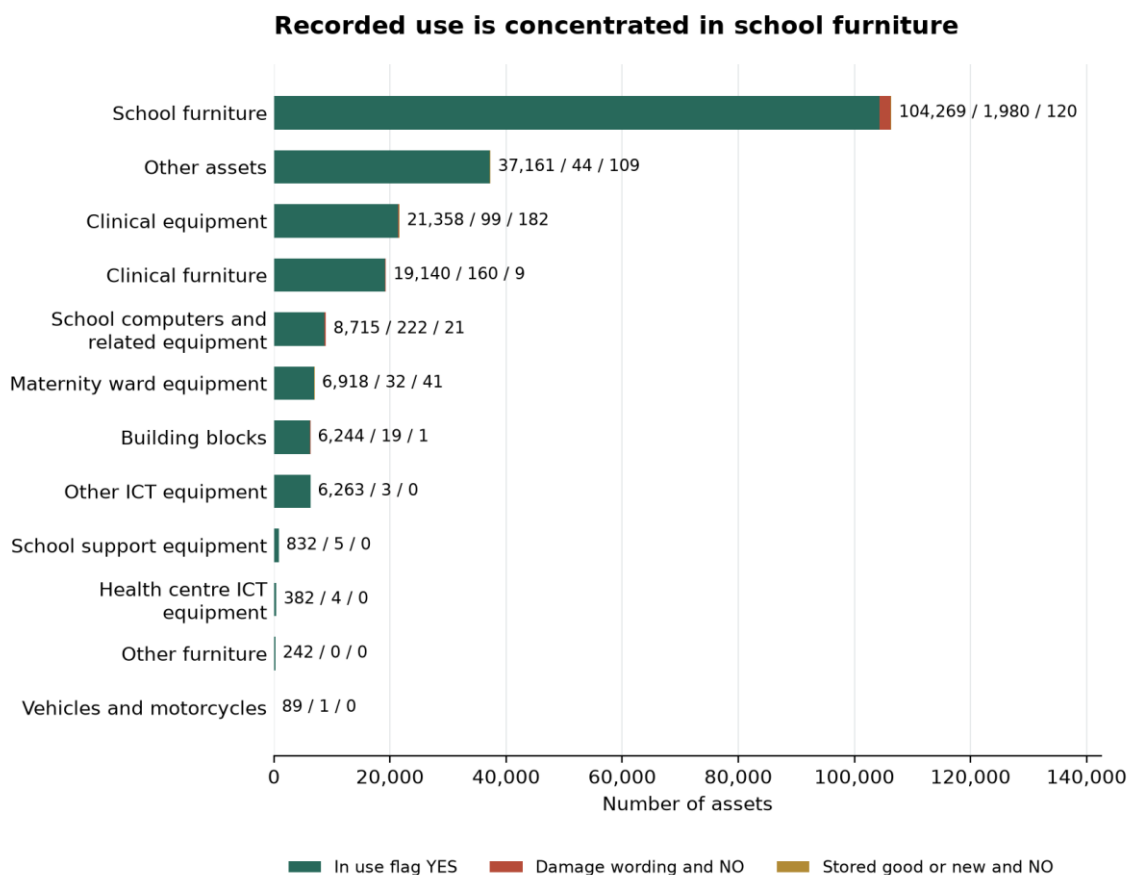


Figure 127: Recorded use is concentrated in school furniture

Table 25: Use flags and recorded reasons by report category

Category	Use flag YES	NO with damage wording	NO with stored or new wording
Clinical equipment	21,358	99	182
Clinical furniture	19,140	160	9
Other assets	37,161	44	109
Health centre ICT equipment	382	4	0
Maternity ward equipment	6,918	32	41
Building blocks	6,244	19	1
School furniture	104,269	1,980	120
School support equipment	832	5	0
Other ICT equipment	6,263	3	0
School computers and related equipment	8,715	222	21
Vehicles and motorcycles	89	1	0
Other furniture	242	0	0

Table 25 contains the data behind the use chart. The reason groups identify the wording recorded for the asset and do not form a separate condition assessment.

Table 26: Identification entries by region

Region	UgIFT marking	Other marking	No entry	Eligible total
Central	1,531	4,555	21,165	27,251
Eastern	6,538	13,292	62,269	82,099
Northern	4,478	7,559	38,875	50,912
Western	3,621	3,293	35,841	42,755
National	4,805	164	10,729	15,698

Table 26 contains the data behind the identification chart. Buildings, structures and land are tracked through property and site records, so physical engraving does not apply to them.

Appendix F Master-list reconciliation and ground-return identities

Each master-list entry below retains its original identity, local government, final supported outcome. Names used by receiving facilities and operating institutions remain within the same reconciliation account.

Table 27: Master-list entries accounted for through reconciliation

Master-list entry	Local government	Reconciled outcome
H010 Butoloogo HC II	Kasanda Central	The master-list entry Butoloogo HC II does not exist under the programme.
S065 Maddu Seed School	Gomba Central	The submitted Kyayi Seed School return was reconciled to the master-list Maddu Seed School.
S066 Bufumira Seed School	Kalangala Central	The master-list entry Bufumira Seed School was reconciled to Nekemiya Memorial Seed Secondary School.
H015 Kyakatebe HC II	Kasanda Central	The master-list entry Kyakatebe HC II was reconciled to Namabaale Health Centre III.

Master-list entry	Local government	Reconciled outcome
H027 Kagganda HC II	Lwengo Central	The master-list entry Kagganda HC II was reconciled to Mbirizi Seed Secondary School.
S081 Mpumudde seed school	Lyantonde Central	The master-list entry Mpumudde seed school was reconciled to Rwamabara Seed Secondary School.
S084 Kiringente Seed School	Mpigi Central	The master-list entry Kiringente Seed School was reconciled to Wamatovu Seed Secondary School.
H036 Kabbo	Mubende Central	The master-list entry Kabbo was reconciled to Nakawala Health Centre III.
S086 Kimenyedde Seed School	Mukono Central	The master-list entry Kimenyedde Seed School was reconciled to St Andrews Ndwadde mutwe Seed Secondary School.
H054 Bussi HC II	Wakiso Central	Bussi is the village name for Zinga Health Centre III; the Zinga return is counted once on H052.
H070 Busia Eastern Division	Busia MC Eastern	The master-list entry Busia Eastern Division does not exist under the programme.
S012 Central Division	Jinja City Eastern	The master-list entry Central Division does not exist under the programme.
S010 Eastern Division	Tororo MC Eastern	The master-list entry Eastern Division does not exist under the programme.
H086 Buyinda HC II	Kaliro Eastern	Buyinda HC II is not a UgIFT beneficiary.
S011 Igombe	Bugweri Eastern	The master-list entry Igombe was reconciled to Mpiita Seed Secondary School.
H125 Kocheke HC II	Bukedea Eastern	The master-list entry Kocheke HC II was reconciled to Kangole / Kocheke Health Centre III.
S127 Bunambutye Seed School	Bulambuli Eastern	The master-list entry Bunambutye Seed School was reconciled to Bumufuni Seed Secondary School.
H065 Dabani	Busia Eastern	The master-list entry Dabani was reconciled to Buwumba Health Centre III.
S112 Butagaya	Jinja Eastern	The master-list entry Butagaya was reconciled to Buwala Seed Secondary School.
S122 Mwema Seed School	Namayingo Eastern	The master-list entry Mwema Seed School was reconciled to Mutumba Seed Secondary School.
S103 Pallisa	Pallisa Eastern	The master-list entry Pallisa was reconciled to Akadot Seed Secondary School.
S167 Kadungulu Seed School	Serere Eastern	The master-list entry Kadungulu Seed School was reconciled to Kagwara Seed Secondary School.
H231 Alangi	Zombo Northern	The UgIFT assets for Alangi were relocated to Amwonyo Health Centre III.
H233 Ther-uru HC II	Zombo Northern	The UgIFT assets for Ther-uru HC II were relocated to Atyak Health Centre III.
S208 Abanga	Zombo Northern	The UgIFT assets for Abanga were relocated to Kango Seed Secondary School.
H190 Alik HCII	Lira Northern	The master-list entry Alik HCII does not exist under the programme.
H195 Acokara HCII	Oyam Northern	The master-list entry Acokara HCII does not exist under the programme.

Master-list entry	Local government	Reconciled outcome
H197 Acimi HC II	Oyam Northern	The master-list entry Acimi HC II does not exist under the programme.
H200 Ariba HC II	Oyam Northern	The master-list entry Ariba HC II does not exist under the programme.
H205 Olok HC II	Pader Northern	Olok Health Centre III was not constructed under the programme.
H149 Pandwong HC II	Kitgum MC Northern	Pandwong HC II exists with no UgIFT assets.
H193 Alira HCII	Oyam Northern	Alira HCII is not a UgIFT beneficiary.
H150 Ngomoromo HC II	Lamwo Northern	The master-list entry Ngomoromo HC II was replaced by Pangira Health Centre III.
H213 Loinya HC II	Maracha Northern	The master-list entry Loinya HC II was replaced by Liko Health Centre III (H212).
H218 Oweko HC II	Nebbi Northern	The master-list entry Oweko HC II was replaced by Pamaka Health Centre III.
S216 Kishangara seed school	Ibanda Western	The master-list entry Kishangara seed school does not exist under the programme.
S214 Bumbaire Seed School	Bushenyi Western	Bumbaire Seed School exists with no UgIFT assets.
S215 Kyamuhunga	Bushenyi Western	Kyamuhunga exists with no UgIFT assets.
S221 Kashenshero	Mitooma Western	Kashenshero exists with no UgIFT assets.
H282 Rwamujojo HC II	Sheema MC Western	Rwamujojo HC II exists with no UgIFT assets.
S237 Kiziranfumbi Seed School	Kikuube Western	Kiziranfumbi Seed School is not a UgIFT beneficiary.
S213 Nsiika T/C	Buhweju Western	The master-list entry Nsiika T/C was reconciled to Ndibarema Memorial Seed Secondary School.
H318 Mantoroba HC II	Bundibugyo Western	The master-list entry Mantoroba HC II was reconciled to Busanga Health Centre III.
S056 Kabonero	Bunyangabu Western	The master-list entry Kabonero was reconciled to Katugunda Seed Secondary School.
S057 Kyamukube Town Council	Bunyangabu Western	The master-list entry Kyamukube Town Council was reconciled to Nsuura Seed Secondary School.
S230 Buhanika	Hoima Western	The master-list entry Buhanika was reconciled to Kidukuru Seed Secondary School.
H329 Kidubuli HC II	Kabarole Western	The master-list entry Kidubuli HC II was reconciled to Iruhura Health Centre III.
H332 Nyabuswa HC II	Kabarole Western	The master-list entry Nyabuswa HC II was reconciled to Nyambuusa Health Centre III.
S252 Kasenda Seed School	Kabarole Western	The master-list entry Kasenda Seed School was reconciled to St Paul Nyabweya Seed Secondary School.
S048 Kagadi	Kagadi Western	The master-list entry Kagadi was reconciled to King Solomon Seed Secondary School.

Master-list entry	Local government	Reconciled outcome
S049 Ruteete	Kagadi Western	The master-list entry Ruteete was reconciled to Kitegwa Community Seed Secondary School.
S232 Kiryanga Seed School	Kagadi Western	The master-list entry Kiryanga Seed School was reconciled to St Catherine Kicucura Seed Secondary School.
H292 Kikoola	Kakumiro Western	The master-list entry Kikoola was reconciled to Mukoora Health Centre III.
S235 Mugarama(new facilities for St Mugagga S.S)	Kibaale Western	The master-list entry Mugarama(new facilities for St Mugagga S.S) was reconciled to St Mugagga Vocational Seed Secondary School.
H354 Musandama HC II	Ntoroko Western	The master-list entry Musandama HC II was replaced by Butungama Health Centre III.

Table 27 provides the facility-level detail supporting section 4.1.

Table 28: Ground-return identities outside master-list names

ID	Name in ground return	Local government	Region
X013	Amei Seed Secondary School	Zombo	Northern
X016	Odupiri HC III	Maracha	Northern
X901	Ekaligo Health Centre III	Yumbe	Northern
X902	Liko Health Centre III	Yumbe	Northern
X017	Lobe HC III	Yumbe	Northern
X018	Nyori HC III	Yumbe	Northern
X019	Onywako HC III	Lira	Northern
X020	Arocha HC III	Apac	Northern
X021	Rupa Seed Secondary School	Moroto	Northern
X022	Lokori Seed Secondary School	Karenga	Northern
X900	Sofia Health Centre III	Busia MC	Eastern
X024	Simu Pondo HC III	Sironko	Eastern
X003	Kabushaho Seed Secondary School	Bushenyi	Western
X004	Kitojo Seed School	Mitooma	Western
X005	Migina HC III	Sheema	Western
X025	Kibuzigye Secondary School	Rubanda	Western
X026	Bushogyi Seed Secondary School	Kanungu	Western
X027	Bikurungu Seed Secondary School	Rukungiri	Western
X007	Rukoki General Hospital	Kasese	Western
X030	Bukuuku Community Secondary School	Fort-Portal City	Western
X010	Silumira HC III	Kakumiro	Western
X032	Buvuma HC III	Buvuma	Central
X903	Buloba Health Centre III	Wakiso	Central
X033	Lwengenyi HC III	Lwengo	Central

Table 28 lists the 24 return identities by local government. Linked receiving facilities and the separately allocated blood banks remain in their own reconciliation accounts.

Appendix G Asset information for institutional handover

The information prepared for institutional handover covers 225,133 assets. It includes asset descriptions, locations, condition, use and custody details, together with available valuation and depreciation information.

Table 29: Asset information prepared for handover

Asset scope	Assets	Information held	Handover purpose
Whole programme	225,133	Identification, location, condition, use, custody and available valuation details.	Institutional accountability, maintenance planning and financial reporting.

Table 29 summarises the asset information prepared for handover. Asset identifiers, classifications, identification marks, use and custody details, and available cost and depreciation values support institutional accountability, maintenance planning and financial reporting.

Appendix H Evidence supporting the findings

The findings draw on physical inspection, discussions with facility managers and technical officers, photographs, asset inventories and supervisor reconciliation. Facility examples identify the location, the issue requiring action and its effect on services. Photographs document the condition of selected facilities and assets at the time of the visits.

Service benefits described by facility managers are presented as their experience of the programme. The action plan sets out the recommended next steps and proposed responsibilities.
