



**CONSULTANCY SERVICES TO VERIFY AND RECORD ASSETS
UNDER THE UGIFT PROGRAMME**

REF: MOFPED/UGIFT/CONS/25/26/00015

ASSET VERIFICATION REPORT

SUBMITTED BY:

SK&CO Seijaaka, Kaawaase & Co.
AUDIT • ADVISORY • FORENSICS Certified Public Accountants

Plot 31, Bukoto Street
P.O Box 7657, Kampala, Uganda
+256 (0) 39 2000216/0772525235
email: cpa@cpa.ug
www.cpa.com

September 2026

Contents

Executive summary	7
1 Introduction and background	13
1.1 Introduction	13
1.2 Background to the verification	13
1.3 Justification	14
1.4 Objectives of the assignment	14
1.5. Scope of Work	15
1.6. Expected deliverables	15
2 Approach and methodology	16
2.1 Preparation:	16
2.2. Data collection	16
2.3. Quality assurance	16
2.4 Asset categories, condition, use and identification.....	16
2.5 Valuation basis	17
2.6 Analysis and reportingr	17
2.7. Challenges and Limitations to the assignment.....	17
4 Findings.....	19
4.1 National level: ministries, departments and agencies	19
4.2 Blood banks	26
4.3 Local governments: health centres and seed schools.....	30
4.4 Conditions and use status	39
4.5 Status of equipment.....	42
4.6 Financial value of verified assets.....	52
4.7 UgIFT support to service delivery.....	54
4.8 Summary of findings	59
5 Recommendations	60
5.1 Maintenance and repairs	60
5.2 Restore safe operation.....	62
5.3 Complete works and bring stored assets into use	62
5.4 Equip staff to operate and maintain assets.....	63
5.5 Strengthen identification and custody.....	63
5.6 Resolve programme-list inconsistencies	64
5.7 Plan for continued service delivery	65
5.8 Priorities for follow-up	65
5.9 Facility findings and recommended actions.....	67
6 Conclusion.....	70
Appendices	71
Appendix A Summary count schedule.....	71
Appendix B Asset totals by category and register class	72
Appendix C Condition and use schedules	73
Appendix D Recorded value and net book value schedules.....	74
Appendix E Utilisation and identification schedules	76
Appendix F Programme-list reconciliation	77
Appendix G Asset information for institutional handover	83
Appendix H Evidence supporting the findings	83
Appendix I Photographic record of verified assets	83

List of tables

Table 1: Key statistics of the UgIFT asset verification.....	7
Table 5: Verified assets engraved and not engraved at national ministries, departments and agencies	19
Table 6: Condition and use of assets at national ministries, departments and agencies.....	20
Table 7: Computers at national ministries, departments and agencies: condition, engraving and use	21
Table 8: Assets at referral and general hospitals by type of hospital	26
Table 9: Assets at the regional blood banks: condition, use, engraving and recorded value.....	26
Table 10: Programme-list facilities verified, completed and providing services	30
Table 11: Facilities requiring completion or preparation for use	32
Table 12: Inconsistencies between the programme list and the facilities found	34
Table 13: Expected facilities and the outcomes established during verification.....	36
Table 14: Confirmed additional beneficiaries outside the programme list	37
Table 15: Assets verified at health centres and seed schools by asset category.....	38
Table 16: Condition and use status by institution group.....	39
Table 17: Engraving of verified assets by institution group.....	43
Table 18: Examples of local governments with assets in storage	47
Table 19: Recorded value, depreciation and net book value by institution group.....	52
Table 20: Recorded value, depreciation and net book value by ministry, department and agency	53
Table 21: User gaps and challenges raised by facilities that described service delivery	57
Table 22: Priority actions to protect assets and restore service	65
Table 23: Facility findings and recommended actions	67
Table 24: Summary count schedule by institution group.....	71
Table 25: Assets by report category and institution group	72
Table 26: Assets by register class and institution group	72
Table 27: Working and not working assets by report category.....	73
Table 28: Stated reasons for assets not in use by institution group.....	74
Table 29: Recorded value and net book value by institution group.....	74
Table 30: National value schedule: MDAs, hospitals and blood banks	75
Table 31: Recorded value and net book value by report category.....	75
Table 32: Engraving of verified assets by institution group.....	76
Table 33: Engraving of verified assets by report category	76
Table 34: Facilities with assets not in use, in storage or broken down by institution group.....	77
Table 35: Programme-list entries with an inconsistency.....	77
Table 36: Ground-return identities outside the programme list	79
Table 37: Verified facilities with works outstanding or not yet providing services	80
Table 38: Asset information prepared for handover.....	83

List of figures

Figure 1: Completed blood bank building at Arua Regional Blood Bank, Arua City (West Nile).....	27
Figure 2: Donor couches in the donor room at Arua Regional Blood Bank, Arua City (West Nile).....	27
Figure 3: Markings PEP II/UBTS/COMP/11/016 and UBTS/UGIFT/ARBB/UPS/001 on uninterruptible power supplies at Arua Regional Blood Bank, Arua City (West Nile).....	27
Figure 4: Blood bank refrigerator at Arua Regional Blood Bank, Arua City (West Nile).....	28
Figure 5: Platelet agitator at Arua Regional Blood Bank, Arua City (West Nile).....	28
Figure 6: Chest freezer at Arua Regional Blood Bank, Arua City (West Nile).....	28
Figure 7: Donor couches in the donor room at Hoima Regional Blood Bank, Hoima City (Bunyoro).....	29
Figure 8: Engraving reading UBTS/UGIFT/VCH/001 on equipment at Hoima Regional Blood Bank, Hoima City (Bunyoro).....	29
Figure 9: Blood collection balance at Hoima Regional Blood Bank, Hoima City (Bunyoro).....	29
Figure 10: Benchtop centrifuge at Hoima Regional Blood Bank, Hoima City (Bunyoro).....	29
Figure 11: Water fire extinguisher at Hoima Regional Blood Bank, Hoima City (Bunyoro).....	29
Figure 12: Generator in an outdoor enclosure at Hoima Regional Blood Bank, Hoima City (Bunyoro).....	29
Figure 13: A third of verified seed schools had works outstanding.....	31
Figure 14: Unfinished school block at Got Apwoyo Seed Secondary School, Nwoya District (Achoi).....	33
Figure 15: Unfinished classroom block at Sidok Seed Secondary School, Kaabong District (Karamoja).....	33
Figure 16: Latrine block under construction at Sidok Seed Secondary School, Kaabong District (Karamoja).....	33
Figure 17: Building works and construction materials at Ndheew Seed Secondary School, Nebbi District (West Nile).....	33
Figure 18: School block awaiting completion at Butungama Seed Secondary School, Ntoroko District (Tooro).....	33
Figure 19: Building works at a seed secondary school, Kiboga District (Buganda).....	33
Figure 20: Classroom block with earthworks in the foreground at Kihungya Seed Secondary School, Buliisa District (Bunyoro).....	33
Figure 21: Unfinished laboratory building at a health centre, Sironko District (Bugisu).....	33
Figure 22: Biology laboratory under construction at a seed secondary school, Buliisa District (Bunyoro).....	33
Figure 23: Unfinished laboratory interior at Kihungya Seed Secondary School, Buliisa District (Bunyoro).....	33
Figure 24: Library interior under construction at Kihungya Seed Secondary School, Buliisa District (Bunyoro).....	34
Figure 25: ICT laboratory interior under construction at Kitawoi Seed Secondary School, Kween District (Sebei).....	34
Figure 26: Laboratory benches with cupboard doors not yet fitted, in a science laboratory block recorded as under construction, at King Solomon Seed Secondary School, Kagadi District (Bunyoro).....	34
Figure 27: Empty computer laboratory at Kaptum Seed Secondary School, Kween District (Sebei), where the buildings had not been handed over and no ICT equipment had been received.....	34
Figure 28: Most assets in every category were working.....	40
Figure 29: Clinical equipment and school computers had the most assets not in use.....	41
Figure 30: Delivery bed with a torn mattress cover at a health centre, Busia District (Bukedi).....	42
Figure 31: Damaged drip stand at a health centre, Moroto District (Karamoja).....	42
Figure 32: Broken desk frame at a seed secondary school, Namisindwa District (Bugisu).....	42
Figure 33: Stacked desks, chairs and stools, some recorded as broken and none engraved, at Napak Seed Secondary School, Napak District (Karamoja).....	42
Figure 34: Cracked health centre block above collapsed ground, Bulambuli District (Bugisu).....	42
Figure 35: Water tank on a cracked base at a seed secondary school, Kibuku District (Bukedi).....	42
Figure 36: Stained and peeling ceiling at a health centre, Sironko District (Bugisu).....	42
Figure 37: Flood-affected older health facility at Butiaba, Buliisa District (Bunyoro).....	42
Figure 38: Most verified movable assets were not engraved.....	43
Figure 39: Engraving reading GOU/MOH-UGIFT PROJECT FY/2023/2024 on a desk at Namwaya Health Centre III, Tororo District (Bukedi).....	44
Figure 40: Engraving reading APESSS MOES/UGIFT/KABE/SPLRS/2023-24/001 on a desk at Aperikira Seed Secondary School, Kaberamaido District (Teso).....	44
Figure 41: Chair engraved UGIFT/ BUDDE SEED S.S M-PHALL CHAIR with a serial number at Budde Seed Secondary School, Butambala District (Buganda).....	44
Figure 42: Chairs engraved BSS UGIFT with serial numbers at Budde Seed Secondary School, Butambala District (Buganda).....	44
Figure 43: Engraving reading GOU/MOH-UGIFT PROJECT F/Y 2023/2024 on a bench at Bududa Health Centre III, Bududa District (Bugisu).....	45
Figure 44: Wheelchair backrest marked GOU/MOH UGIFT-PROJECT. FY2023/2024 at Kalemungole Health Centre III, Moroto District (Karamoja).....	45
Figure 45: Refrigerator marked GOU/MOH-UGIFT PROJECT FY2024-2025/01 at Kalemungole Health Centre III, Moroto District (Karamoja).....	45
Figure 46: Engraving reading GOU/MOH-UGIFT PROJECT FY2023-2024/01 on a weighing scale at Kalemungole Health Centre III, Moroto District (Karamoja).....	45

Figure 47: Engraving reading GOU/MOH-UGIFT PROJECT FY2023-2024/01 on a delivery bed at Kalemungole Health Centre III, Moroto District (Karamoja)	45
Figure 48: Engraving reading GOU/MOH-UGIFT PROJECT FY/2023/2024 on a table at Kamoru Health Centre III, Kotido District (Karamoja)	45
Figure 49: Engraving reading KDLG-UGFIT/HLTH/MAT/ODT/003 on a table at Kyabasara Health Centre III, Kagadi District (Bunyoro)	45
Figure 50: Classroom desks marked RUPA SEED with serial numbers, without a UgIFT marking, at Rupa Seed School, Moroto District (Karamoja).....	46
Figure 51: Engraving reading KWN/MED-EQ/MOYOK HCIII on a steel cupboard at Moyok Health Centre III, Kween District (Sebei)	46
Figure 52: Engraving reading KING SOLOMON SEED SECONDARY SCHOOL, without a UgIFT marking, on furniture at King Solomon Seed Secondary School, Kagadi District (Bunyoro)	46
Figure 53: Microscope marked KAMORU HC III by hand at Kamoru Health Centre III, Kotido District (Karamoja).....	46
Figure 54: Hand-scratched marking beginning Bumugibole/2020- on a wheelchair armrest at Bumugibole Health Centre III, Bulambuli District (Bugisu)	46
Figure 55: Desktop computers, a printer and UPS units still boxed in the store at Lungulu Seed Secondary School, Nwoya District (Acholi), awaiting a power connection for installation.....	48
Figure 56: Largely empty ICT and library block with a few chairs and items kept in one corner at Iriiri Seed Secondary School, Napak District (Karamoja), not yet in use while the school remained with the contractor	48
Figure 57: HP computer sets stacked in store with cables still bundled and not installed at Bumufuni Seed Secondary School, Bulambuli District (Bugisu)	49
Figure 58: Laboratory stools and desks stored and not yet in use at Butungama Seed Secondary School, Ntoroko District (Tooro), where the school buildings were still under construction	49
Figure 59: Boxed projector, air conditioner and other equipment in store at King Solomon Seed Secondary School, Kagadi District (Bunyoro), kept boxed because the school was still under construction	49
Figure 60: Chairs, desks and laboratory stools stacked in a hall at King Solomon Seed Secondary School, Kagadi District (Bunyoro), where most assets remained in storage because the school was still under construction	49
Figure 61: Clinical equipment kept in store among cartons and not in use at Kihuukya Health Centre III, Hoima City (Bunyoro)	50
Figure 62: Boxed handheld pulse oximeters at Kibiri Health Centre III, Makindye-Ssabagabo Municipal Council (Buganda), where equipment was still being arranged after the facility opened on 31 August 2026.....	50
Figure 63: Hospital beds and screens stacked in storage at a health centre, Kagadi District (Bunyoro)	50
Figure 64: Pedal suction unit marked MAJANJI H/C III still in its packing, recorded as not in use for lack of technical knowledge, Majanji Health Centre III, Busia District (Bukedi)	50
Figure 65: Breakdowns and storage were the main reasons assets were not in use	51
Figure 66: Power and user skills were the main reasons equipment stood idle	52
Figure 67: Seed schools and health centres hold most of the recorded value.....	53
Figure 68: MoES and MoFPED hold the largest ministry recorded values	54
Figure 69: Maternity care and access to education were the most reported benefits	55
Figure 70: Health centre building at Kibiri HC III, Makindye-Ssabagabo Municipal Council (Buganda)	56
Figure 71: Health centre buildings and covered walkway at Kihuukya HC III, Hoima City (Bunyoro).....	56
Figure 72: Binocular microscope at Kihuukya HC III, Hoima City (Bunyoro).....	56
Figure 73: Adult weighing scale with a height meter and waiting benches at Iruhura HC III, Kabarole District (Tooro).....	56
Figure 74: Maternity block entrance and access ramp at Kamuli HC III, Tororo District (Bukedi).....	56
Figure 75: Classroom furnished with desks and a whiteboard at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)	57
Figure 76: Books displayed on library shelves at Sibanga Seed School, Manafwa District (Bugisu).....	57
Figure 77: ICT laboratory block and entrance ramp at Sisiyi Seed Secondary School, Bulambuli District (Bugisu)	57
Figure 78: Power, staffing and space were the gaps most often raised.....	58
Figure 79: Most facilities met repairs from their own funds or staff	61
Figure 80: Annual, monthly and quarterly checks were the most common stated intervals.....	61
Figure 81: Infant radiant warmer at a health centre, Makindye-Ssabagabo Municipal Council (Buganda)	84
Figure 82: Oxygen cylinders marked KIBIRI HCIII at Kibiri HC III, Makindye-Ssabagabo Municipal Council (Buganda)	84
Figure 83: Wooden waiting bench at Kibiri HC III, Makindye-Ssabagabo Municipal Council (Buganda)	84
Figure 84: Delivery bed and clinical furniture at a health centre, Kabarole District (Tooro)	84
Figure 85: Oxygen concentrator at Kalemungole HC III, Moroto District (Karamoja)	84
Figure 86: Suction apparatus at Kalemungole HC III, Moroto District (Karamoja)	84
Figure 87: Oxygen concentrator at Kamoru HC III, Kotido District (Karamoja)	84
Figure 88: Instrument trolley with delivery instruments at Kamoru HC III, Kotido District (Karamoja)	84
Figure 89: Medical-waste bins and ward beds at Butiaba HC III, Buliisa District (Bunyoro)	84
Figure 90: Laboratory centrifuge at Butiaba HC III, Buliisa District (Bunyoro)	84
Figure 91: Blood pressure apparatus on a mobile stand at Butiaba HC III, Buliisa District (Bunyoro).....	85
Figure 92: Office chairs at Butiaba HC III, Buliisa District (Bunyoro)	85

Figure 93: Kangaroo care chair at Kyabasara HC III, Kagadi District (Bunyoro)	85
Figure 94: Infant weighing scale at Buwembe HC III, Busia District (Bukedi)	85
Figure 95: Autoclave above a gas cylinder at Buwembe HC III, Busia District (Bukedi)	85
Figure 96: Autoclave at Atar HC III, Kween District (Sebei)	85
Figure 97: Kangaroo care chair at Atar HC III, Kween District (Sebei)	85
Figure 98: Binocular microscope on a trolley at Namusita HC III, Budaka District (Bukedi)	85
Figure 99: Infant weighing scales at Namusita HC III, Budaka District (Bukedi)	86
Figure 100: Delivery bed with side rails at Kabweri HC III, Kibuku District (Bukedi)	86
Figure 101: Health centre building, Nwoya District (Acholi)	86
Figure 102: Solar panels at Kalemungole HC III, Moroto District (Karamoja)	86
Figure 103: Patient toilet block at Kalemungole HC III, Moroto District (Karamoja)	86
Figure 104: Power house at Kyabasara HC III, Kagadi District (Bunyoro)	86
Figure 105: Latrine block and paved access at Kyabasara HC III, Kagadi District (Bunyoro)	86
Figure 106: Solar batteries at Bunangaka HC III, Bulambuli District (Bugisu)	87
Figure 107: Solar batteries and control equipment at Atar HC III, Kween District (Sebei)	87
Figure 108: Sanitation block with external handwashing basins at Kibiri HC III, Makindye-Ssabagabo Municipal Council (Buganda)	87
Figure 109: Waste disposal structure at Kibiri HC III, Makindye-Ssabagabo Municipal Council (Buganda)	87
Figure 110: Water tanks on a steel tower at Kabweri HC III, Kibuku District (Bukedi)	87
Figure 111: Science laboratory tables and stools at a seed secondary school, Kalangala District (Buganda)	87
Figure 112: Library shelves and reading tables at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)	87
Figure 113: Anatomical teaching model at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)	88
Figure 114: Laboratory glassware and equipment at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)	88
Figure 115: Desktop computers and classroom furniture at a seed secondary school, Busia District (Bukedi)	88
Figure 116: Classroom desks at a seed secondary school, Ntoroko District (Tooro)	88
Figure 117: Classroom desks at King Solomon Seed Secondary School, Kagadi District (Bunyoro)	88
Figure 118: Laboratory benches and sinks at Bweema Seed Secondary School, Buvuma District (Buganda)	88
Figure 119: Classroom desks at Bweema Seed Secondary School, Buvuma District (Buganda)	89
Figure 120: Laboratory supplies and an anatomical teaching model at Rupa Seed School, Moroto District (Karamoja)	89
Figure 121: Computer equipment in the school ICT room at Kabeywa Seed Secondary School, Kapchorwa District (Sebei)	89
Figure 122: Library shelving and tables at Kabeywa Seed Secondary School, Kapchorwa District (Sebei)	89
Figure 123: Office desk and other furniture at Lwamata Town Council Seed Secondary School, Kiboga District (Buganda)	89
Figure 124: Laboratory tables at Lwamata Town Council Seed Secondary School, Kiboga District (Buganda)	89
Figure 125: Library shelving at Lwamata Town Council Seed Secondary School, Kiboga District (Buganda)	89
Figure 126: Anatomical skeleton teaching model at Kamonkoli Seed Secondary School, Budaka District (Bukedi)	89
Figure 127: Laboratory benches, stools and sinks at Nansanga Seed Secondary School, Budaka District (Bukedi)	90
Figure 128: Library shelving with books at Nansanga Seed Secondary School, Budaka District (Bukedi)	90
Figure 129: Buildings at a seed secondary school, Nwoya District (Acholi)	90
Figure 130: School blocks at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)	90
Figure 131: School buildings and courtyard at a seed secondary school, Buvuma District (Buganda)	91
Figure 132: Raised water storage tank at a seed secondary school, Buvuma District (Buganda)	91
Figure 133: Sanitation block at Bweema Seed Secondary School, Buvuma District (Buganda)	91
Figure 134: Water tank and enclosed service structures at Bweema Seed Secondary School, Buvuma District (Buganda)	91
Figure 135: Borehole apron and pipework at Katikekire Seed School, Moroto District (Karamoja)	91
Figure 136: Section of the science laboratory exterior at Iriiri Seed Secondary School, Napak District (Karamoja)	91
Figure 137: Water storage tanks at Lopei Seed Secondary School, Napak District (Karamoja)	91
Figure 138: Computer and library block at Lopei Seed Secondary School, Napak District (Karamoja)	92
Figure 139: Water tanks on a rendered plinth and steel tower at Alerek Seed Secondary School, Abim District (Karamoja)	92
Figure 140: Water storage tanks at Rengen Seed School, Kotido District (Karamoja)	92
Figure 141: Gas cylinders and pipework at King Solomon Seed Secondary School, Kagadi District (Bunyoro)	92
Figure 142: Water tank on a masonry support at King Solomon Seed Secondary School, Kagadi District (Bunyoro)	92
Figure 143: Elevated water tank on a steel tower at King Solomon Seed Secondary School, Kagadi District (Bunyoro)	92
Figure 144: Rainwater tank beside a staff house at Rupa Seed School, Moroto District (Karamoja)	92

List of acronyms

GOU	Government of Uganda
HC	Health centre
ICT	Information and communications technology
IFMIS	Integrated Financial Management Information System
KCCA	Kampala Capital City Authority
LGFC	Local Government Finance Commission
MAAIF	Ministry of Agriculture, Animal Industry and Fisheries
MDA	Ministry, department or agency
MoDVA	Ministry of Defence and Veteran Affairs
MoES	Ministry of Education and Sports
MOES	Ministry of Education and Sports (as engraved)
MoFPED	Ministry of Finance, Planning and Economic Development
MoGLSD	Ministry of Gender, Labour and Social Development
MoH	Ministry of Health
MOH	Ministry of Health (as engraved)
MoLG	Ministry of Local Government
MoLHUD	Ministry of Lands, Housing and Urban Development
MoPS	Ministry of Public Service
MoWE	Ministry of Water and Environment
MoWT	Ministry of Works and Transport
NEMA	National Environment Management Authority
OAG	Office of the Auditor General
OPM	Office of the Prime Minister
PforR	Programme-for-Results
PPDA	Public Procurement and Disposal of Public Assets Authority
RCU	Reform Coordination Unit
TELA	Teacher Effectiveness and Learner Assessment
UBTS	Uganda Blood Transfusion Services
UgIFT	Uganda Intergovernmental Fiscal Transfer
UGX	Uganda shillings
UPS	Uninterruptible power supply

Executive summary

The Uganda Intergovernmental Fiscal Transfers (UgIFT) Programme is a government programme implemented through a Programme-for-Results (PforR) operation, launched and aligned with the broader Intergovernmental Fiscal Transfer Reform Programme (2015). UgIFT began with US\$200 million in financial year 2017/18, supporting education and health. It was later expanded through additional financing of US\$300 million, including support for refugee hosting districts, to water and environment and to agriculture (micro-scale irrigation), bringing the overall funding to US\$500 million.

The implementation of the UgIFT programme came to an end on 31 December 2025. As part of the programme closure activities, the Ministry of Finance, Planning and Economic Development (MoFPED), through the Reform Coordination Unit (RCU), carried out an end of programme asset verification exercise to take stock of the assets procured under the programme and to help put in place plans to hand them over to government for sustainability purposes.

The exercise was conducted at two levels: the national level ministries, departments and agencies (MDAs) of government, and the local governments, covering the government seed secondary schools in underserved subcounties and the health facilities upgraded from Health Centre II to Health Centre III. At national level, the verification focused on retooling assets such as computers, tablets, photocopiers, furniture, motorcycles and motor vehicles. At local government level, all 176 local governments (districts, cities and municipalities) were visited and the assets verified.

The verification found that UgIFT buildings and equipment were supporting services, while unfinished works, power constraints, damage and delayed installation prevented some assets from serving their intended purpose. The main follow-up is to put unused assets into service and sustain those already working.

Scope and coverage

National verification began on 24 July 2026 with the 15 MDAs listed for the exercise, 13 of which held UgIFT assets. The national findings also cover the assets at 68 referral and general hospitals and on two other national votes. The three regional blood banks and the 176 local governments were verified from 24 August to 7 September 2026. At local government level, the programme list, which sets out the facilities planned for verification before the exercise started, held 629 facilities: 371 health centres and 258 seed schools (section 2.4). Accessories and consumables were not part of the verification.

Findings are reported at national level in the order of the fieldwork: national institutions in section 4.1, the blood banks in section 4.2 and the local government health centres and seed schools in section 4.3, followed by conditions and use status, status of equipment, financial value and service delivery in sections 4.4 to 4.7. Table 1 summarises the key statistics.

Table 1: Key statistics of the UgIFT asset verification

Measure	Result
Coverage and facilities	
MDAs visited	15, of which 13 held UgIFT assets
Regional blood banks verified	3 (Arua, Hoima and Soroti)
Local governments visited	176
Facilities on the programme list	629 (371 health centres and 258 seed schools)
Facilities verified	590 (93.8%)
Verified facilities with works completed	475 (80.5%)

Measure	Result
Verified facilities with works not completed	115 (19.5%)
Verified facilities providing services	520 (88.1%)
Programme-list facilities that were not UgIFT in practice	18 (2.9%), including 10 that do not exist or were not constructed
Assets	
Assets in the UgIFT asset verification records	234,613
Working and in use	221,093 (94.2%)
Not working and not in use	13,520 (5.8%)
Broken down, damaged or obsolete	3,392 (1.4%)
In storage	3,200 (1.4%)
Computers on national votes working and in use	1,059 of 1,074 (98.6%)
Identification	
Verified assets (movable assets)	224,705
Engraved	49,463 (22.0%)
Properly engraved (UgIFT marking)	23,440 (10.4%)
Not properly engraved (another marking only)	26,023 (11.6%)
Not engraved	175,242 (78.0%)
Value at 30 September 2026	
Recorded value	UGX 997,840,855,042
Net book value	UGX 812,316,492,277
Maintenance and service delivery	
Facilities working to a fixed maintenance interval	50 of 494 (10.1%)
Facilities reporting idle or unusable equipment	156 of 477 (32.7%)
Health centres reporting at least one benefit	237 of 284 (83.5%)
Health centres reporting improved maternity and delivery services	117 of 284 (41.2%)
Seed schools reporting at least one benefit	144 of 193 (74.6%)
Facilities raising power as a gap	200 of 477 (41.9%)

Counts of facilities for coverage, facilities, maintenance and service delivery; counts of assets otherwise. Facilities verified is a share of the programme list, and the works and services shares are of verified facilities. Asset shares are of all assets unless another base is shown, identification shares are of verified assets, and maintenance and service delivery shares are of the facilities that answered.

Conditions and use status

The UgIFT asset verification records hold 234,613 assets: 25,627 at national institutions and 208,982 (89.1%) at health centres and seed schools. Of all assets, 221,093 (94.2%) were working and in use and 13,520 (5.8%) were not working and not in use; the records treat a working asset as in use, so the two shares are the same. Of the assets not in use, 3,392 (25.1%) were broken down, damaged or obsolete and 3,200 (23.7%) were in storage. Clinical equipment (86.7%) and school computers and related equipment (85.5%) had the lowest shares in use (section 4.4).

Identification (engraving) and custody

Of the 224,705 verified assets, which are the movable assets, 22.0% were engraved and 78.0% were not engraved. Only 10.4% were properly engraved with the UgIFT marking, while 11.6% were not properly engraved, carrying another marking only, such as a school, district or ministry code; these made up 52.6% of the engraved assets (section 4.5.1).

The records also describe assets that were not at the facility at the time of the visit: 2,522 (18.7%) of the assets not in use had not yet been delivered or handed over, were held elsewhere or were not at the facility when the teams visited, including 985 assets for five seed schools that the suppliers had not yet delivered. A further 525 assets, mostly computers and related equipment at seed schools, were reported stolen or lost.

National level: ministries, departments and agencies

The 16,902 assets on MDA and other national votes include 10,783 at the Ministry of Education and Sports (MoES), mainly 9,324 Teacher Effectiveness and Learners Assessment (TELA) handsets and 1,001 tablets. LGFC and MoPS received no UgIFT assets. Of the 16,902 assets, 16,882 (99.9%) were working and in use; the other 20 were 16 assets whose location MoWT was tracing, 3 damaged laptops at OPM and 1 boarded off pickup at MoH.

Of the 15,609 verified assets on national votes, 4,849 (31.1%) were engraved, 97.7% of them with the UgIFT marking. Every verified asset was engraved at OPM, PPDA and OAG, while the MoES handsets and tablets account for 10,325 of the 10,760 assets not engraved (Table 5).

The national votes hold 1,074 computers (424 desktops and 650 laptops). Of these, 1,059 (98.6%) were working and in use and 15 (1.4%) were not: 12 MoWT desktops whose location was being traced and the 3 damaged OPM laptops, the only computers broken down (0.3%). A total of 1,037 (96.6%) were engraved and 37 (3.4%) were not engraved, and 1,024 (95.3%) carried the UgIFT marking.

The 68 referral and general hospitals hold 8,099 assets, mainly oxygen cylinders and regulators (4,730 assets), oxygen plant components and intensive care unit equipment. All were working and in use, and none of the 7,745 verified assets was engraved (section 4.1.15).

Blood banks

UgIFT financed the construction of the Arua and Hoima regional blood banks, which were completed and commissioned, and the rehabilitation of Soroti Regional Blood Bank, all operating under Uganda Blood Transfusion Services (UBTS). The records hold 626 blood bank assets, of which 602 (96.2%) were working and in use; the 24 not in use were all at Arua, among them 6 broken blood pressure machines. Only 43 of the 605 verified assets (7.1%) were engraved, all at Arua, and 26 (4.3%) carried the UgIFT marking. Arua and Soroti named too few vehicles for blood collection and an unreliable water source among their challenges, together with too few medical personnel at Arua and insecurity at Soroti (section 4.2).

Local governments: health centres and seed schools

Of the 629 programme-list facilities, 590 (93.8%) were verified (Table 10). Works were complete at 475 (80.5%): 92.2% of verified health centres but only 63.8% of verified seed schools. Of the verified facilities, 520 (88.1%) were providing services, including 63 where some works were still outstanding, while 24 (4.1%), 21 of them seed schools, were not yet providing services (section 4.3.1).

Construction and service readiness need attention together. Got Apwoyo Seed Secondary School in Nwoya had not been commissioned and its ICT package remained at district headquarters. At Ndhew and Mamba seed schools in Nebbi, unfinished buildings delayed installation, while at Atego in the same district computers were already working in older rooms as construction continued.

School furniture was the largest asset category, with 109,713 assets or 75.5% of seed school assets, and clinical equipment and clinical furniture made up 72.5% of health centre assets. Health centres had the highest share not working (8.9%) and seed schools the largest number broken down (2,722). Seed schools had engraved 25.3% of their verified assets and health centres 15.2%, but more than half of these carried another marking only (section 4.3.3).

Inconsistencies with the programme list

Reconciliation identified 55 programme-list entries (8.7%) that differed from the facilities found: 10 that do not exist or were not constructed under the programme, 4 replaced by another facility, 30 operating under another name, 3 that are not UgIFT beneficiaries, 3 whose UgIFT assets were relocated to another facility and 5 that exist with no UgIFT assets (Table 12).

In all, 18 programme-list facilities (2.9%) were not UgIFT facilities in practice, although the programme list recorded 16 of them as complete. Eight (1.3%) exist but are not UgIFT beneficiaries or received no UgIFT assets. The other 10 do not exist or were not constructed under the programme: the health centre entries Olok HC II (Pader), Alik HC II (Lira), Acimi HC II, Acokara HC II and Ariba HC II (Oyam), Busia Eastern Division (Busia Municipal Council) and Butoloogo HC II (Kassanda), and the seed school entries Eastern Division (Tororo Municipal Council), Central Division (Jinja City) and Kishangara Seed School (Ibanda).

The programme list also recorded 44 facilities as complete where works were outstanding, and three facilities found outside the list were confirmed as additional beneficiaries. Section 4.3.2 sets out these cases and Appendix F names every facility with an inconsistency.

Utilisation status of assets

Utilisation, the share of assets in use, was 94.2%: 99.9% at MDAs, 100.0% at hospitals, 96.2% at blood banks, 94.6% at seed schools and 91.1% at health centres. Idle assets were nonetheless spread widely: 255 of the 354 health centres (72.0%) and 132 of the 255 seed schools (51.8%) in the records had at least one asset not in use.

The 3,200 assets in storage were at 181 facilities, 2,681 (83.8%) of them at health centres, with clinical equipment the largest group (1,685). Of the stored assets, 190 (5.9%) were waiting for a power connection, 80 (2.5%) for a building or room and 141 (4.4%) were held at district stores or at another facility, while 519 (16.2%) were described as new, boxed or in good condition. Examples include 211 stored assets at health centres in Kabarole and 159 in Omoro, and computer equipment kept in store at Akadot Seed Secondary School in Pallisa, which has no electricity, and at Lungulu Seed Secondary School in Nwoya, which was awaiting a power connection.

The 3,392 assets broken down were at 183 facilities, and school furniture accounted for 2,462 (72.6%) of them. The largest group was at Mpungwe Seed Secondary School in Mayuge District, with 275 assets, mainly learners' chairs and laboratory stools (section 4.5.2).

Of the 477 facilities that described their services, 156 (32.7%) reported equipment that was idle or could not be used. They linked it to power (45.5%), training or skills to operate the equipment (33.3%), installation or assembly (20.5%), incomplete buildings or lack of space (17.3%), missing accessories or consumables (9.6%) and staffing (5.8%). Training led at health centres (45.9%) and power at seed schools (53.3%). Pamaka Health Centre III in Nebbi, for example, could not use its oxygen equipment because of power constraints.

Maintenance practice

Of the 469 facilities that described their maintenance arrangements, 260 (55.4%) met repairs at facility level from their own funds or staff and 151 (32.2%) drew on district, regional or national technical support, while 36 (7.7%) reported no repair arrangement. Busaale Health Centre III in Kayunga, which used Primary Health Care funds for maintenance, still needed roof, door and solar repairs.

Of the 494 facilities that described how they maintain or check their assets, only 50 (10.1%) worked to a fixed interval: 28.0% of these annually, 22.0% monthly, 20.0% quarterly and 18.0% every school term. Another 62 (12.6%) repaired items as the need arose, and 318 of the 463 facilities that answered (68.7%) kept a regular record of asset functionality or breakdowns (section 5.1).

Service delivery benefits and user gaps

Of the 284 health centres that described service delivery, 237 (83.5%) reported at least one benefit from the UgIFT support. Improved maternity and delivery services were reported by 117 (41.2%), and 51 (18.0%) reported more or safer births at the facility; improved access to care was reported by 70 (24.6%) and more patients attending by 60 (21.1%). Kagumba Health Centre III in Kamuli reported more than 50 deliveries a month in its new maternity ward.

Of the 193 seed schools, 144 (74.6%) reported a benefit, led by a better learning environment (74, 38.3%) and improved access to secondary education (59, 30.6%), while practical science or ICT teaching improved at 39 schools (20.2%). Enrolment at Bwizi Seed Secondary School in Kamwenge grew from 204 to 1,108 students (section 4.7.1).

Nearly all facilities, 452 of the 477 (94.8%), also raised at least one gap, most often power (41.9%), staffing (32.3%), inadequate space or infrastructure (31.7%), security or fencing (27.3%) and repair or maintenance support (22.2%). Training to operate equipment was raised mainly by health centres (28.9%) and incomplete works mainly by seed schools (28.0%) (section 4.7.2).

Financial value

The 234,613 assets carry a recorded value of UGX 997,840,855,042 and a net book value of UGX 812,316,492,277 at 30 September 2026 (section 4.6). Seed schools hold UGX 678,247,549,426 (68.0%) and health centres UGX 259,662,849,164 (26.0%), mainly in buildings. National institutions hold UGX 59,499,320,714 (6.0%): MDAs UGX 31,967,493,589 (3.2%), hospitals UGX 26,080,242,410 (2.6%) and blood banks UGX 1,451,584,715 (0.1%). MoES holds UGX 14,925,128,359, or 46.7% of the MDA total. Net book value is 85.0% of recorded value at seed schools and 84.1% at health centres, but 39.1% at MDAs and 14.0% at hospitals, where the equipment is largely depreciated.

Main recommendations

Chapter 5 links each recommendation to the finding it answers. The main recommendations are:

- **Maintenance and repairs (section 5.1):** only 10.1% of facilities worked to a fixed maintenance interval and 36 reported no repair arrangement. Facilities should adopt a condition check every school term in schools and every quarter in health centres, an annual count of UgIFT assets and a fault list, with district offices reviewing unresolved repairs each quarter.
- **Restore safe operation (section 5.2):** 3,392 assets were broken down, damaged or obsolete. Facilities and districts should assess them in order of their effect on care and teaching, starting with clinical equipment and unsafe school furniture; OPM should decide on its three damaged laptops and UBTS on the six broken blood pressure machines at Arua.
- **Complete works and bring stored assets into use (section 5.3):** 115 verified facilities had works outstanding and 3,200 assets were in storage. Districts should agree site-specific completion plans, starting with the 22 of these facilities that were not yet providing services, and set dates to connect, install and issue stored assets once rooms and power are ready.
- **Equip staff to operate and maintain assets (section 5.4):** 52 facilities, 51 of them health centres, linked idle equipment to staff being unable to operate it. Suppliers and district health officers should provide practical training and demonstrate equipment to its users before acceptance.

- **Strengthen identification and custody (section 5.5):** 175,242 verified assets (78.0%) were not engraved and 26,023 carried another marking only. Asset managers should apply the UglFT marking, starting with hospital equipment and the MoES handsets and tablets, and document transfers between facilities.
- **Resolve programme-list inconsistencies (section 5.6):** MoFPED, with MoH, MoES and the local governments concerned, should approve a corrected programme list that removes or annotates the 18 entries that were not UglFT facilities in practice, links replaced and renamed entries, corrects the construction status of 48 entries and adds the 3 confirmed additional beneficiaries.
- **Plan for continued service delivery (section 5.7):** power, staffing and space were the gaps most often raised (41.9%, 32.3% and 31.7% of facilities). Districts and sector ministries should address them first and confirm facility readiness before future deliveries.

Table 22 in section 5.8 sets out eight priority actions with proposed owners, timing and evidence of completion. The proposed priorities are to make unsafe items safe, restore essential equipment, complete works and utilities, and install usable stored assets, with facility managers leading routine checks and minor repairs, supported by district engineers, health and education officers and the relevant technical teams.

1 Introduction and background

1.1 Introduction

This report presents the findings of the UglIFT asset verification undertaken by the Ministry of Finance, Planning and Economic Development as part of programme closure. It sets out the status of the assets provided by the programme at the national institutions responsible for its implementation¹, and at local government level in seed secondary schools and health facilities upgraded from Health Centre II to Health Centre III. The report also covers the assets of the three blood banks that the programme supported directly.

1.2 Background to the verification

The programme ended on 31 December 2025.

The Uganda Intergovernmental Fiscal Transfers (UglIFT) Programme is a government programme implemented through a Programme-for-Results (PforR) launched and aligned with the broader IGFT Reform Programme (2015). UglIFT 1.0 began with US\$200 million in FY2017/18, supporting Education and Health. This was later expanded through additional financing of US\$300 million, including US\$240 million in credit and US\$60 million in grants, with US\$50 million from the IDA Refugee Support Window, expanding beyond Education and Health to water and Environment and Agriculture (micro-scale irrigation) making the overall funding total of US\$500 million.

The Intergovernmental Fiscal Transfer Reform Programme (IGFT RP) was revised in 2020 to align with the Third National Development Plan (NDP III-2020/21 to 2024/25), and to directly contribute to Four (04) Programmes i.e. Human Capital Development; Public Sector Transformation; Natural Resources, Environment, Climate change, Land and Water Management; and Development Plan Implementation.

The Overall development objective of the UglIFT Programme was to: “Improve the adequacy, equity, and effectiveness of financing and the oversight, management, and delivery of Local Government services in Education, Health, Water and Environment, and Agriculture (micro-scale irrigation), including refugees and their host communities”.

Specifically, the Programme sought to:

- i. Increase the adequacy and predictability of fiscal transfers to Local Governments for service delivery;
- ii. Improve the equity and transparency of allocation mechanisms through the introduction of formula-based transfers;
- iii. Strengthen performance incentives and accountability systems for Local Governments; and
- iv. Expand access to quality education and health infrastructure, particularly in under-served areas.

The UglIFT Programme had four components aimed at strengthening the intergovernmental fiscal transfer system while supporting investments in service delivery infrastructure. These included;

Component 1: Reform of the Intergovernmental Fiscal Transfer System

This supported the design and implementation of a reformed fiscal transfer framework based on objective and transparent allocation criteria. This resulted into introduction of formula-based grants - Revised allocation formulas reflecting population, infrastructure gaps, and service delivery needs.

Component 2: Education Infrastructure Development

This component financed the construction and upgrading of education facilities, particularly government secondary schools in under-served sub-counties. This involved Construction and equipping of new secondary schools - Classrooms, laboratories, administration blocks, sanitation facilities, teachers' houses, furniture and ICT equipment in the different local governments.

Component 3: Health Infrastructure Development

¹ UglIFT Programme provided assets to other national and subnational agencies that were not directly involved in implementation such as KCCA, MODVA, hospitals and health centres across the country

This supported investments in health facilities to improve access to primary health care services at the local level. The major outputs under the component were construction and upgrading of health centers - Staff accommodation, sanitation facilities and provision of medical equipment.

Component 4: Local Government Performance and Institutional Strengthening

This aimed at Strengthening local government capacity in planning, budgeting, procurement, and infrastructure management. Under this component, Annual local government performance assessments have been undertaken across the 176 Local governments, Capacity building and technical support Strengthened monitoring and reporting systems across the Local governments.

The Programme was implemented through a clearly defined results framework that connected actions and incentives across three levels of government to strengthen service delivery outcomes. The programme came to an end in December 2025 and had accomplished the following outputs under the different components;

a) Budget Support

- **Education:** 196 of 259 Seed Schools are complete of which 189 are operational
- **Health:** 354 of 373 health facility upgrades/new constructions (HC II to HC III) are complete
- **Water and Environment:** 758 - piped water systems, 5,398- point water sources, 7,082 water supply systems rehabilitated, 325 designs completed, and 256 sanitation facilities in the targeted service units
- **Agriculture** (Micro-scale Irrigation): Over 6,235 irrigation systems were installed (4,843 hectares under irrigation), 632 irrigation demonstration sites in 135 LGs set up,
- **Refugee intervention:** 51 primary schools and 35 health facilities in refugee hosting districts (RHD) were transitioned and integrated into the LG service
- **Blood banks:** Regional Blood Banks in Arua and Hoima were completed and commissioned while Soroti Regional Blood Bank was rehabilitated

b) Under grant management

Assets for institutional strengthening and retooling including ICT equipment and vehicles. The Ministry of Finance planning and Economic development (MoFPED) through PFM Coordination Unit (RCU) manages the Government of Uganda counterpart funding of the programme to support the grant management component of the UglFT programme. The grant management supports in financing of Central Government actions intended to achieve programme objectives and disbursement linked indicators (DLIs). To this end, MoFPED through RCU supported MDAs to acquire different assets meant to support programme implementation.

1.3 Justification

The UglFT programme came to an end on 31st December 2025. As part of the programme's closure activities, MoFPED, through RCU, commissioned an end-of-programme asset verification exercise to take stock of the assets procured under the programme and to establish where those assets were, how they were being used as part of the processes to hand them over to government for sustainability purposes.

1.4 Objectives of the assignment

The objective of the assignment was to undertake verification and recording of all assets acquired under the UglFT Programme. Specifically, the assignment intended to;

- i. Identify and verify the existence of the assets
- ii. Verify the assets condition and status: specifically, the condition on functionality, usage/performance and location among others
- iii. Assess financial management aspects: residual value of the investments/hardware/tools for purposes of financial reporting for project closure
- iv. List the assets that are obsolete, unserviceable and require disposal
- v. Develop a computerized database of the investment/hardware/tools to facilitate recording of new deployed assets/investments.
- vi. Undertake PFM Assessment on Asset Management practices (including sustainability, Operations and Maintenance) of the UglFT implementing LGs

1.5. Scope of Work

The assignment all institutions at National and local government that directly implemented the UglIFT programme from coordination, support and implementation across the country. At the local government level, the study focused on upgradedimproved health facilities and seed secondary schools only as these had received assets upgraded under the programmes as a result.

Specifically, the assignment involved the following tasks;

- i. Verification of the Asset's Records of targeted ministries departments and agencies and local governments
- ii. Physical and Functional Verification of assests
- iii. Data Consolidation for generation of a single data base of assets provided by the programme
- iv. Generation of an IFMIS ready Asset Register for Integration, and Migration into IFMIS
- v. Review of the UglIFT Asset Management Practices

1.6. Expected deliverables

Key expected outputs of the consultant include:

- (i) Report with the list and current status of assets acquired under the programmes;
- (ii) An automated up-to-date assets data base of UglIFT Investments across MDALGs;
- (iii) Report on the estimated value of assets under the programme as well as operations and maintenance arrangements;
- (iv) IFMS-Ready Asset Register and Data Migration Report
- (v) Report on functionality of assets relating to systems investments;
- (vi) Report on Assessment of Asset Management Practices, Risks and recommendations.

2 Approach and methodology

The verification exercise was conducted using a participatory and consultative process and implemented in three interlinked phases: Preparatory and inception phase, Data collection phase and the report writing phase.

2.1 Preparation:

The Inception phase was completed and the inception report submitted on 18th June 2026 which provided an agreed the scope, approach and work plan for the exercise. The team also undertook a pilot test field study was conducted within the Wakiso District Local Government, with verification carried out at Buloba Health Centre and Sumbwe Seed School which helped in design of data collection tool and the deployment plans

2.2. Data collection

This exercise was undertaken in two phases first at National level and later at the Local government level.

National level: Physical visits to verify assets provided by the programme at the national-level was completed on the 19th of August 2026. This covered 15 MDAs including; Ministry of Works and transport (MoWT), Ministry of Education and Sports (MoES), Ministry of Agriculture Animal Industries and Fisheries (MAAIF), Ministry of Health (MoH), Office of the Prime Minister (OPM), Ministry of Water and Environment (MoWE), Ministry of Gender, Labour and Social Development (MoGLSD), Local Government Finance Commission, National Environment Management Authority (NEMA), Public Procurement and Disposal of Assets Authority (PPDA), Office of the Auditor General (OAG), Ministry of Public Service (MoPs), Ministry of lands housing and Urban Development, Ministry of Local Government (MoLG), and Ministry of Finance, Planning and Economic Development (MoFPED).

Local government level: The local government verification involved national wide coverage of all UgiFT upgrade/constructed health centres, blood banks and seed schools. This involved the training of teams and field visits to the facilities.

Training of field teams: The verification exercise started with a training of the asset verification teams. A total of 85 Research Assistants (RAs) were trained. The training took place from 21st to 23rd August 2026 and physical verification started on the 24th of August 2026 across all the 176 Local governments. During the Asset verification, the RAs visited Seed Schools, Health Centres and Blood banks.

Physical verification: This exercise commenced on the 24th of August 2026 and was completed on 17th September 2026. The local government physical verification involved entry meetings with the LG leadership at the LG headquarters for authorization and review of reports relating to UgiFT assets, key informant interviews with the technical teams especially the Chief Administrative officers (CAOs), finance officers, District health teams and district education officers. Thereafter, the RAs proceeded to the facilities for physical verification of the assets.

At local government level, the programme list held 629 facilities: 371 health centres and 258 seed secondary schools. The list recorded 547 facilities (87.0%) as complete and 82 (13.0%) as ongoing; ongoing works were more common among seed schools (63, or 24.4%) than among health centres (19, or 5.1%).

2.3. Quality assurance

Regional supervisors checked daily field activity and reviewed the completed tools. The central technical team carried out spot checks and helped resolve operational questions. Teams compared institutional asset information with the items and explanations provided during visits, while supervisors referred matters requiring clarification to the team leader and field coordinator.

2.4 Asset categories, condition, use and identification

Asset categories. Each asset is counted once and assigned to one report category. Health centre assets are grouped as clinical equipment, clinical furniture, maternity ward equipment and health centre ICT equipment, and seed school assets as school furniture, school computers and related equipment and school support equipment. Other ICT equipment, other furniture, vehicles and motorcycles, building blocks and other assets complete the categories, which apply to national institutions, blood banks and local governments alike. Appendix B reconciles the report categories with the asset classes used for financial reporting.

Condition and use. Condition and use are reported as recorded for each asset during the verification. A working asset is one recorded as functional and in use. An asset recorded as faulty is reported as not working and not in use. This covers assets that were broken down or damaged as well as assets held in storage, held elsewhere, not yet delivered or awaiting power, installation, completion of buildings or trained users, and the reasons recorded by the teams distinguish between them. Percentages are shares of the assets in each institution group or category.

Identification. The engraving statistics use verified assets as their base: the movable assets verified at each institution. Buildings, structures and land are identified through property and site records, and accessories and consumables were not part of the verification, so both are excluded from this base. An asset is properly engraved when it carries the UglIFT programme marking, including variant spellings of the programme identifier, and not properly engraved when it carries another marking only, such as a school, facility, district or ministry code without the programme identifier. Assets carrying no engraving are reported as not engraved.

2.5 Valuation basis

Recorded values, depreciation and net book values follow the Government of Uganda Asset Accounting Policies and Guidelines 2023. Recognition follows sections 3.2.1 and 3.3.3, and useful lives follow the asset class framework in Annex 1. Depreciation is charged on a straight line basis with nil residual value under sections 5.5 and 5.7, up to 30 September 2026; capital work in progress is not depreciated.

Unit values, useful lives and commencement dates are those held in the UglIFT asset verification records, and any unit value below UGX 10,000 is carried at zero. Net book value is calculated for each asset as its recorded value less accumulated depreciation, with a minimum of zero, before amounts are totalled. Section 4.6 presents the values by institution group and Appendix D gives the detailed schedules.

2.6 Analysis and reporting

This draft report is a result of triangulation of the literature review of the different policy and national documents including asset registers, asset records at local and national level, physical inspection, discussions with facility managers, photographs and the asset counts for each institution. The report is presented indicating findings at National level and local government level as indicated in the different sections below.

2.7. Challenges and Limitations to the assignment

Difficult terrain and poor physical accessibility of facilities: Physical accessibility presented a significant operational challenge especially for facilities located in areas characterised by difficult terrain and limited transport accessibility such as Bwesumbu HC III, Bwesumbu Seed School, Buhuhira and Kabingo in Kasese District. In addition, accessing facilities within the Island was difficult, time consuming and expensive. This led the teams to overshoot the anticipated time for data collection.

High transportation cost: Given the national wide coverage, the rising fuel prices led to high field costs. The field teams spent more money than was anticipated. The cost were extra ordinary higher for island facilities like Kalangala, Buvuma, Mayuge among others. For instance, Kalangala had 3 facilities with long distance on water that required hiring a private boat since it was not a common route to the transporters and outside the ferry schedules. A similar situation was encountered in Buvuma and Namayingo districts.

In Kyotera, Nangoma health centre was not visited. This is because the health centre is closer to Tanzania and the easiest route is via Mutukula which would require the team to have passports. In Buvuma, the facilities in Lwajje and Lubyia were closer to Tanzania and required special boat hire amounting to two million Uganda shillings.

Poor record keeping

In many LGs and facilities, there were no clear records about the assets delivered under UglIFT. The LGs and the facilities had incomplete or missing UglIFT asset registers which delayed data collection. Subsequently, the teams took longer in such facilities identifying the assets as most of these were not engraved with the UglIFT identifiers

while others were not engraved at all. Additionally, the field teams encountered situations where some Assets could not be physically accessed especially for schools since it was holiday time.

Loss of institutional memory: There was loss of institutional memory after the transfer of staff that were present during the delivery of these assets. In addition, there were capacity gaps especially in health centres where the officers on site could not identify the stated assets as indicated on the tool and delivery books. This affected timely progress of the verification

4 Findings

The findings follow the order in which the verification took place. National verification began on 24 July 2026 with the ministries, departments and agencies (MDAs), and section 4.1 presents the national level, including the other national votes and the referral and general hospitals. The blood banks and the local governments were verified from 24 August to 7 September 2026; section 4.2 presents the blood banks and section 4.3 the health centres and seed schools. Sections 4.4 to 4.7 then cover conditions and use, the status of equipment, financial values and service delivery across all institutions.

All findings are reported at national level, and a district is named only to locate an example. Counts are of assets unless facilities are stated. Engraving percentages use verified assets as the base: movable assets, excluding buildings, structures and land. Accessories and consumables were not part of the verification.

4.1 National level: ministries, departments and agencies

National verification covered the 15 MDAs listed for the exercise, 13 of which held UgIFT assets. The Local Government Finance Commission (LGFC) and the Ministry of Public Service (MoPS) received no UgIFT assets; MoPS supported the programme through the recruitment of staff. National institutions together hold 25,627 assets: 16,902 on MDA and other national votes, 8,099 at referral and general hospitals and 626 at the blood banks. The main management questions were whether assets remained in use, could be identified and had clear responsibility for custody and maintenance. Recorded values are summarised in section 4.6, and detailed valuation schedules are provided in Appendix D.

The 16,902 assets on national votes comprise 16,668 at the 13 MDAs and 234 on two other national votes: Kampala Capital City Authority (KCCA), with 51, and the Ministry of Defence and Veteran Affairs (MoDVA), with 183. After the verification records were updated with the IFMIS asset records on 28 September 2026, the MoES holdings include 9,324 Teacher Effectiveness and Learners Assessment (TELA) handsets and 1,001 tablets, bringing the ministry to 10,783 assets, the largest holding of any MDA.

Of the 16,902 assets, 16,882 (99.9%) were working and in use. The other 20 (0.1%) were not working and not in use: 16 at MoWT whose location the ministry was tracing, 3 damaged laptops at OPM, which were the only assets broken down, and 1 boarded off pickup at MoH.

Of the 15,609 verified assets, 4,849 (31.1%) were engraved and 10,760 (68.9%) were not engraved. Properly engraved assets, carrying the UgIFT marking, numbered 4,736 (30.3% of verified assets and 97.7% of those engraved), while 113 (0.7%) were not properly engraved, carrying another marking only: a vehicle registration number (57 assets) or an institution asset code (56). The 9,324 TELA handsets and 1,001 tablets at MoES account for 10,325 of the 10,760 assets not engraved.

Table 5 shows the verified assets, engraved and not engraved, at each institution. Verified assets are movable assets; buildings and land are identified through property and site records. Each engraving should link to the asset number, institution and current custodian.

Table 2: Verified assets engraved and not engraved at national ministries, departments and agencies

Institution	Assets	Verified assets	Engraved	Not engraved	Engraved %
MoFPED	458	358	272	86	76.0%
MoWT	88	72	63	9	87.5%
MoES	10,783	10,783	458	10,325	4.2%
MAAIF	2,045	1,227	1,204	23	98.1%
MoH	264	73	41	32	56.2%

Institution	Assets	Verified assets	Engraved	Not engraved	Engraved %
OPM	10	10	10	0	100.0%
MoWE	2,939	2,782	2,740	42	98.5%
MoGLSD	10	10	8	2	80.0%
NEMA	6	6	1	5	16.7%
PPDA	5	5	5	0	100.0%
OAG	20	20	20	0	100.0%
MoLG	13	13	8	5	61.5%
MoLHUD	27	26	13	13	50.0%
KCCA	51	46	6	40	13.0%
MoDVA	183	178	0	178	0.0%
Total	16,902	15,609	4,849	10,760	31.1%

Verified assets are movable assets; buildings, structures and land are excluded, and accessories and consumables were not part of the verification. Engraved % is the share of verified assets.

Every verified asset was engraved at OPM, PPDA and OAG, and almost all were engraved at MoWE (98.5%) and MAAIF (98.1%). Engraving was lowest on the MoDVA oxygen equipment (0.0%), at MoES (4.2%), where the handsets and tablets were not engraved, and at KCCA (13.0%) and NEMA (16.7%).

Table 6 gives the working, not working, broken down, in use and not in use assets at each institution, with the main reasons assets were not in use. Twelve of the 15 institutions had every asset working and in use.

Table 3: Condition and use of assets at national ministries, departments and agencies

Institution	Assets	Working	Not working	Broken down	In use	Not in use	Main reasons not in use
MoFPED	458	458 (100.0%)	0 (0.0%)	0 (0.0%)	458 (100.0%)	0 (0.0%)	-
MoWT	88	72 (81.8%)	16 (18.2%)	0 (0.0%)	72 (81.8%)	16 (18.2%)	Location being traced by the ministry (16)
MoES	10,783	10,783 (100.0%)	0 (0.0%)	0 (0.0%)	10,783 (100.0%)	0 (0.0%)	-
MAAIF	2,045	2,045 (100.0%)	0 (0.0%)	0 (0.0%)	2,045 (100.0%)	0 (0.0%)	-
MoH	264	263 (99.6%)	1 (0.4%)	0 (0.0%)	263 (99.6%)	1 (0.4%)	Pickup boarded off (1)
OPM	10	7 (70.0%)	3 (30.0%)	3 (30.0%)	7 (70.0%)	3 (30.0%)	Damaged laptops (3)
MoWE	2,939	2,939 (100.0%)	0 (0.0%)	0 (0.0%)	2,939 (100.0%)	0 (0.0%)	-
MoGLSD	10	10 (100.0%)	0 (0.0%)	0 (0.0%)	10 (100.0%)	0 (0.0%)	-
NEMA	6	6 (100.0%)	0 (0.0%)	0 (0.0%)	6 (100.0%)	0 (0.0%)	-
PPDA	5	5 (100.0%)	0 (0.0%)	0 (0.0%)	5 (100.0%)	0 (0.0%)	-
OAG	20	20 (100.0%)	0 (0.0%)	0 (0.0%)	20 (100.0%)	0 (0.0%)	-
MoLG	13	13 (100.0%)	0 (0.0%)	0 (0.0%)	13 (100.0%)	0 (0.0%)	-
MoLHUD	27	27 (100.0%)	0 (0.0%)	0 (0.0%)	27 (100.0%)	0 (0.0%)	-
KCCA	51	51 (100.0%)	0 (0.0%)	0 (0.0%)	51 (100.0%)	0 (0.0%)	-
MoDVA	183	183 (100.0%)	0 (0.0%)	0 (0.0%)	183 (100.0%)	0 (0.0%)	-
Total	16,902	16,882 (99.9%)	20 (0.1%)	3 (0.0%)	16,882 (99.9%)	20 (0.1%)	Location being traced 16; damaged 3; boarded off 1

Percentages are of the assets at each institution. Broken down assets are included in the not working count.

The national votes hold 1,074 computers (424 desktops and 650 laptops), together with 4,209 tablets and 9,364 phones, most of them TELA handsets. Of the 1,074 computers, 1,059 (98.6%) were working and in use and 15 (1.4%) were not: 12 MoWT desktops whose location was being traced and 3 damaged OPM laptops, the only computers broken down (0.3%).

A total of 1,037 computers (96.6%) were engraved and 37 (3.4%) were not engraved; 1,024 (95.3%) carried the UgIFT marking. Table 7 gives these shares for each MDA.

Table 4: Computers at national ministries, departments and agencies: condition, engraving and use

Institution	Computers	Working %	Not working %	Engraved %	Not engraved %	In use %	Not in use %
MoFPED	113	100.0%	0.0%	91.2%	8.8%	100.0%	0.0%
MoWT	33	63.6%	36.4%	84.8%	15.2%	63.6%	36.4%
MoES	456	100.0%	0.0%	100.0%	0.0%	100.0%	0.0%
MAAIF	211	100.0%	0.0%	100.0%	0.0%	100.0%	0.0%
MoH	26	100.0%	0.0%	65.4%	34.6%	100.0%	0.0%
OPM	10	70.0%	30.0%	100.0%	0.0%	70.0%	30.0%
MoWE	188	100.0%	0.0%	96.8%	3.2%	100.0%	0.0%
MoGLSD	8	100.0%	0.0%	100.0%	0.0%	100.0%	0.0%
NEMA	4	100.0%	0.0%	0.0%	100.0%	100.0%	0.0%
PPDA	3	100.0%	0.0%	100.0%	0.0%	100.0%	0.0%
OAG	16	100.0%	0.0%	100.0%	0.0%	100.0%	0.0%
MoLG	6	100.0%	0.0%	50.0%	50.0%	100.0%	0.0%
Total	1,074	98.6%	1.4%	96.6%	3.4%	98.6%	1.4%

Computers are desktops and laptops; tablets, phones and peripherals are excluded. MoLHUD, KCCA and MoDVA held no computers. The only computers broken down were 3 laptops at OPM.

Accounting Officers should complete the outstanding engraving, keep custody and location details current, and include serviceable equipment in routine maintenance. Damaged items require technical assessment and a decision on repair or disposal.

4.1.1 Ministry of Finance, Planning and Economic Development

MoFPED held 458 assets: 217 ICT items, 122 other assets, 99 furniture and fittings and 20 transport assets. The main items were office chairs and desks, desktop computers, tablets and 20 Toyota Hilux double cabin pickups. All 458 assets (100.0%) were working and in use, and none was broken down. Of the 358 verified assets, 272 (76.0%) were engraved and 86 (24.0%) were not engraved; 252 (70.4%) were properly engraved with the UgIFT marking, and 20 (5.6%), the pickups, were not properly engraved, carrying their registration numbers only. The recorded value of the ministry's UgIFT assets is UGX 6,152,854,000.

The ministry held 113 computers (73 desktops and 40 laptops), all working and in use; 103 (91.2%) were engraved and 10 (8.8%) were not engraved. Its 17 tablets and 14 office desk phones were all working and engraved. The ministry keeps a UgIFT asset register and the consolidated register for all MDAs that received UgIFT assets.

Expected: Staff computers should support their workload, and portable equipment should remain identifiable and accountable. Found: The computers were working, but users reported that some keyboards and power backup units had failed and that some older computers were freezing. Laptop losses were supported by police letters. The team also reported difficulty obtaining some laptops for engraving.

Gap: Equipment reliability, follow-up of lost assets and completion of identification each required a specific management response. Recommended action: The ministry should assess the failed accessories and freezing computers, follow up the reported laptop losses, and arrange a supervised exercise to engrave all remaining portable equipment.

Expected: Furniture should remain assigned to a location and custodian when offices move. Found: When programme staff moved to premises already furnished, their earlier furniture was left in the old building. Some remained in store, while staff said other items had gone to different offices.

Gap: The move had split the furniture between storage and other offices, requiring confirmation of its present custody and use. Recommended action: The ministry should inspect the old store and recipient offices, confirm the condition and custodian of each item, and approve reuse or other appropriate treatment of furniture no longer required.

4.1.2 Ministry of Works and Transport

MoWT held 88 assets: 63 ICT items, 24 other assets and 1 transport asset, a Toyota Hilux pickup. The ICT items were mainly desktop computers, monitors and uninterruptible power supply (UPS) units. Of the 88 assets, 72 (81.8%) were working and in use and 16 (18.2%) were not working and not in use; none was broken down. Of the 72 verified assets, 63 (87.5%) were engraved, 62 (86.1%) of them with the UgIFT marking, and 9 (12.5%) were not engraved. The recorded value is UGX 455,932,376.

At the time of the visit, the ministry was tracing the location of the 16 assets not in use, 12 Dell OptiPlex desktop computers and 4 UPS units. None of them was reported damaged. Of the ministry's 33 computers (28 desktops and 5 laptops), 21 (63.6%) were working and in use and the 12 desktops being traced made up the other 36.4%; 28 (84.8%) were engraved and 5 (15.2%) were not engraved.

Repairs and servicing of the Toyota Hilux pickup were handled by MoFPED. The custody and maintenance arrangements should remain clear during handover.

Expected: Installed office and conferencing equipment should support the secretariat and carry a traceable asset identity. Found: The secretariat reported that the installed photocopiers supported its daily work. The colour photocopier, the video conferencing system and five Lenovo desktop computers were working but not engraved.

Gap: Working equipment, including an operational conferencing system, still required clear identification and custody, and the location of 16 assets was being traced. Recommended action: The ministry should engrave the colour photocopier and desktop computers, identify the conferencing system and its components, assign a custodian, and apply a suitable durable identifier without damaging the equipment. It should also complete the tracing of the 12 desktop computers and 4 UPS units and confirm their custodians.

4.1.3 Ministry of Education and Sports

MoES held 10,783 assets, all ICT equipment: 9,324 TELA handsets, 1,001 tablets (976 of them inspection tablets), 456 laptops, a photocopier and a printer. TELA is the system, financed by UgIFT, that the ministry uses to monitor attendance and performance in schools; the handsets and inspection tablets are deployed in local governments and remain MoES assets. The recorded value is UGX 14,925,128,359, the highest of any MDA.

All 10,783 assets (100.0%) were working and in use. Of the verified assets, 458 (4.2%) were engraved, all with the UgIFT marking, and 10,325 (95.8%) were not engraved: none of the handsets or tablets carries an engraving. All 456 laptops were working, in use and properly engraved.

Recommended action: The ministry should link each handset and tablet to its serial number and to the school or office that holds it, and apply a durable identifier where the device allows.

4.1.4 Ministry of Agriculture, Animal Industry and Fisheries

MAAIF held 2,045 assets: 1,206 ICT items, 837 other assets and 2 transport assets. The ICT items were mainly 819 tablets, 211 computers (162 desktops and 49 laptops), 149 monitors and 15 printers. All 2,045 assets (100.0%) were working and in use. Of the 1,227 verified assets, 1,204 (98.1%) were engraved, 1,200 (97.8%) with the UgIFT marking, and 23 (1.9%) were not engraved, among them two drones, a handheld global positioning system (GPS) unit and a projector. The recorded value is UGX 2,332,681,629.

All 211 computers and 819 tablets were working, in use and properly engraved. The ministry had working laptops and printers carrying the UgIFT engraving. Keeping those engravings linked to the equipment and its custodian will support continued accountability after programme closure. Routine condition checks should identify new faults and keep usable equipment in service.

4.1.5 Ministry of Health

MoH held 264 assets: 200 other assets, 39 ICT items and 25 transport assets. Of these, 263 (99.6%) were working and in use; one double cabin pickup (0.4%) had been boarded off and was not in use, and none was broken down. Of the 73 verified assets, 41 (56.2%) were engraved and 32 (43.8%) were not engraved; 14 (19.2%) were properly engraved with the UgIFT marking and 27 (37.0%) were not properly engraved, carrying another marking only: a vehicle registration number (16) or an office asset code (11). The recorded value is UGX 1,216,859,097.

The ministry's 26 computers (2 desktops and 24 laptops) were all working and in use; 17 (65.4%) were engraved and 9 (34.6%) were not engraved.

Expected: Office equipment in use should be identifiable by a durable engraving. Found: Two heavy duty printers, one at the Industrial Area engineering office and one at headquarters, were in use and in good condition but not engraved. Nine laptops were also not engraved.

Gap: Working equipment at separate offices still lacked the engraving needed for straightforward physical identification. Recommended action: The ministry should engrave these items, link the engravings to their serial numbers and office locations, and obtain custody confirmation from the receiving units.

4.1.6 Office of the Prime Minister

OPM held 10 ICT items, all HP Envy laptops. Seven (70.0%) were working and in use, and three (30.0%) were damaged, broken down and out of use. All 10 laptops (100.0%) were properly engraved with the UgIFT marking. The recorded value is UGX 53,535,300.

The office should assess repair needs for the three damaged laptops and return serviceable equipment to use.

Expected: Computers should have enough capacity for the work assigned to their users. Found: Users reported that the capacity of the HP Envy i3 laptops was below the volume of work handled, such as the performance assessment of local governments, although the machines were described as being in fair condition.

Gap: A usable laptop could still be poorly matched to the workload of its user. Recommended action: The office should assess the requirements of the affected users and decide whether upgrading, reallocating or replacing the laptops would provide suitable capacity.

4.1.7 Ministry of Water and Environment

MoWE held 2,939 assets: 2,767 ICT items and 172 other assets. The main items were 2,368 tablets, 2,344 of them Euron tablets, 188 computers (157 Dell OptiPlex all in one desktops and 31 laptops) with their keyboards and UPS units, and 16 real time kinematic GPS machines. All 2,939 assets (100.0%) were working and in use. Of the 2,782 verified assets, 2,740 (98.5%) were engraved, 2,707 (97.3%) with the UgIFT marking, and 42 (1.5%) were not engraved. The recorded value is UGX 5,000,313,297.

All 188 computers were working and in use; 182 (96.8%) were engraved and 6 (3.2%) were not engraved.

Expected: Portable tablets should carry an asset identifier and have an assigned custodian. Found: Ten Apple tablets were not engraved.

Gap: Portable equipment required an identification method that would allow each unit to be traced to its user and location. Recommended action: The ministry should apply suitable durable identifiers, link them to serial numbers, and confirm custody before the next physical check.

4.1.8 Ministry of Gender, Labour and Social Development

MoGLSD held 10 ICT items: 8 laptops and 2 tablets. All 10 (100.0%) were working and in use. Eight (80.0%) were properly engraved with the UglIFT marking and 2 (20.0%) were not engraved. The recorded value is UGX 46,180,000.

Laptops serving Finance and Administration were working and engraved. Two tablets, one for Finance and Administration and the other for Youth and Children Affairs, were working but not engraved. The ministry should engrave the tablets and link their identifiers to the units and officers responsible for them.

4.1.9 National Environment Management Authority

NEMA held 6 ICT items: 4 laptops, a printer and a heavy duty photocopier. All 6 (100.0%) were working and in use. One (16.7%) was engraved and 5 (83.3%) were not engraved, including all 4 laptops. The recorded value is UGX 46,824,409.

Expected: Computers and shared office equipment should remain identifiable wherever they are used. Found: Four Lenovo laptops serving the executive office and environmental audit, together with a heavy duty printer, were working but not engraved. The authority was awaiting a MoFPED team to engrave them.

Gap: The equipment could support work, but lacked a durable identifying mark. Recommended action: The authority should engrave the five items, record their serial numbers and custodians, and include them in regular physical checks.

4.1.10 Public Procurement and Disposal of Public Assets Authority

PPDA held 5 ICT items: 3 Lenovo ThinkPad laptops, a Samsung Galaxy tablet and an HP printer. All 5 (100.0%) were working, in use and properly engraved with the UglIFT marking. The recorded value is UGX 30,153,500.

The laptops, tablet and printer were assigned to the legal unit and the strategy and planning unit. The authority should keep the engravings linked to current custodians and update custody whenever equipment moves between units.

4.1.11 Office of the Auditor General

OAG held 20 assets: 18 ICT items (16 laptops and 2 printers) and 2 pickup vehicles. All 20 (100.0%) were working, in use and engraved: 6 (30.0%) were properly engraved with the UglIFT marking and 14 (70.0%) were not properly engraved, carrying only the office's own asset code (12) or a vehicle registration number (2). Of the 16 laptops, 6 (37.5%) carried the UglIFT marking and 10 (62.5%) the office's asset code. The recorded value is UGX 388,773,680.

The two pickups had changed registration numbers. The office should retain the link between the earlier and current registrations, the chassis numbers and the assigned custodians so that each vehicle remains traceable.

4.1.12 Ministry of Local Government

MoLG held 13 assets: 12 ICT items and 1 transport asset, a pickup. The ICT items were 6 computers (2 desktops and 4 laptops), 4 computer peripherals, a copier and a heavy duty photocopier. All 13 (100.0%) were working

and in use. Eight (61.5%) were engraved, 7 (53.8%) with the UgIFT marking, and 5 (38.5%) were not engraved; of the 6 computers, 3 (50.0%) were engraved and 3 (50.0%) were not. The ministry keeps a well organised UgIFT asset register. The recorded value is UGX 343,320,450.

The District Administration unit had a working pickup, photocopier and computer equipment. Two laptops and a desktop set, including its keyboard and mouse, were not engraved. The ministry should engrave this equipment and confirm its location and custodian while keeping the working assets in service.

4.1.13 Ministry of Lands, Housing and Urban Development

MoLHUD held 27 assets: 25 Honda motorcycles and 2 other assets. All 27 (100.0%) were working and in use. Of the 26 verified assets, 13 (50.0%) were not properly engraved, carrying only their registration numbers, and 13 (50.0%) were not engraved; none carried the UgIFT marking.

The ministry received survey equipment and motorcycles that it gave out to local governments, and it provided a list of the beneficiaries. The ministry should keep the beneficiary list current and apply the UgIFT engraving so that each motorcycle can be traced to the receiving local government.

4.1.14 Other national votes

Two other national votes hold UgIFT assets. KCCA held 51 assets: 25 mobile phones, an office desk phone, 5 monitors and 5 keyboards, together with 10 oxygen cylinders and 5 oxygen regulators at Kisenyi Health Centre IV. All 51 (100.0%) were working and in use. Of the 46 verified assets, 6 (13.0%) were engraved with the UgIFT marking and 40 (87.0%) were not engraved: the 25 mobile phones and the oxygen cylinders and regulators. The recorded value is UGX 54,024,515.

MoDVA held 183 assets issued under two Ministry of Health distributions: 131 oxygen cylinders, 41 oxygen regulators and 11 pressure swing adsorption (PSA) oxygen plant components, namely oxygen generators, air compressors, dryers, air and oxygen tanks and a medical air buffer tank. All 183 (100.0%) were working and in use, and none of the 178 verified assets was engraved. The recorded value is UGX 91,162,979.

Custody, identification and maintenance responsibilities should remain with the institution that holds and uses each asset. Both votes should engrave the phones and oxygen equipment and confirm the custodian of each item.

4.1.15 Referral and general hospitals

The UgIFT asset verification records hold 8,099 assets at 68 hospitals: 4 national referral hospitals, 17 regional referral hospitals and 47 general hospitals. The assets were issued through programme equipment distributions: oxygen cylinders and regulators (4,730 assets), PSA oxygen plant components (1,650), intensive care unit equipment (1,394), medical equipment under the Uganda Reproductive, Maternal and Child Health Services Improvement Project (287), X-ray machines (19), computed tomography scanners (14) and other oxygen plant items (5). Medical and laboratory equipment makes up 7,230 of the 8,099 assets.

All 8,099 hospital assets (100.0%) were working and in use, and none was broken down. None of the 7,745 verified assets was engraved (0.0%). The recorded value is UGX 26,080,242,410, of which UGX 24,338,709,624 is at the regional referral hospitals, mainly in intensive care unit equipment. Table 8 summarises the holdings by type of hospital.

Table 5: Assets at referral and general hospitals by type of hospital

Hospital type	Hospitals	Assets	Working and in use	Verified assets	Engraved	Recorded value UGX
National referral hospitals	4	905	905 (100.0%)	888	0 (0.0%)	402,916,589
Regional referral hospitals	17	4,311	4,311 (100.0%)	4,108	0 (0.0%)	24,338,709,624
General hospitals	47	2,883	2,883 (100.0%)	2,749	0 (0.0%)	1,338,616,197
Total	68	8,099	8,099 (100.0%)	7,745	0 (0.0%)	26,080,242,410

Engraved is the share of verified assets. Recorded value is the cost in the UgIFT asset verification records.

The largest holdings were at Moroto Regional Referral Hospital (368 assets), Masaka Regional Referral Hospital (363) and Kabale Regional Referral Hospital (347); among general hospitals, Mityana General Hospital held the most (199). Hospital managements should engrave the equipment, link each engraving to the serial number and the unit that holds it, and keep custody and maintenance responsibilities with the unit that uses each asset.

4.2 Blood banks

UgIFT financed the construction of the Arua and Hoima regional blood banks, which were completed and commissioned, and the rehabilitation of Soroti Regional Blood Bank. The three banks operate under Uganda Blood Transfusion Services (UBTS) and were verified during the local government fieldwork from 24 August to 7 September 2026. They are reported here as a separate group.

The UgIFT asset verification records hold 626 blood bank assets. The field returns for the three banks give the verified position of each bank: Arua 179 assets, Hoima 59 and Soroti 115, a total of 353. The UBTS vote records 273 assets for the Arua (161) and Hoima (112) banks, drawn from the supplier equipment inventories for the two banks.

Of the 626 assets, 602 (96.2%) were working and in use and 24 (3.8%) were not working and not in use, all on the Arua field return: 6 broken blood pressure machines (1.0% of blood bank assets) and 18 items that had been used up. Of the 605 verified assets, 43 (7.1%) were engraved and 562 (92.9%) were not engraved. All 43 engraved assets were at Arua: 26 (4.3%) were properly engraved with the UgIFT marking and 17 (2.8%) were not properly engraved, carrying another marking only. The recorded value is UGX 1,451,584,715, with a net book value of UGX 937,479,171.

Across the three field returns, 329 of the 353 assets (93.2%) were working and in use, and 43 of the 341 verified assets (12.6%) were engraved. Table 9 gives the position at each bank.

Table 6: Assets at the regional blood banks: condition, use, engraving and recorded value

Blood bank	Assets	Working	Not working	In use	Verified assets	Engraved	Not engraved	Recorded value UGX
Arua Regional Blood Bank, field return	179	155 (86.6%)	24 (13.4%)	155 (86.6%)	168	43 (25.6%)	125 (74.4%)	1,045,918,115
Hoima Regional Blood Bank, field return	59	59 (100.0%)	0 (0.0%)	59 (100.0%)	58	0 (0.0%)	58 (100.0%)	266,361,213
Soroti Regional Blood Bank, field return	115	115 (100.0%)	0 (0.0%)	115 (100.0%)	115	0 (0.0%)	115 (100.0%)	29,317,538
Arua Regional Blood Bank, UBTS vote	161	161 (100.0%)	0 (0.0%)	161 (100.0%)	152	0 (0.0%)	152 (100.0%)	86,697,863
Hoima Regional Blood Bank, UBTS vote	112	112 (100.0%)	0 (0.0%)	112 (100.0%)	112	0 (0.0%)	112 (100.0%)	23,289,986
Total	626	602 (96.2%)	24 (3.8%)	602 (96.2%)	605	43 (7.1%)	562 (92.9%)	1,451,584,715

Field return rows give the verified position of each bank; UBTS vote rows are the assets recorded for the Arua and Hoima banks on the UBTS vote. Working and in use are percentages of assets; engraved and not engraved are percentages of verified assets. The finer condition codes on the Hoima return are described in section 4.2.2.

4.2.1 Arua Regional Blood Bank

The Arua field return lists 179 assets: 61 medical and laboratory items, 51 items of furniture and fittings, 19 ICT items, 3 vehicles and 45 other assets. The infrastructure found comprised a self-contained flat with a donor room and a board room, a block with the cold room and a storage room, a residential house for medical staff, and power supply works, including a 1,000 kVA ground mounted transformer, a 33 kV ring main unit and 230 metres of overhead line, all in good condition and working. The bank keeps a UgIFT asset register specific to the programme assets.

Of the 179 assets, 155 (86.6%) were working and in use. The 24 not in use were six blood pressure machines, four manual and two digital, that were broken (3.4%), and 18 items that had been used up, among them ten thermometers for monitoring blood in transport and storage and five vacuum flasks. The four stationary and eight mobile donor couches, the laboratory equipment (refrigerators, freezers, centrifuges, cell washer, analysers, incubator and microscope) and three station wagons were in good condition and in use.

Of the 168 verified assets, 43 (25.6%) were engraved and 125 (74.4%) were not engraved. The 26 properly engraved assets (15.5%) carry the UgIFT marking and include donor couches, filing cabinets, office chairs and tables, the reception table, UPS units and the washing machine. The 17 not properly engraved assets (10.1%) carry UBTS equipment codes, mainly on laboratory equipment and desktop computers. The recorded value of the field return assets is UGX 1,045,918,115. Figures 1 to 6 show the completed building, donor couches, the markings on two uninterruptible power supplies, a blood bank refrigerator, a platelet agitator and a chest freezer.

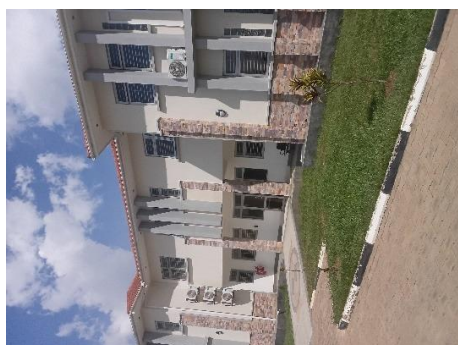


Figure 1: Completed blood bank building at Arua Regional Blood Bank, Arua City (West Nile)



Figure 2: Donor couches in the donor room at Arua Regional Blood Bank, Arua City (West Nile)



Figure 3: Markings PEP II/UBTS/COMP/11/016 and UBTS/UGIFT/ARBB/UPS/001 on uninterruptible power supplies at Arua Regional Blood Bank, Arua City (West Nile)



Figure 4: Blood bank refrigerator at Arua Regional Blood Bank, Arua City (West Nile)



Figure 5: Platelet agitator at Arua Regional Blood Bank, Arua City (West Nile)



Figure 6: Chest freezer at Arua Regional Blood Bank, Arua City (West Nile)

The senior laboratory technician reported that the blood bank had benefited to a large extent from the programme. The challenges raised were few medical personnel, limited care of the facility, the lack of a borehole and too few vehicles when other facilities need blood urgently. The bank recommended recruiting more medical personnel, providing a reliable water source and improving the murram access road, which carries soil into the premises during the rains.

The UBTS vote records 161 assets for the Arua bank, mainly laboratory equipment such as blood bank refrigerators and freezers, plasma blast freezers, centrifuges, blood collection balances and donor couches, with desktop and laptop computers and air conditioners. All 161 are recorded as working and in use, none of the 152 verified assets is engraved, and their recorded value is UGX 86,697,863.

4.2.2 Hoima Regional Blood Bank

The Hoima field return lists 59 assets: 38 medical and laboratory items, 2 items of furniture and fittings, 1 structure and 18 other assets, including office and boardroom furniture, fire extinguishers, storage cabins and a heavy duty generator. All 59 assets (100.0%) are recorded as working and in use, and none of the 58 verified assets was engraved. The recorded value of the field return assets is UGX 266,361,213. Figures 7 to 12 show the donor room, the mark UBTS/UGIFT/VCH/001 on one item, a blood collection balance, a benchtop centrifuge, a fire extinguisher and a generator.



Figure 7: Donor couches in the donor room at Hoima Regional Blood Bank, Hoima City (Bunyoro)



Figure 8: Engraving reading UBTS/UGIFT/VCH/001 on equipment at Hoima Regional Blood Bank, Hoima City (Bunyoro)



Figure 9: Blood collection balance at Hoima Regional Blood Bank, Hoima City (Bunyoro)



Figure 10: Benchtop centrifuge at Hoima Regional Blood Bank, Hoima City (Bunyoro)



Figure 11: Water fire extinguisher at Hoima Regional Blood Bank, Hoima City (Bunyoro)



Figure 12: Generator in an outdoor enclosure at Hoima Regional Blood Bank, Hoima City (Bunyoro)

The condition codes on the Hoima return describe the 52 equipment lines in more detail. Forty were good and in use; five were in good condition but not yet in use (a constant temperature incubator, a table top autoclave, a biosafety cabinet, a plasma blast freezer and a benchtop centrifuge); five were in use but needed repair (a benchtop centrifuge, two benchtop tube sealers and two double pan weighing scales); and two plasma baths were coded as not for blood bank use. The cell washer and plasma thawing bath carried the same remark. Fifteen equipment items were held in the blood bank stores.

Recommended action: The bank should repair the five items that need repair, bring the equipment held in the stores into service or reallocate it, and engrave the verified assets.

The UBTS vote records 112 assets for the Hoima bank, among them blood collection balances, donor couches, benchtop tube sealers, haematology analysers, plasma blast freezers, preparative centrifuges and blood bank refrigerators. All 112 are recorded as working and in use, none is engraved, and their recorded value is UGX 23,289,986.

4.2.3 Soroti Regional Blood Bank

The Soroti field return lists 115 assets in 32 equipment lines from the medical equipment supplied to the bank: 69 medical and laboratory items, 8 ICT items, 4 items of furniture and fittings and 34 other assets. The main items

were donor couches, digital blood pressure monitors, spring balances, cool boxes, manual plasma extractors and bio mixers. All 115 assets (100.0%) were in use and in good condition. The recorded value is UGX 29,317,538.

The bank keeps a record of all assets provided under UgIFT and records functionality and breakdowns through incident reports. Maintenance is provided through an external service arrangement, under which no maintenance had yet been carried out at the time of the visit.

The bank reported that the programme provided accommodation for critical staff and ramps for persons with disabilities. The challenges raised were insecurity, leaking staff quarters, a shallow well, too few security lights, too few vehicles for blood collection, and a lack of computers and air conditioners. The bank recommended installing surveillance cameras, building a perimeter wall, repairing the shallow well or drilling a borehole, and providing vehicles for blood collection and more computers.

4.3 Local governments: health centres and seed schools

Local government verification began on 24 August 2026 and covered the 629 facilities on the programme list, the health centres and seed schools planned before the exercise started: 371 health centres and 258 seed schools (section 2.2). Follow-up established which facilities retained their original names, which had replacements or relocated assets, and which listed institutions had not received programme support. These distinctions matter because a name on the list does not, by itself, demonstrate that the intended facility and its assets are available for service.

The findings are reported at national level. Section 4.3.1 shows how many programme-list facilities were verified, completed and providing services; Section 4.3.2 sets out the inconsistencies between the programme list and the facilities found; and Section 4.3.3 presents the assets verified at health centres and seed schools.

4.3.1 Facilities verified, completed and providing services


Of the 629 facilities on the programme list, teams verified 590 (93.8%) on the ground as UgIFT facilities: 347 health centres (93.5%) and 243 seed schools (94.2%). The verified count includes 29 facilities verified under their operating name and three verified through the facility that replaced them. The other 39 facilities (6.2%) were accounted for through reconciliation: 18 were not UgIFT facilities in practice, the UgIFT assets of three had been relocated to another facility, two are counted once under another programme-list entry, and 16 were accounted for through documented follow-up. Every programme-list facility was therefore accounted for through verification or reconciliation. Table 10 and Figure 13 summarise the position.

Table 7: Programme-list facilities verified, completed and providing services

Measure	Health centres	Seed schools	Total
Programme list	371	258	629
Verified	347 (93.5%)	243 (94.2%)	590 (93.8%)
Works completed	320 (92.2%)	155 (63.8%)	475 (80.5%)
Works not completed	27 (7.8%)	88 (36.2%)	115 (19.5%)
Providing services	327 (94.2%)	193 (79.4%)	520 (88.1%)
Not yet providing services	3 (0.9%)	21 (8.6%)	24 (4.1%)
Accounted for through reconciliation	24 (6.5%)	15 (5.8%)	39 (6.2%)

Counts are facilities. Verified and accounted for through reconciliation are percentages of the programme list; the other percentages are of verified facilities.

A third of verified seed schools had works outstanding

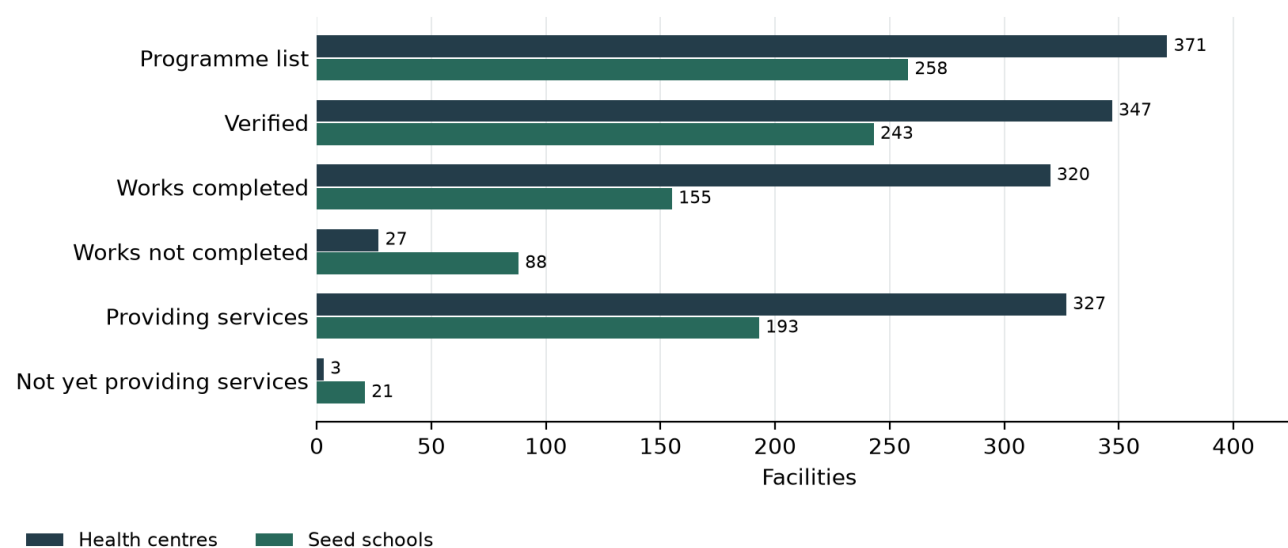

Source: UgIFT programme list, field returns and verification records.

Figure 13: A third of verified seed schools had works outstanding

Works were complete at 475 of the verified facilities (80.5%): 320 health centres (92.2%) and 155 seed schools (63.8%). Works were not complete at 115 (19.5%): 27 health centres (7.8%) and 88 seed schools (36.2%). For 86 of these, the field returns or the building entries in the verification records confirmed that works were outstanding; the other 29 were recorded as ongoing on the programme list. In the field, 44 facilities recorded as complete on the programme list had works outstanding, for example Kaptum and Kitawoi seed schools in Kween, while four recorded as ongoing were found complete.

At 45 of the 86 facilities, main blocks such as classrooms, laboratories, libraries, ICT blocks or maternity wards were still under construction. At 16, only ancillary structures such as staff houses, latrines, kitchens, placenta pits or incinerators remained. At nine, the contractor had not yet handed the works over, and at the other 16 the works were reported as still under construction or incomplete.

At the time of the visits, 520 verified facilities (88.1%) were providing services: 327 health centres (94.2%) and 193 seed schools (79.4%). They include 63 facilities where some works were still outstanding. Twenty-four verified facilities (4.1%) were not yet providing services: three health centres (0.9%) and 21 seed schools (8.6%). Most were schools still under construction or not yet handed over by the contractor:

- **Health centres (3):** Bukibologoto Health Centre III (Bulambuli), Kaptum Health Centre III (Kween) and Amanyiri Health Centre III (Yumbe).
- **Seed schools (21):** Kotomor and Omiya Pacwa (Agago), Akwon (Amolatar), Amuru Town (Amuru), Bushiribo (Bududa), Senendet (Bukwo), Burondo (Bundibugyo), Muhula (Butaleja), St Luke Kibibi (Butambala), Sidok (Kaabong), Rengen (Kotido), Kaptum and Moyok (Kween), Padibe (Lamwo), Butta (Manafwa), Moruita (Nakapiripirit), Iriiri and Lopei (Napak), Got Apwoyo (Nwoya), Okum (Otuke) and Aleka (Oyam).

All three health centres and 19 of the 21 schools had works outstanding. At St Luke Kibibi the main structures were complete and the school awaited formal commissioning and handover, and Lopei was complete, handed over and due to open the following year. Several of these facilities kept their assets in store pending completion and handover of the works: the UgIFT equipment for Kaptum Health Centre III was packed in the facility store awaiting completion of the maternity ward, the assets of Omiya Pacwa and Padibe seed schools were held at the district stores, and most of the equipment for Amanyiri Health Centre III was held at the Yumbe district stores.

Table 11 sets out five facilities where completion or preparation for use was still needed, with the gap and the action recommended for each.

Table 8: Facilities requiring completion or preparation for use

Location	Expected position and field finding	Gap or service implication	Recommended action
Got Apwoyo Seed Secondary School, Nwoya	Expected: Got Apwoyo was intended to provide secondary education with completed buildings and installed ICT equipment. Found: The team found construction continuing and the school uncommissioned. Its ICT package remained at Nwoya District headquarters, while delivered furniture and structures had not been brought into use.	The assets were not yet supporting teaching at the intended school, and custody was divided between the district and the site.	Nwoya District and the Ministry of Education should set a completion and handover plan, check the stored equipment, and arrange installation, testing and signed transfer when the school is ready.
Bukibologoto Health Centre, Bulambuli	Expected: Bukibologoto was listed as complete and was intended to provide care from the constructed health facility. Found: The team found that mudslides had damaged the works before completion. A corner was undermined and a wall cracked. Care was being provided at Simu subcounty offices, with equipment held in district stores.	The planned facility was unavailable for its intended use, and the temporary service and storage arrangements needed a lasting solution.	Bulambuli District and the Ministry of Health should obtain an engineering assessment, decide on repair or relocation, inventory the equipment and provide for continuing care.
Kyangwali Seed Secondary School, Kikuube	Expected: Kyangwali school needed completed works, electricity, security and handover to use its assets fully. Found: The team recorded continuing construction. The school reported a lack of electricity and an incomplete perimeter fence, and the facility had not been handed over.	Finishing the buildings alone would not make the school ready: power, security and responsibility for the assets also remained unresolved.	Kikuube District, the Ministry of Education and the contractor should close these requirements through one readiness plan, followed by joint testing and handover. The plan should name who will operate, safeguard and maintain the assets.
Sidok Seed Secondary School, Kaabong	Expected: Sidok school needed completed buildings and checked equipment before the investment could support full operations. Found: The team found blocks, a kitchen and toilets under construction, with termite workings on the plaster of two blocks. The school consignment remained unopened and its contents had not been counted.	Unfinished works and equipment still to be opened and checked kept the school from being ready for use.	Kaabong District should secure completion and treatment of the affected works, then arrange a witnessed opening, count and condition check of the equipment. Accepted items should be recorded, assigned to custodians and issued for use.
Buwagogo Seed Secondary School, Manafwa	Expected: Buwagogo school was intended to use its supplied ICT equipment for teaching. Found: The team found the March 2024 ICT consignment still boxed in the store, with contractor installation pending and commissioning delayed.	Delivery had not translated into operational ICT capacity. Equipment continued to require secure custody while installation remained outstanding.	Manafwa District and the Ministry of Education should agree an installation and commissioning date with the contractor, reconcile the stored equipment against delivery records and test it before acceptance. The handover should assign responsibility for operation, maintenance and reporting of faults.

The photographs that follow record works still in progress at the time of the visits. Figures 14 to 20 show unfinished school blocks, latrines and building works at seed schools, including Got Apwoyo (Figure 14) and Sidok (Figures 15 and 16). Figures 21 to 27 show laboratory, library and ICT buildings awaiting completion or equipment at a health centre and at seed schools, among them the ICT laboratory at Kitawoi (Figure 25) and the empty computer laboratory at Kaptum Seed Secondary School (Figure 27).



Figure 14: Unfinished school block at Got Apwoyo Seed Secondary School, Nwoya District (Acholi)



Figure 15: Unfinished classroom block at Sidok Seed Secondary School, Kaabong District (Karamoja)



Figure 16: Latrine block under construction at Sidok Seed Secondary School, Kaabong District (Karamoja)



Figure 17: Building works and construction materials at Ndhew Seed Secondary School, Nebbi District (West Nile)



Figure 18: School block awaiting completion at Butungama Seed Secondary School, Ntoroko District (Tooro)



Figure 19: Building works at a seed secondary school, Kiboga District (Buganda)



Figure 20: Classroom block with earthworks in the foreground at Kihungya Seed Secondary School, Buliisa District (Bunyoro)



Figure 21: Unfinished laboratory building at a health centre, Sironko District (Bugisu)



Figure 22: Biology laboratory under construction at a seed secondary school, Buliisa District (Bunyoro)



Figure 23: Unfinished laboratory interior at Kihungya Seed Secondary School, Buliisa District (Bunyoro)



Figure 24: Library interior under construction at Kihungya Seed Secondary School, Buliisa District (Bunyoro)



Figure 25: ICT laboratory interior under construction at Kitawoi Seed Secondary School, Kween District (Sebei)



Figure 26: Laboratory benches with cupboard doors not yet fitted, in a science laboratory block recorded as under construction, at King Solomon Seed Secondary School, Kagadi District (Bunyoro)



Figure 27: Empty computer laboratory at Kaptum Seed Secondary School, Kween District (Sebei), where the buildings had not been handed over and no ICT equipment had been received

4.3.2 Inconsistencies

Reconciliation of the programme list against the facilities found identified 55 entries (8.7% of the programme list) in six groups: 10 that do not exist or were not constructed under the programme, four replaced by another facility, 30 operating under another name, three that are not UgIFT beneficiaries, three whose UgIFT assets were relocated to another facility and five that exist with no UgIFT assets. Table 12 names the facilities in each group by their programme-list name and district.

The 55 entries are part of the 629 programme-list facilities, and 32 of them were verified under their operating or replacing name. Identity corrections should be settled alongside decisions on incomplete works, custody, handover and operational readiness, so that the programme account reflects where services and assets are located. Appendix F gives the outcome for each entry.

Table 9: Inconsistencies between the programme list and the facilities found

Outcome	Health centres	Seed schools	Total (% of 629)	Facilities (programme-list name and district: operating or receiving name)
Does not exist or was not constructed under the programme	7	3	10 (1.6%)	Health centres: Olok HC II (Pader); Alik HC II (Lira); Acimi HC II (Oyam); Acokara HC II (Oyam); Ariba HC II (Oyam); Busia Eastern Division (Busia Municipal Council); Butoloogo HC II (Kassanda) Seed schools: Eastern Division (Tororo Municipal Council); Central Division (Jinja City); Kishangara Seed School (Ibanda)
Replaced by another facility	4	0	4 (0.6%)	Health centres: Oweko HC II (Nebbi); Pamaka HC III; Loinya HC II (Maracha); Liko HC III, already on the programme list; Ngomoromo HC II (Lamwo); Pangira HC III; Musandama HC II (Ntoroko); Butungama HC III

Outcome	Health centres	Seed schools	Total (% of 629)	Facilities (programme-list name and district: operating or receiving name)
Operates under another name	10	20	30 (4.8%)	Health centres: Kocheka HC II (Bukedea): Kangole/Kocheka HC III; Dabani (Busia): Buwumba HC III; Mantoroba HC II (Bundibugyo): Busanga HC III; Kidubuli HC II (Kabarole): Iruhura HC III; Nyabuswa HC II (Kabarole): Nyambuusa HC III; Kabbo (Mubende): Nakawala HC III; Kikoola (Kakumiro): Mukoora HC III; Kyakatebe HC II (Kassanda): Namabaale HC III; Kagganda HC II (Lwengo): Mbirizi SSS; Bussi HC II (Wakiso): Zinga HC III, already on the programme list Seed schools: Kadungulu Seed School (Serere): Kagwara SSS; Pallisa (Pallisa): Akadot SSS; Bunambutye Seed School (Bulambuli): Bumufuni SSS; Igombe (Bugweri): Mpiita SSS; Butagaya (Jinja): Buwala SSS; Mwema Seed School (Namayingo): Mutumba SSS; Kimenyedde Seed School (Mukono): St Andrews Ndwadde mutwe SSS; Nsiika T/C (Buhweju): Ndibarema Memorial SSS; Kagadi (Kagadi): King Solomon SSS; Kiryanga Seed School (Kagadi): St Catherine Kicucura SSS; Ruteete (Kagadi): Kitegwa Community SSS; Kasenda Seed School (Kabarole): St Paul Nyabweya SSS; Kabonero (Bunyangabu): Katugunda SSS; Kyamukube Town Council (Bunyangabu): Nsuura SSS; Bufumira Seed School (Kalangala): Nekemiya Memorial SSS; Kiringente Seed School (Mpigi): Wamatovu SSS; Mpumudde Seed School (Lyantonde): Rwamabara SSS; Buhanika (Hoima): Kidukuru SSS; Maddu Seed School (Gomba): return submitted as Kyayi Seed School; Mugarama, new facilities for St Mugagga (Kibaale): St Mugagga Vocational SSS
Not a UgIFT beneficiary	2	1	3 (0.5%)	Health centres: Alira HC II (Oyam); Buyinda HC II (Kaliro) Seed schools: Kiziranfumbi Seed School (Kikuube)
UgIFT assets relocated to another facility	2	1	3 (0.5%)	Health centres: Alangi (Zombo): Amwonyo HC III; Ther-uru HC II (Zombo): Atyak HC III Seed schools: Abanga (Zombo): Kango SSS
Exists with no UgIFT assets	2	3	5 (0.8%)	Health centres: Pandwong HC II (Kitgum Municipal Council); Rwamujojo HC II (Sheema Municipal Council) Seed schools: Bumbaire Seed School (Bushenyi); Kyamuhunga (Bushenyi); Kashenshero (Mitooma)
Total	27	28	55 (8.7%)	

Counts are programme-list facilities. HC means health centre; SSS means Seed Secondary School.

Programme-list facilities that were not UgIFT

Eight programme-list facilities (1.3%) exist but were not UgIFT facilities in practice: three are not UgIFT beneficiaries and five exist with no UgIFT assets. They are four health centres (1.1% of 371) and four seed schools (1.6% of 258), and all eight were recorded as complete on the programme list. With the 10 that do not exist or were not constructed under the programme, 18 programme-list facilities (2.9%) were not UgIFT facilities: 11 health centres (3.0%) and seven seed schools (2.7%); 16 of the 18 were recorded as complete on the programme list. At three further facilities in Zombo (Alangi, Ther-uru and Abanga), the facilities exist but their UgIFT assets were relocated to another facility; with these, 21 programme-list facilities (3.3%) held no UgIFT assets at the listed site.

The ten programme-list facilities that do not exist or were not constructed under the programme are:

- **Health centres (7):** Olok HC II (Pader), Alik HC II (Lira), Acimi HC II, Acokara HC II and Ariba HC II (Oyam), Busia Eastern Division (Busia Municipal Council) and Butoloogo HC II (Kassanda).
- **Seed schools (3):** Eastern Division (Tororo Municipal Council), Central Division (Jinja City) and Kishangara Seed School (Ibanda).

Eight of the ten were recorded as complete on the programme list, and the Eastern Division and Central Division school entries as ongoing. Table 13 sets out the expected position, the finding and the recommended action for the main cases.

Table 10: Expected facilities and the outcomes established during verification

Location	Expected position and field finding	Gap or service implication	Recommended action
Olok Health Centre, Pader	Expected: Olok was listed as a completed health facility intended to serve its catchment in Pader. Found: The district health officer confirmed to the verification team that Olok Health Centre had not been constructed and did not exist in the district.	The entry recorded as complete does not correspond to a facility on the ground. The reason for non-construction requires a documented resolution.	Pader District and the Ministry of Health should reconcile the approved project, construction and payment records, correct the beneficiary schedule and decide how the intended health-service need will be met.
Busia Eastern Division health-centre entry, Busia Municipal Council	Expected: The beneficiary schedule should identify the particular health facility supported in Busia Municipality. Found: Reconciliation confirmed that no health facility called Busia Eastern Division existed. A separate return identified Sofia Health Centre III within Eastern Division.	An administrative division had been used as a facility name. The available confirmation did not identify Sofia as its replacement or establish that the two names referred to the same beneficiary.	The municipality and Ministry of Health should resolve the original beneficiary identity and document the programme status of Sofia before linking or changing the two entries.
Ngomoromo, Oweko, Musandama and Loinya health centres, Lamwo, Nebbi, Ntoroko and Maracha	Expected: The beneficiary schedule should name the facility that received each planned investment. Found: Supervisors confirmed that Pangira replaced Ngomoromo in Lamwo, Pamaka replaced Oweko in Nebbi, Butungama replaced Musandama in Ntoroko, and Liko replaced Loinya in Maracha. Liko was already listed separately.	The programme account needs to link each original entry to its confirmed replacement to prevent duplicate counting and identify the service location.	The districts and Ministry of Health should attach the replacement decisions, link the original projects to their recipients and retain one active facility identity for each recipient.
Alangi, Ther-uru and Abanga, Zombo	Expected: Asset locations and custodians should agree with the facilities holding and using the equipment. Found: The supervisor confirmed that Alangi, Ther-uru and Abanga existed, but their UgIFT assets had moved respectively to Amwonyo Health Centre, Atyak Health Centre and Kango Seed Secondary School.	The original beneficiary names no longer described where the assets were held. Custody, location and the service arrangements at the original sites needed to be made clear.	Zombo District should reconcile transfer approvals and signed receipts with both sets of inventories, name the current custodians and confirm how the original catchments are served.
Alira Health Centre and Kiziranfumbi Seed Secondary School, Oyam and Kikuube	Expected: The programme beneficiary schedule should include institutions supported under UgIFT. Found: The later Oyam clarification confirmed that Alira Health Centre existed but was not among the facilities upgraded under UgIFT. The supervisor also confirmed that Kiziranfumbi Seed Secondary School in Kikuube was outside the programme.	The list confused the existence of an institution with its status as a UgIFT beneficiary. Alira had initially been reported absent, but that account was corrected.	The local governments and sector ministries should approve the scope corrections, remove the institutions from the active UgIFT schedule and preserve the reasons for the changes.
Pandwong Health Centre; Bumbaie, Kyamuhunga and Kashenshero schools; Rwamujojo Health Centre, Kitgum Municipal Council, Bushenyi, Mitooma and Sheema Municipal Council	Expected: Each listed beneficiary should have a supported account of the programme assistance it received. Found: Supervisors confirmed that Pandwong Health Centre, Bumbaie and Kyamuhunga schools, Kashenshero school and Rwamujojo Health Centre existed but had not benefited from UgIFT assets.	Their appearance on the beneficiary list did not establish delivery. The cause of the difference between the list and the reported benefits needs to be resolved.	The responsible districts, municipalities and sector ministries should check beneficiary approvals and delivery records, then correct the schedule or record an approved outstanding delivery with an accountable officer and follow-up date.

Location	Expected position and field finding	Gap or service implication	Recommended action
Bussi/Zinga and Dabani/Buwumba, Wakiso and Busia	Expected: Each facility should have one stable identity, with local and former names linked to it. Found: Bussi was confirmed to be the village name for the already-listed Zinga Health Centre in Wakiso. In Busia, the Buwumba return was reconciled to the programme-list entry named Dabani.	Different names could make one facility appear to be two, distort coverage and separate its asset history from the correct institution.	The districts should adopt the confirmed operating names, retain the old names as aliases and link the beneficiary, project and asset information to one facility identifier. Zinga should be counted once.

Facilities found outside the programme list

Teams also submitted information under 24 facility names that are not on the programme list: 15 health facilities and nine seed schools. The verification records hold 6,090 assets under these names, with a recorded value of UGX 23,219,308,548. They are counted separately from the 629 programme-list facilities. Follow-up confirmed three as additional programme beneficiaries: Rukoki General Hospital in Kasese Municipality, Silumira Health Centre III in Kakumiro and Bukuuku Community Seed Secondary School in Fort Portal City. Together they hold 692 assets with a recorded value of UGX 1,626,028,542, and their inclusion in the approved programme account should be regularised (Table 14).

Table 11: Confirmed additional beneficiaries outside the programme list

Location	Expected position and field finding	Gap or service implication	Recommended action
Rukoki General Hospital, Kasese Municipality	Expected: Confirmed beneficiaries should be included in the programme account. Found: The supervisor confirmed that Rukoki General Hospital was a UgiFT beneficiary in Kasese Municipality, although it was absent from the programme list used for verification. The verification records hold 183 assets for the hospital, with a recorded value of UGX 541,711,918.	The programme list omitted a confirmed recipient.	The Ministry of Health and municipality should approve the beneficiary entry and link its asset information to a stable facility identifier.
Silumira Health Centre III, Kakumiro	Expected: The beneficiary schedule should include supported health facilities. Found: The supervisor confirmed that Silumira Health Centre III had benefited in Kakumiro but was not on the programme list. The verification records hold 155 assets for the health centre, with a recorded value of UGX 385,797,109.	The facility was missing from the list used to plan and account for verification.	Kakumiro District and the Ministry of Health should approve the addition and connect the beneficiary decision to the facility asset inventory.
Bukuuku Community Seed Secondary School, Fort Portal City	Expected: Confirmed seed-school beneficiaries should appear in the programme account, with assets handed over for full use. Found: Bukuuku was confirmed as an additional beneficiary. The team recorded improved science and computer teaching following laboratory construction, while some asset handover remained pending. The verification records hold 354 assets for the school, with a recorded value of UGX 698,519,515.	The school was omitted from the programme list and handover was incomplete.	The city and Ministry of Education should regularise the beneficiary entry and complete joint handover of the outstanding assets.

The remaining 21 names should be resolved through the same checks of facility identity, programme approval and asset custody. Some entries came from combined returns, and some may be local or former names of programme-list facilities. A further 11 names found on the ground match a programme-list entry, as the facility that replaced it, the facility that received its relocated assets, or the same facility under its operating name or a corrected district; they are counted on that entry and are not additional. Appendix F lists all 24 names while the outstanding identity and scope decisions are completed.

4.3.3 Assets verified at health centres and seed schools

Health centres and seed schools held 208,982 of the 234,613 assets in the UglFT asset verification records (89.1%): 63,606 at health centres and 145,376 at seed schools. Table 15 shows them by asset category at national level. Buildings are shown with a dash because they are identified through property and site records rather than by engraving.

Table 12: Assets verified at health centres and seed schools by asset category

Asset category	Assets	Verified assets	Engraved	Not engraved
Health centres				
Clinical equipment	25,960	25,960	2,815 (10.8%)	23,145 (89.2%)
Clinical furniture	20,139	20,139	3,934 (19.5%)	16,205 (80.5%)
Other assets	8,129	8,119	1,028 (12.7%)	7,091 (87.3%)
Maternity ward equipment	7,438	7,438	1,510 (20.3%)	5,928 (79.7%)
Health centre ICT equipment	410	410	155 (37.8%)	255 (62.2%)
Vehicles and motorcycles	5	5	4 (80.0%)	1 (20.0%)
Building blocks	1,525	-	-	-
Health centres subtotal	63,606	62,071	9,446 (15.2%)	52,625 (84.8%)
Seed schools				
School furniture	109,713	109,713	31,656 (28.9%)	78,057 (71.1%)
Other assets	19,049	17,390	850 (4.9%)	16,540 (95.1%)
School computers and related equipment	10,266	10,059	2,445 (24.3%)	7,614 (75.7%)
School support equipment	916	916	140 (15.3%)	776 (84.7%)
Other ICT equipment	587	587	29 (4.9%)	558 (95.1%)
Vehicles and motorcycles	6	6	1 (16.7%)	5 (83.3%)
Building blocks	4,839	-	-	-
Seed schools subtotal	145,376	138,671	35,121 (25.3%)	103,550 (74.7%)
Total	208,982	200,742	44,567 (22.2%)	156,175 (77.8%)

Counts are assets. Verified assets are movable assets; buildings are identified through property and site records, and accessories and consumables were not part of the verification. Percentages are of verified assets.

School furniture was the largest category, with 109,713 assets or 75.5% of seed school assets, and school computers and related equipment accounted for a further 10,266 assets. At health centres, clinical equipment (25,960 assets, 40.8%) and clinical furniture (20,139, 31.7%) made up 72.5% of health centre assets, and maternity ward equipment accounted for 7,438 assets.

Of the 200,742 verified assets at health centres and seed schools, 44,567 (22.2%) were engraved and 156,175 (77.8%) were not engraved. Seed schools had the higher share engraved, 35,121 (25.3%), against 9,446 (15.2%) at health centres. Apart from the few vehicles and motorcycles, health centre ICT equipment (37.8%) and school furniture (28.9%) had the highest shares engraved, while clinical equipment (10.8%) and the other assets and other ICT equipment at seed schools (4.9% each) had the lowest. At health centres, 3,817 verified assets (6.1%) were properly engraved with the UglFT marking and 5,629 (9.1%) were not properly engraved; at seed schools the figures were 14,861 (10.7%) and 20,260 (14.6%). Section 4.5.1 sets out the identification position for all institutions, and Appendix I gives the photographic record of verified assets, grouped as health centres and then seed schools.

4.4 Conditions and use status

The UgIFT asset verification records classify each asset as working, meaning functional and in use, or not working, meaning faulty and not in use, so the working and in-use shares are the same. Of the 234,613 assets in the records, 221,093 (94.2%) were working and in use and 13,520 (5.8%) were not working and not in use. Of the assets not in use, 3,392 (25.1% of those not in use; 1.4% of all assets) were broken down, damaged or obsolete, and a further 1,114 (0.5% of all assets) were recorded as not functional. Others were in storage, awaiting delivery, power, building works or installation, held elsewhere, or stolen or lost, as set out in sections 4.5.1 and 4.5.2.

Table 16 shows condition and use by institution group, with national holdings first, then blood banks and local government facilities. National holdings were almost all working: 99.9% of MDA assets and all 8,099 hospital assets. The four MDA assets counted as broken down were three damaged laptops at OPM and a pickup at MoH that had been boarded off (section 4.1). Blood banks had 24 assets (3.8%) not working, six of them broken down. At local government level, health centres had the highest share not working (8.9%, 5,685 assets), while seed schools had the largest number broken down (2,722, 1.9% of school assets).


Table 13: Condition and use status by institution group

Institution group	Assets	Working	Not working	Broken down	In use	Not in use
Ministries, departments and agencies	16,902	16,882 (99.9%)	20 (0.1%)	4 (0.0%)	16,882 (99.9%)	20 (0.1%)
Hospitals	8,099	8,099 (100.0%)	0 (0.0%)	0 (0.0%)	8,099 (100.0%)	0 (0.0%)
Blood banks	626	602 (96.2%)	24 (3.8%)	6 (1.0%)	602 (96.2%)	24 (3.8%)
Health centres	63,606	57,921 (91.1%)	5,685 (8.9%)	660 (1.0%)	57,921 (91.1%)	5,685 (8.9%)
Seed schools	145,376	137,585 (94.6%)	7,791 (5.4%)	2,722 (1.9%)	137,585 (94.6%)	7,791 (5.4%)
Local government offices	4	4 (100.0%)	0 (0.0%)	0 (0.0%)	4 (100.0%)	0 (0.0%)
Total	234,613	221,093 (94.2%)	13,520 (5.8%)	3,392 (1.4%)	221,093 (94.2%)	13,520 (5.8%)

Working means functional and in use; not working means faulty and not in use. Broken down covers assets not in use that the records describe as broken down, damaged or obsolete, and forms part of not working; for MDAs it includes one vehicle that had been boarded off. Percentages are of each group's assets.

Condition varied more by asset category than by institution group (Figure 28). Most assets in every category were working. Clinical equipment and school computers and related equipment had the lowest shares in use, at 86.7% of 26,112 assets and 85.5% of 10,266 assets respectively, followed by health centre ICT equipment (89.0%) and school support equipment (90.8%). Other ICT equipment, mostly the handsets and tablets held by MDAs, was 99.7% in use.

Most assets in every category were working

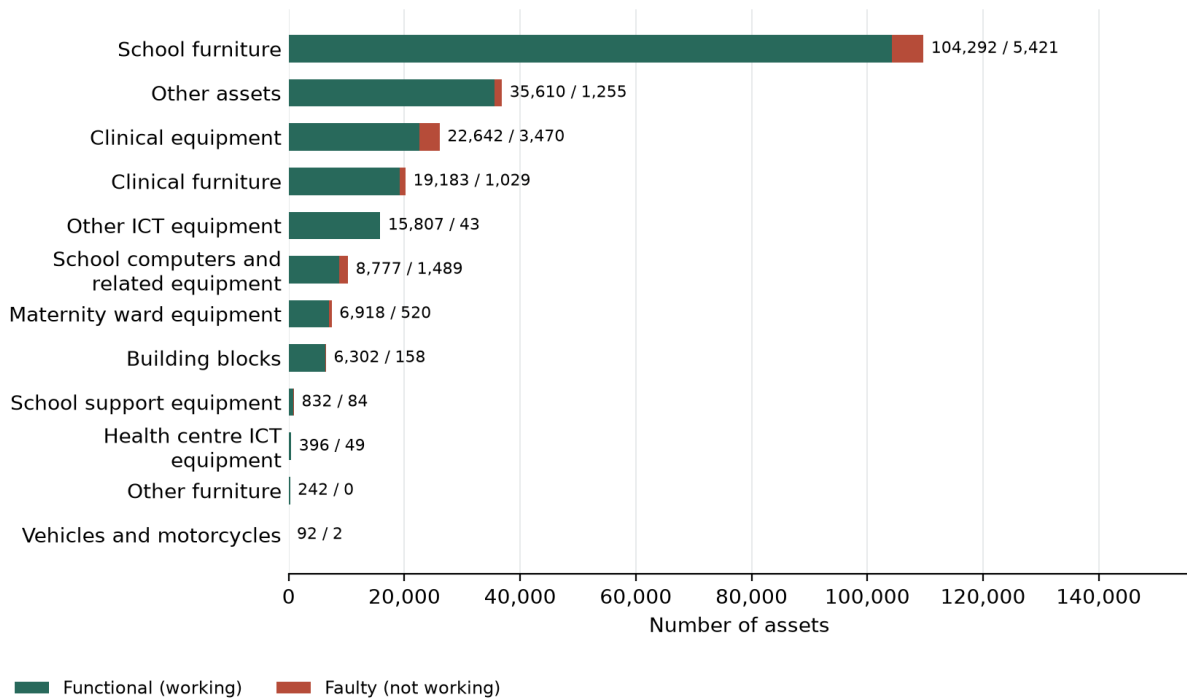


Source: UgIFT asset verification records; condition recorded for each asset.

Figure 28: Most assets in every category were working

Figure 29 divides the assets not in use in each category into those broken down, those in storage and those out of use for other reasons. In clinical equipment, 1,677 of the 3,470 assets not in use were in storage and 226 were broken down. In school furniture, 2,462 of the 5,421 assets not in use were broken down. In school computers and related equipment, 1,489 assets were not in use, of which 301 were in storage and 208 were broken down.

Clinical equipment and school computers had the most assets not in use

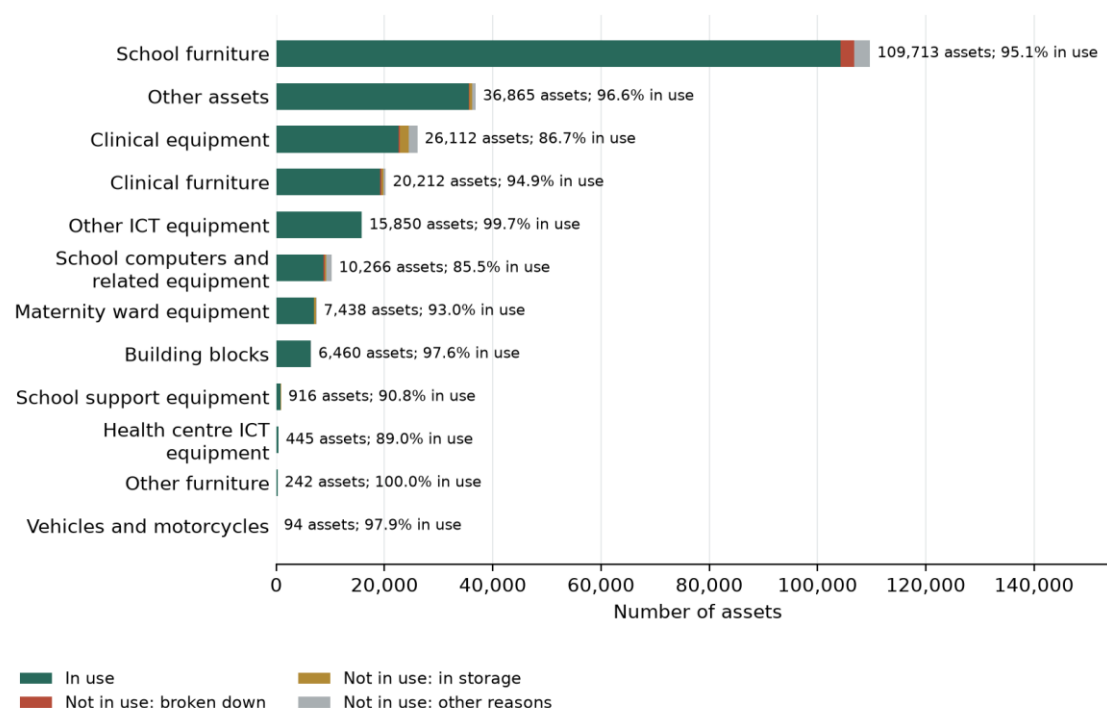

Source: UgIFT asset verification records; use status and the reason recorded for each asset.

Figure 29: Clinical equipment and school computers had the most assets not in use

Of the 224,705 verified assets, which are the movable assets, 49,463 (22.0%) were engraved and 175,242 (78.0%) were not engraved; buildings, structures and land are excluded from this count. Section 4.5.1 sets out engraving by institution group and the share properly engraved with the UgIFT marking.

The visits showed why availability, condition and use need to be considered together. At Kalemungole Health Centre III in Moroto District, neonatal respiratory equipment remained in an unopened carton and treatment trolleys were still wrapped, while the drip stands in daily use included some that were broken. At Sikuda Seed Secondary School in Busia District, a cracked stool was still in use among 118 stools in good working condition, while 23 desks were out of use, 21 of them awaiting repair.

Broken-down and stored assets require different action: damaged items need technical assessment, while usable stored items need the conditions for safe installation and use. Figures 30 to 37 show damage seen during the visits, from a torn delivery bed mattress cover, a damaged drip stand and broken school furniture to a cracked health centre block, a cracked water tank base, a peeling ceiling and a flood-affected older health facility.



Figure 30: Delivery bed with a torn mattress cover at a health centre, Busia District (Bukedi)



Figure 31: Damaged drip stand at a health centre, Moroto District (Karamoja)



Figure 32: Broken desk frame at a seed secondary school, Namisindwa District (Bugisu)



Figure 33: Stacked desks, chairs and stools, some recorded as broken and none engraved, at Napak Seed Secondary School, Napak District (Karamoja)



Figure 34: Cracked health centre block above collapsed ground, Bulambuli District (Bugisu)



Figure 35: Water tank on a cracked base at a seed secondary school, Kibuku District (Bukedi)



Figure 36: Stained and peeling ceiling at a health centre, Sironko District (Bugisu)



Figure 37: Flood-affected older health facility at Butiaba, Buliisa District (Bunyoro)

4.5 Status of equipment

This section describes the status of equipment after delivery. Section 4.5.1 covers identification, that is whether assets carry the engraving that links them to the programme, and custody, that is whether they are held where they were allocated. Section 4.5.2 covers utilisation: assets in storage, assets in use and assets broken down, and the blockers that keep equipment idle. Maintenance and repair arrangements and the priorities for follow-up are presented with the recommendations in chapter 5.

4.5.1 Identification (engraving) and custody

Identification links each asset to the programme and to the institution responsible for it. Verified assets for identification are the movable assets; buildings, structures and land are tracked by location, ownership and handover records instead. As noted in section 4.4, 49,463 of the 224,705 verified assets (22.0%) were engraved. Of these, 23,440 were properly engraved with the UgIFT marking (10.4% of verified assets; 47.4% of engraved assets) and 26,023 were not properly engraved, carrying another marking only (11.6% of verified assets; 52.6% of engraved assets).


Table 17 and Figure 38 show the position by institution group. MDAs had the highest share engraved (31.1%), and 97.7% of their engraved assets carried the UgIFT marking. None of the 7,745 verified hospital assets were engraved, and 92.9% of blood bank assets were not engraved. At local government level, 25.3% of verified seed school assets and 15.2% of verified health centre assets were engraved, but more than half of these carried another marking only: 20,260 of the 35,121 engraved school assets (57.7%) and 5,629 of the 9,446 engraved health centre assets (59.6%). Some facilities had no engraved assets at all: at Lungulu Seed Secondary School in Nwoya District, none of the assets had been engraved.

Table 14: Engraving of verified assets by institution group

Institution group	Verified assets	Engraved	Properly engraved	Not properly engraved	Not engraved
Ministries, departments and agencies	15,609	4,849 (31.1%)	4,736 (30.3%)	113 (0.7%)	10,760 (68.9%)
Hospitals	7,745	0 (0.0%)	0 (0.0%)	0 (0.0%)	7,745 (100.0%)
Blood banks	605	43 (7.1%)	26 (4.3%)	17 (2.8%)	562 (92.9%)
Health centres	62,071	9,446 (15.2%)	3,817 (6.1%)	5,629 (9.1%)	52,625 (84.8%)
Seed schools	138,671	35,121 (25.3%)	14,861 (10.7%)	20,260 (14.6%)	103,550 (74.7%)
Local government offices	4	4 (100.0%)	0 (0.0%)	4 (100.0%)	0 (0.0%)
Total	224,705	49,463 (22.0%)	23,440 (10.4%)	26,023 (11.6%)	175,242 (78.0%)

Verified assets are movable assets; buildings, structures and land are excluded. Properly engraved means engraved with the UgIFT marking; not properly engraved means engraved with another marking only. Percentages are of verified assets.

Most verified movable assets were not engraved

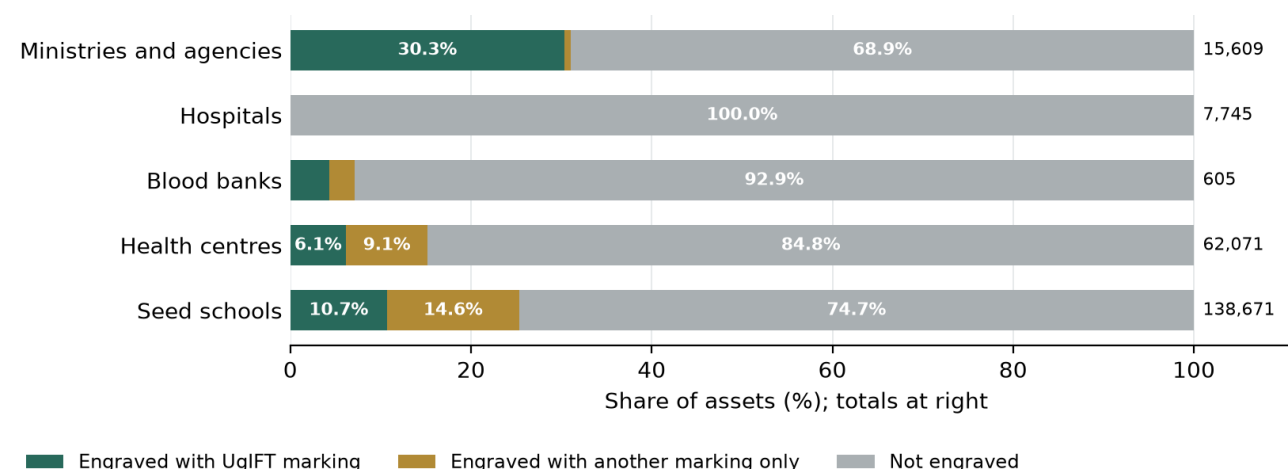

Source: UgIFT asset verification records; movable assets only.

Figure 38: Most verified movable assets were not engraved

The markings seen during verification show what proper engraving looks like. Health centre items carried markings such as GOU/MOH-UGIFT PROJECT with the financial year, in which GOU stands for the Government

of Uganda and MOH for the Ministry of Health; the marking refers to the ministry, not to a hospital. School items carried markings such as MOES/UGIFT, in which MOES stands for the Ministry of Education and Sports, together with school, district and item codes, the financial year and a serial number. Figure 39 shows the Ministry of Health marking on a desk at Namwaya Health Centre III in Tororo District, and Figure 40 the Ministry of Education and Sports marking on a desk at Aperikira Seed Secondary School in Kaberamaido District. Chairs at Budde Seed Secondary School in Butambala District carried the UgIFT identifier with the school name and serial numbers (Figures 41 and 42).



Figure 39: Engraving reading GOU/MOH-UGIFT PROJECT FY/2023/2024 on a desk at Namwaya Health Centre III, Tororo District (Bukedi)



Figure 40: Engraving reading APESSS MOES/UGIFT/KABE/SPLRS/2023-24/001 on a desk at Aperikira Seed Secondary School, Kaberamaido District (Teso)



Figure 41: Chair engraved UgIFT/ BUDDE SEED S.S M-PHALL CHAIR with a serial number at Budde Seed Secondary School, Butambala District (Buganda)



Figure 42: Chairs engraved BSS UGIFT with serial numbers at Budde Seed Secondary School, Butambala District (Buganda)

The programme marking appeared on a range of health centre items, including a bench at Bududa Health Centre III, a wheelchair, a refrigerator, a weighing scale and a delivery bed at Kalemungole Health Centre III, and a table at Kamoru Health Centre III in Kotido District (Figures 43 to 48). At Kyabasara Health Centre III in Kagadi District, the district code KDLG (Kagadi District Local Government) was combined with the programme identifier, which counts as proper engraving (Figure 49).



Figure 43: Engraving reading GOU/MOH-UGIFT PROJECT F/Y 2023/2024 on a bench at Bududa Health Centre III, Bududa District (Bugisu)



Figure 44: Wheelchair backrest marked GOU/MOH UGIFT-PROJECT. FY2023/2024 at Kalemungole Health Centre III, Moroto District (Karamoja)




Figure 45: Refrigerator marked GOU/MOH-UGIFT PROJECT FY2024-2025/01 at Kalemungole Health Centre III, Moroto District (Karamoja)



Figure 46: Engraving reading GOU/MOH-UGIFT PROJECT FY2023-2024/01 on a weighing scale at Kalemungole Health Centre III, Moroto District (Karamoja)



Figure 47: Engraving reading GOU/MOH-UGIFT PROJECT FY2023-2024/01 on a delivery bed at Kalemungole Health Centre III, Moroto District (Karamoja)



Figure 48: Engraving reading GOU/MOH-UGIFT PROJECT FY/2023/2024 on a table at Kamoru Health Centre III, Kotido District (Karamoja)



Figure 49: Engraving reading KDLG-UGFIT/HLTH/MAT/ODT/003 on a table at Kyabasara Health Centre III, Kagadi District (Bunyoro)

School, facility or district codes alone are not proper programme marking. Desks at Rupa Seed Secondary School in Moroto District carried the school name and serial numbers only, a steel cupboard at Moyok Health Centre III in Kween District carried a district and facility code, and furniture at King Solomon Seed Secondary School in Kagadi District carried the school name only. At Kamoru Health Centre III, a microscope carried the facility name written by hand, and at Bumugibole Health Centre III in Bulambuli District a wheelchair carried a hand-scratched code (Figures 50 to 54).



Figure 50: Classroom desks marked RUPA SEED with serial numbers, without a UgIFT marking, at Rupa Seed School, Moroto District (Karamoja)



Figure 51: Engraving reading KWN/MED-EQ/MOYOK HCIII on a steel cupboard at Moyok Health Centre III, Kween District (Sebei)



Figure 52: Engraving reading KING SOLOMON SEED SECONDARY SCHOOL, without a UgIFT marking, on furniture at King Solomon Seed Secondary School, Kagadi District (Bunyoro)



Figure 53: Microscope marked KAMORU HC III by hand at Kamoru Health Centre III, Kotido District (Karamoja)



Figure 54: Hand-scratched marking beginning Bum/2020- on a wheelchair armrest at Bumugibole Health Centre III, Bulambuli District (Bugisu)

Custody concerns where an asset is held and who is responsible for it, and engraving supports it: at Nalubembe Health Centre III in Kibuku District, assets were not issued for use for fear of loss because they had not been engraved. Where assets have moved, custody needs to move with them. Equipment from three Busia health centres, Bumunji, Buwembe and Majanji, had gone to Masafu General Hospital, including oxygen therapy apparatus, an oxygen concentrator, patient beds, an examination couch, a delivery bed, a nebuliser and a bubble continuous positive airway pressure (CPAP) unit.

Equipment intended for Todora Health Centre III in Nwoya District had gone to Paraa Health Centre III while construction was under way at Todora, and not all of it had been transferred back. In Manafwa District, items supplied to Bukimanayi Health Centre III had been redistributed to Bugobero Health Centre IV. The districts concerned should confirm the continuing allocation and retain signed handover or transfer documentation.

The records also describe assets that were not at the facility at the time of the visit. Of the 13,520 assets not in use, 2,522 (18.7%) at 152 facilities had not yet been delivered or handed over, were held elsewhere, or were not at the facility when the teams visited. They include 985 assets, mostly furniture, for five seed schools that the suppliers had not yet delivered, such as the chairs, stools, desks and tables still in the finishing phase for Kyarusozzi Seed Secondary School in Kyenjojo District, and 159 assets held at district stores or at another facility until the receiving facility was ready.

A further 525 assets at 32 facilities, 515 of them at 26 seed schools and mostly computers and related equipment, were reported stolen or lost. At Kabweri Seed Secondary School in Kibuku District, 28 desktop computers were out of use because they or their system units had been stolen, and the case was before the court.

4.5.2 Utilisation status of assets

This section separates the assets in storage, the share of assets in use and the assets broken down, and then sets out the blockers that kept equipment idle. Counts are of assets unless facilities are stated.

Assets in storage

The records place 3,200 assets not in use in storage, 23.7% of the 13,520 assets not in use and 1.4% of all assets, at 181 facilities. Most were at health centres: 2,681 assets (83.8%) at 164 of the 354 health centres in the records (46.3%). The other 519 were at 17 of the 255 seed schools (6.7%). Of the stored assets, 3,037 were in facility stores and 163 at district stores.

Clinical equipment made up 1,685 of the stored assets, followed by other assets (463), clinical furniture (369), school computers and related equipment (330) and maternity ward equipment (314). The items most often in storage were stethoscopes (133), uninterruptible power supply (UPS) units (129), manual vacuum aspiration (MVA) kits (122), neonatal bag valve masks (92), medical waste bins (81) and drip stands (80).

The records give the reasons for storage. Of the stored assets, 190 (5.9%) at 11 facilities were waiting for a power connection and 80 (2.5%) at four facilities for a building or room to be ready. A further 141 (4.4%) were held at district stores or at another facility; 93 (2.9%) were kept in store because of insecurity, because existing equipment was still in use or while awaiting placement in wards; 81 (2.5%) were broken down; 47 (1.5%) had components stolen; and 20 (0.6%) lacked accessories or parts. Another 158 (4.9%) were described as new, boxed or unopened and 361 (11.3%) as in good condition.

The remaining 2,023 stored assets (63.2%) were kept in the facility store; 1,918 of them were at health centres and 1,199 were clinical equipment, for example 171 assets at Kyarwabuganda Health Centre III in Mbarara City and 143 at Lama Health Centre III in Moyo District. Across all assets not in use, 483 at 29 facilities, 341 at health centres and 142 at seed schools, were kept in store and described as good, new, sealed or unopened. They can be brought into use once the room, power and installation are in place; 140 of them were waiting for a building or room to be ready.

Table 18 gives examples of local governments with assets in storage and the reasons recorded.

Table 15: Examples of local governments with assets in storage

Local government	Facility type	Assets in storage	Main items	Stated reason
Kabarole	Health centres (5)	211	Stethoscopes, MVA kits, drip stands, office chairs and bedside lockers	Still kept in the facility stores at Iruhura, Nyakitokoli, Nyambuusa and two other health centres
Omoro	Health centres (5)	159	Drip stands, bedside lockers, examination couches and patient screens	Kept in store; at Tekulu Health Centre III, 56 assets were held in store or in the incomplete maternity ward
Alebtong	Health centres (5)	138	Bubble CPAP units, neonatal bag valve masks, and hollow ware and instrument sets	Kept in store because of insecurity at Abia Health Centre III (45); no power at Awei and Adwir (7)
Kapelebyong	Health centres (2)	126	Infant and adult resuscitators, digital blood pressure machines and glucometers	In store and in good condition at Akoromit Health Centre III (117)
Amuria	Health centres (4)	116	Neonatal bag valve masks, delivery instrument sets, resuscitators and MVA kits	In store and in good condition (54); at Alere Health Centre III, staff were still using their existing equipment (27)
Kazo	Health centres (4)	80	Infant resuscitators, neonatal bag valve masks, stethoscopes and oxygen concentrators	In good condition and kept in store (65)

Local government	Facility type	Assets in storage	Main items	Stated reason
Kaberamaido	Seed school	132	Computer sets (system units, monitors, keyboards, mice and UPS units), surge protectors and security cameras	Not yet delivered to Aperikira Seed Secondary School; still at the district stores
Pallisa	Seed school	126	Computer sets, servers, network switches and wireless routers	In the school store at Akadot Seed Secondary School because the school has no electricity
Bukwo	Seed school	25	UPS units, a server, a network switch, a printer and a projector	In good shape and still in boxes in the store at Senendet Seed Secondary School
Amuru	Seed school	22	Desktop computers	Still boxed at Amuru Seed Secondary School; no electricity at the school

Assets not in use whose field description places them in a facility or district store. Figures in brackets are assets.

The photographs show the same pattern. At Lungulu Seed Secondary School in Nwoya District, desktop computers, a printer and UPS units remained boxed in the store because the school was awaiting a power connection, without which the equipment could not be installed (Figure 55). The other school photographs show chairs and other items kept in a largely empty ICT and library block at Iriiri Seed Secondary School in Napak District, which remained with the contractor, computer sets stacked in store with their cables still bundled at Bumufuni Seed Secondary School in Bulambuli District, and furniture and equipment stored at Butungama and King Solomon seed schools while the buildings were completed (Figures 56 to 60).



Figure 55: Desktop computers, a printer and UPS units still boxed in the store at Lungulu Seed Secondary School, Nwoya District (Acholi), awaiting a power connection for installation



Figure 56: Largely empty ICT and library block with a few chairs and items kept in one corner at Iriiri Seed Secondary School, Napak District (Karamoja), not yet in use while the school remained with the contractor



Figure 57: HP computer sets stacked in store with cables still bundled and not installed at Bumufuni Seed Secondary School, Bulambuli District (Bugisu)

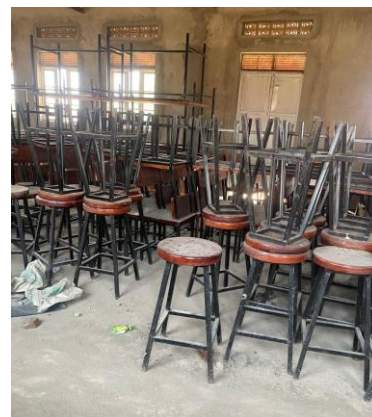


Figure 58: Laboratory stools and desks stored and not yet in use at Butungama Seed Secondary School, Ntoroko District (Tooro), where the school buildings were still under construction



Figure 59: Boxed projector, air conditioner and other equipment in store at King Solomon Seed Secondary School, Kagadi District (Bunyoro), kept boxed because the school was still under construction



Figure 60: Chairs, desks and laboratory stools stacked in a hall at King Solomon Seed Secondary School, Kagadi District (Bunyoro), where most assets remained in storage because the school was still under construction

At health centres, clinical equipment was kept among cartons at Kihuukya Health Centre III in Hoima City, handheld pulse oximeters were still boxed at Kibiri Health Centre III, which had opened on 31 August 2026, and beds and screens were stacked in storage at Kyabasara Health Centre III in Kagadi District. At Majanji Health Centre III in Busia District, a pedal suction unit was still in its packing because staff lacked the technical knowledge to use it (Figures 61 to 64).



Figure 61: Clinical equipment kept in store among cartons and not in use at Kihuukya Health Centre III, Hoima City (Bunyoro)



Figure 62: Boxed handheld pulse oximeters at Kibiri Health Centre III, Makindye-Ssabagabo Municipal Council (Buganda), where equipment was still being arranged after the facility opened on 31 August 2026



Figure 63: Hospital beds and screens stacked in storage at a health centre, Kagadi District (Bunyoro)



Figure 64: Pedal suction unit marked MAJANJI H/C III still in its packing, recorded as not in use for lack of technical knowledge, Majanji Health Centre III, Busia District (Bukedi)

Utilisation

Utilisation is the share of assets in use. In the records, 221,093 of the 234,613 assets (94.2%) were in use at the time of the visit. Use was highest at national level (Table 16), where only three MDAs and one blood bank had any asset not in use. At local government level, 94.6% of seed school assets and 91.1% of health centre assets were in use, but idle assets were spread widely: 255 of the 354 health centres (72.0%) and 132 of the 255 seed schools (51.8%) in the records had at least one asset not in use.

By broad asset type, 95.1% of furniture and fittings, 93.9% of ICT equipment and 91.2% of medical and laboratory equipment were in use. Medical and laboratory equipment therefore had the lowest share in use, with 4,412 assets idle, mainly clinical equipment at health centres.

Computers at seed schools were among the least used equipment. Of the 3,875 desktop and laptop computers at seed schools, 3,264 (84.2%) were in use and 611 (15.8%) were not in use, at 33 of the 163 schools holding computers. Of the 613 computers not in use at seed schools and health centres, 245 had been stolen or lost, 97 were broken down, 72 awaited power, 44 awaited installation or a finished building, 20 were held elsewhere and 89 were not at the facility at the time of the visit. By comparison, 98.6% of the 1,074 computers held by MDAs were in use (section 4.1).

Broken down

The records describe 3,392 assets not in use as broken down, damaged or obsolete: 25.1% of assets not in use and 1.4% of all assets, at 183 facilities. Seed schools held 2,722 of them, at 68 schools (26.7% of the seed schools in the records), and health centres 660, at 112 health centres (31.6%). Six were blood pressure machines at the Arua Regional Blood Bank and four were at MDAs (section 4.1).

Furniture made up most of the broken-down assets. School furniture accounted for 2,462 (72.6%); at seed schools the broken items were mainly chairs (1,046), desks (682), stools (657) and tables (152). At health centres, the most common were bedside lockers (67), wheelchairs (54), patient screens (41), filing cabinets (36) and office chairs (32). Clinical furniture accounted for 277 broken-down assets, clinical equipment for 226 and school computers and related equipment for 208, including 106 UPS units.


The largest groups of broken school furniture were at Mpungwe Seed Secondary School in Mayuge District (275 assets, mainly learners' chairs and laboratory stools), Laponi Seed Secondary School in Agago District, where 70 desks were broken and needed replacement, Busiime Seed Secondary School in Busia District (50 desks needing repair) and Palam Seed Secondary School in Katakwi District (43 tables). At Malaba Seed Secondary School in Tororo District, 34 chairs and four tables were not in good condition. Among health centres, Mirambi Health

Centre III in Bundibugyo District, Owiny Health Centre III in Kwanja District and Nyanja Health Centre III in Mukono Municipal Council had the largest numbers, mainly medical waste bins, bedside lockers, drip stands, patient screens and wheelchairs.

Utilisation blockers

Figure 65 sets out the reasons recorded for the assets not in use. After breakdowns (3,392 assets, 25.1%), the largest groups were assets kept in storage (2,542, 18.8%; the other 658 stored assets are counted under their specific reason), assets not yet delivered or handed over, held elsewhere or not at the facility at the time of the visit (2,522, 18.7%), assets in working order but not yet put to use (1,347, 10.0%) and assets waiting for power, building works, installation or trained users (1,324, 9.8%).

Breakdowns and storage were the main reasons assets were not in use

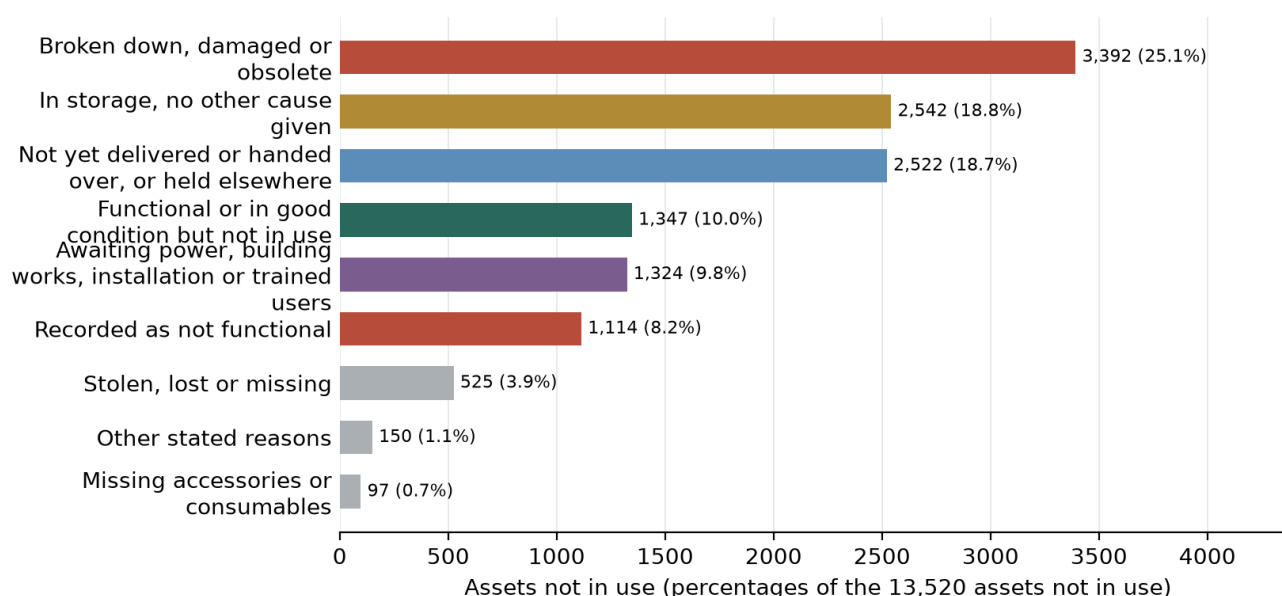

Source: UgIFT asset verification records; reason recorded against each asset not in use.


Figure 65: Breakdowns and storage were the main reasons assets were not in use

The asset-level blockers were specific. Installation or assembly held back 493 assets (3.6% of assets not in use) at 21 facilities, including 360 laboratory stools not yet assembled at Alerek Seed Secondary School in Abim District. Buildings or rooms that were not ready held back 483 (3.6%) at 39 facilities: at Ngai Seed Secondary School in Oyam District, 126 laboratory stools and 23 tables were not in use because the science laboratory had not yet been commissioned, and at Muhula Seed Secondary School in Butaleja District, 120 new desks awaited handover of the school by the contractor.

Lack of power held back 331 assets (2.4%) at 31 facilities, including 28 desktop computers and 28 UPS units at Bubentsye Seed Secondary School in Mbale District. Missing accessories, parts or consumables held back 97 (0.7%) at 41 facilities, such as paediatric beds supplied without mattresses at Okwerodot Health Centre III in Kole District. A further 16 assets awaited trained users and one a specialist operator.

The facility interviews give the users' view. Of the 477 facilities that described their services, 156 (32.7%) reported equipment that was idle or could not be used: 111 health centres (39.1% of 284) and 45 seed schools (23.3% of 193). Figure 66 shows the reasons they gave. Power, meaning no or unreliable electricity or weak solar systems, was cited by 71 of these facilities (45.5%); training or skills to operate the equipment by 52 (33.3%); installation, assembly or connection by 32 (20.5%); incomplete buildings or lack of space by 27 (17.3%); missing accessories or consumables by 15 (9.6%); and staffing, meaning no personnel or specialists to use the equipment, by 9 (5.8%).

Power and user skills were the main reasons equipment stood idle

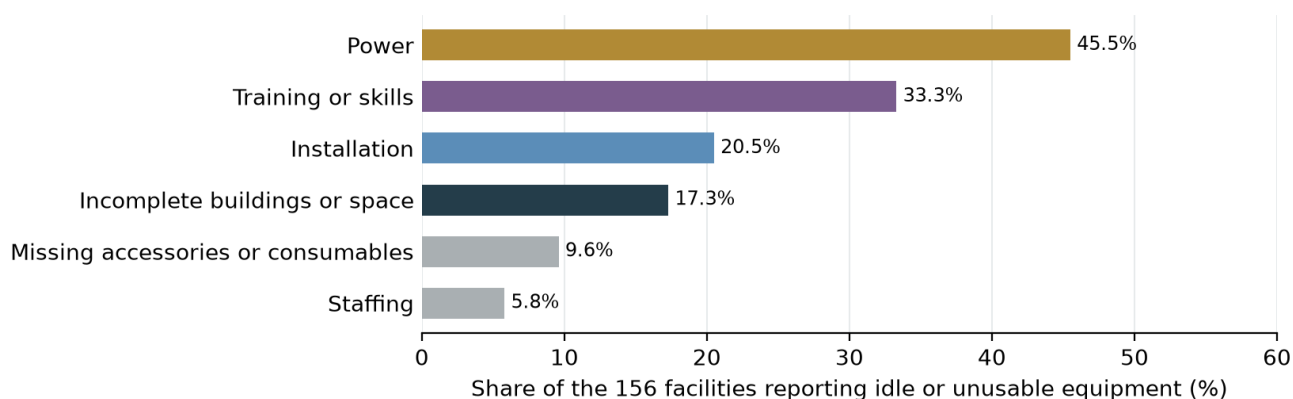

Source: Facility interviews during verification (service delivery question).

Figure 66: Power and user skills were the main reasons equipment stood idle

The blockers differed by facility type. At health centres, training was the most common reason (51 of 111, 45.9%), ahead of power (47, 42.3%) and installation (20, 18.0%). At seed schools, power led (24 of 45, 53.3%), followed by incomplete buildings or space (14, 31.1%) and installation (12, 26.7%). Examples include most of the supplied items at Rukoni West Health Centre III in Ntungamo District, kept in the store because there was no power to run them, equipment at Rubingo Health Centre III in Fort Portal City still in its boxes because it had not been assembled, instruments at Terenpoy Health Centre III in Kween District unused for lack of technical staff, and equipment at Lake Mburo Seed Secondary School in Kiruhura District kept in the store until the buildings were finished.

4.6 Financial value of verified assets

The 234,613 assets in the UgIFT asset verification records carry a recorded value of UGX 997,840,855,042, accumulated depreciation of UGX 185,538,888,776 and a net book value of UGX 812,316,492,277 at 30 September 2026. The values follow the valuation basis in section 2.5, under which net book value is recorded value less accumulated depreciation for each asset, with a minimum of zero. Table 19 presents the values by institution group, from the national level to the local governments.

Table 16: Recorded value, depreciation and net book value by institution group


Institution group	Assets	Recorded value UGX	Share of recorded value	Accumulated depreciation UGX	Net book value UGX	Net book value as % of recorded value
Ministries, departments and agencies	16,902	31,967,493,589	3.2%	19,480,446,057	12,487,047,532	39.1%
Hospitals	8,099	26,080,242,410	2.6%	22,423,146,484	3,657,095,926	14.0%
Blood banks	626	1,451,584,715	0.1%	514,105,544	937,479,171	64.6%
Health centres	63,606	259,662,849,164	26.0%	41,291,859,808	218,378,252,366	84.1%
Seed schools	145,376	678,247,549,426	68.0%	101,549,907,057	576,704,905,370	85.0%
Local government offices	4	431,135,738	0.0%	279,423,826	151,711,912	35.2%
Total	234,613	997,840,855,042	100.0%	185,538,888,776	812,316,492,277	81.4%

Values at 30 September 2026. Net book value is calculated asset by asset with a minimum of zero, so for a group it can exceed recorded value less accumulated depreciation. Local government offices hold four transport assets.

National institutions hold UGX 59,499,320,714, or 6.0% of the recorded value: ministries, departments and agencies hold UGX 31,967,493,589 (3.2%), hospitals UGX 26,080,242,410 (2.6%) and the blood banks UGX 1,451,584,715 (0.1%). Hospital holdings are largely depreciated, with a net book value of UGX 3,657,095,926, or 14.0% of recorded value; the regional referral hospitals account for UGX 24,338,709,624 of the hospital value. At the blood banks, net book value stands at 64.6% of recorded value.

Local governments hold the rest. Seed schools account for UGX 678,247,549,426 (68.0%) and health centres for UGX 259,662,849,164 (26.0%), together 94.0% of the recorded value; four transport assets held by district offices make up the remainder. Buildings drive these values: building blocks account for UGX 697,270,758,260 (69.9%) of the total recorded value, of which UGX 498,200,387,586 is at seed schools and UGX 198,198,049,954 at health centres. School furniture adds UGX 94,352,912,507 (9.5%). Figure 67 compares recorded value with net book value for each institution group.

Seed schools and health centres hold most of the recorded value

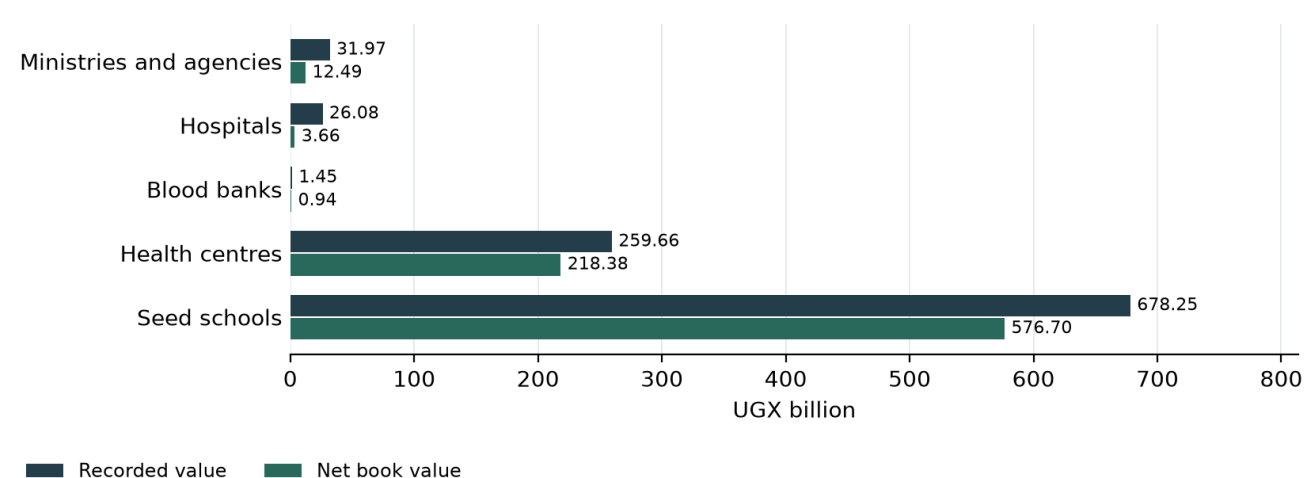

Source: UglIFT asset verification records; recorded value and net book value at 30 September 2026.

Figure 67: Seed schools and health centres hold most of the recorded value

Table 20 gives the values for each ministry, department and agency, including Kampala Capital City Authority (KCCA) and the Ministry of Defence and Veteran Affairs (MoDVA), and Figure 68 ranks them by recorded value. The 10,783 MoES assets, all ICT equipment and mainly Teacher Effectiveness and Learners Assessment (TELA) handsets, inspection tablets and laptops, carry UGX 14,925,128,359 (46.7% of the MDA total). MoFPED follows with UGX 6,152,854,000 (19.2%), of which UGX 4,550,385,492 is for 20 double cabin vehicles, and MoWE with UGX 5,000,313,297 (15.6%).

Table 17: Recorded value, depreciation and net book value by ministry, department and agency


Institution	Assets	Recorded value UGX	Share of MDA recorded value	Accumulated depreciation UGX	Net book value UGX	Net book value as % of recorded value
MoFPED	458	6,152,854,000	19.2%	4,272,041,257	1,880,812,743	30.6%
MoWT	88	455,932,376	1.4%	326,484,882	129,447,494	28.4%
MoES	10,783	14,925,128,359	46.7%	10,607,476,704	4,317,651,655	28.9%
MAAIF	2,045	2,332,681,629	7.3%	984,457,129	1,348,224,500	57.8%
MoH	264	1,216,859,097	3.8%	463,977,008	752,882,089	61.9%
OPM	10	53,535,300	0.2%	48,181,770	5,353,530	10.0%
MoWE	2,939	5,000,313,297	15.6%	2,089,906,834	2,910,406,463	58.2%

Institution	Assets	Recorded value UGX	Share of MDA recorded value	Accumulated depreciation UGX	Net book value UGX	Net book value as % of recorded value
MoGLSD	10	46,180,000	0.1%	13,660,000	32,520,000	70.4%
NEMA	6	46,824,409	0.1%	32,841,273	13,983,136	29.9%
PPDA	5	30,153,500	0.1%	13,066,516	17,086,984	56.7%
OAG	20	388,773,680	1.2%	111,591,545	277,182,135	71.3%
MoLG	13	343,320,450	1.1%	284,804,160	58,516,290	17.0%
MoLHUD	27	829,749,997	2.6%	124,320,000	705,429,997	85.0%
KCCA	51	54,024,515	0.2%	53,024,515	1,000,000	1.9%
MoDVA	183	91,162,979	0.3%	54,612,464	36,550,515	40.1%
Total	16,902	31,967,493,589	100.0%	19,480,446,057	12,487,047,532	39.1%

Values at 30 September 2026, rounded to the nearest shilling for each institution; the total may differ from the sum of the rows by UGX 1.

ICT equipment makes up UGX 22,851,705,326 (71.5%) of the recorded value at the ministries, departments and agencies, and vehicles UGX 6,427,809,389 (20.1%). Much of this equipment is well into its useful life: the net book value of UGX 12,487,047,532 is 39.1% of recorded value overall, and only 28.9% at MoES and 30.6% at MoFPED, the two largest holders.

MoES and MoFPED hold the largest ministry recorded values

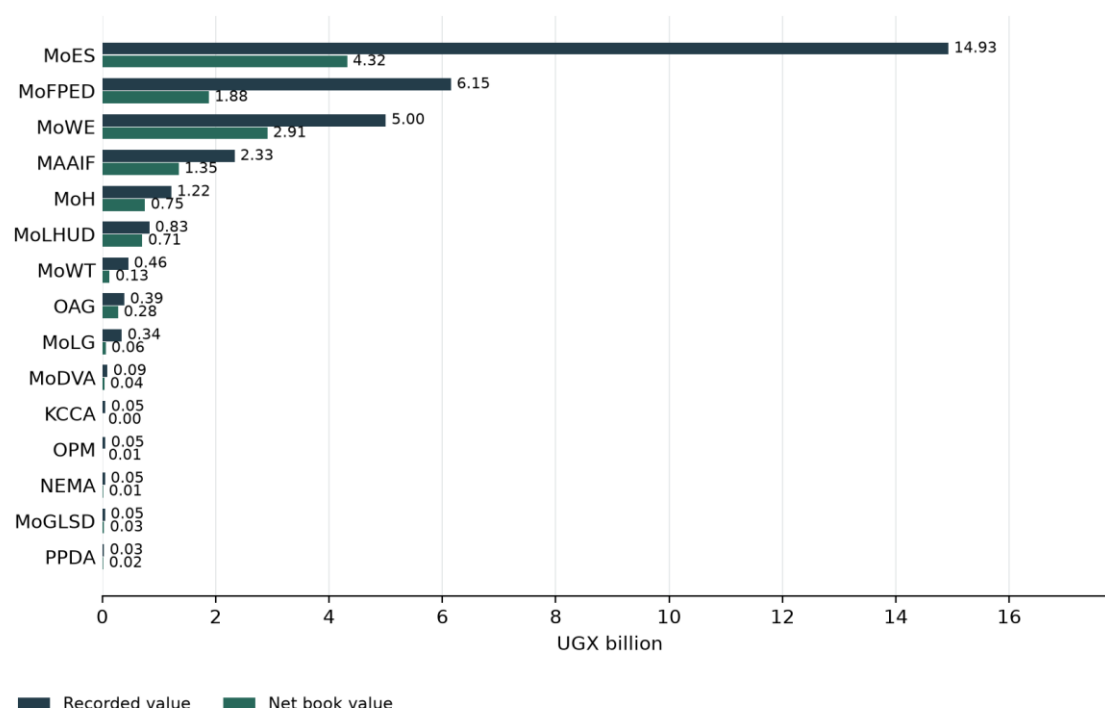

Source: UgIFT asset verification records; national ministry and agency votes.

Figure 68: MoES and MoFPED hold the largest ministry recorded values

4.7 UgIFT support to service delivery

During the interviews, teams asked each facility how the UgIFT support had helped service delivery in the area, and what issues, challenges and recommendations it had. Of the facilities on the programme list, 284 health centres and 193 seed schools described service delivery in their answers. The percentages in this section are


shares of these facilities: they show how widely a benefit or a gap was reported, not the number of patients, mothers or learners served. A facility counts once under each benefit or gap it described.

4.7.1 Benefits reported by facilities

Of the 284 health centres, 237 (83.5%) reported at least one benefit from the UgIFT support. Improved maternity and delivery services were reported by 117 (41.2%), and 51 (18.0%) reported more or safer births at the facility. Improved antenatal, immunisation, laboratory or other specific services were reported by 89 (31.3%), improved access to care or shorter distances by 70 (24.6%) and more patients attending by 60 (21.1%). More than half, 163 (57.4%), linked better services to the equipment and furniture supplied.

Of the 193 seed schools, 144 (74.6%) reported at least one benefit. A better learning environment, with classrooms, furniture and libraries, was reported by 74 (38.3%), and improved access to secondary education or shorter distances by 59 (30.6%). Practical science or ICT teaching improved at 39 schools (20.2%), and 37 (19.2%) reported higher enrolment. Forty schools (20.7%) also reported jobs and local economic benefits around the school. Figure 69 compares the benefits most often reported by the two types of facility.

Maternity care and access to education were the most reported benefits

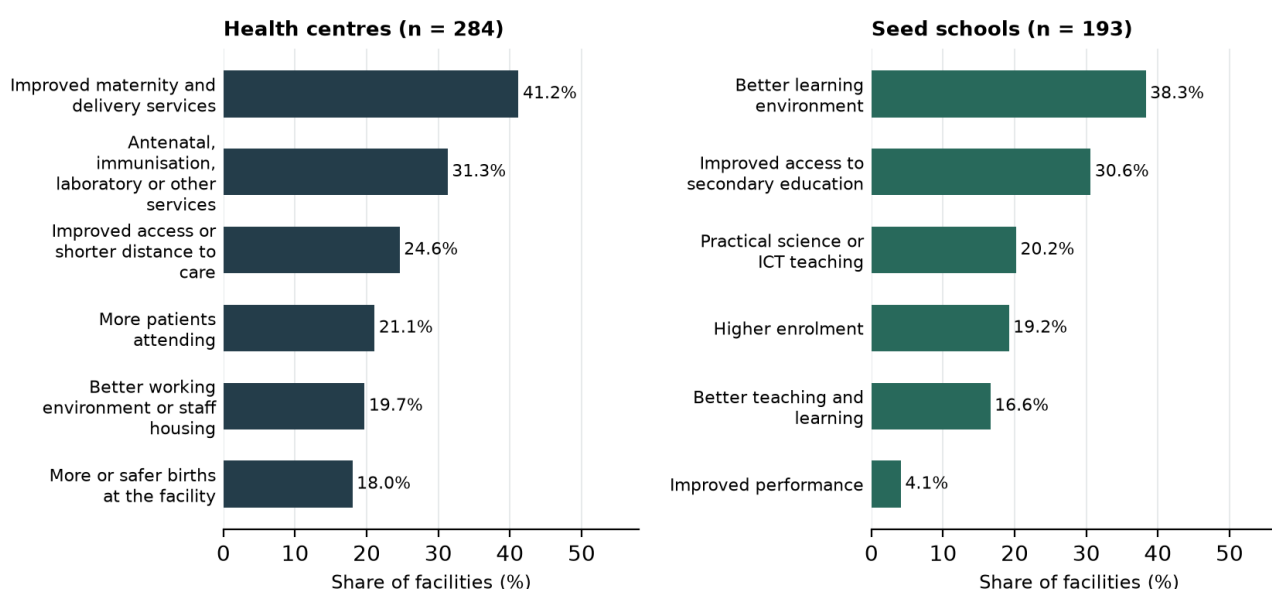

Source: Facility interviews during verification (service delivery question).

Figure 69: Maternity care and access to education were the most reported benefits

Health centre accounts show what these benefits meant for mothers and patients. Staff at Lukale Health Centre III in Buvuma said women could give birth locally instead of crossing water and had greater privacy. Kagumba Health Centre III in Kamuli reported more than 50 deliveries a month in the new maternity ward, and antenatal attendance rose from 56 to over 165 mothers a month. Kabahango Health Centre III in Bunyangabu conducted about 55 deliveries a month where it had conducted none before, and patient attendance rose from about 400 to 750. At Kataraza Health Centre III in Kyenjojo, pregnant mothers no longer walk about 40 kilometres to reach a health centre, and at Pamaka Health Centre III in Nebbi staff described increased attendance and community confidence.

Health centres gave equally practical examples of wider services. Kachuru Health Centre III in Butebo now offers laboratory services, inpatient care and minor surgery, and at Mutungo Health Centre III in Makindye-Ssabagabo Municipal Council the new building replaced an open tent shelter. Kibiri Health Centre III, in the same municipality, had begun operations by 31 August 2026, while staff were still arranging some equipment.

At Kihuukya Health Centre III in Hoima City, the renovated maternity block and walkways were recorded in use and a binocular microscope was seen functioning. Iruhura Health Centre III in Kabarole recorded adult weighing scales and waiting benches in use. Kamuli Health Centre III in Tororo reported improved service delivery, alongside continuing staffing and accommodation needs. Figures 70 to 74 show these health centre buildings and equipment in service.



Figure 70: Health centre building at Kibiri HC III, Makindye-Ssabagabo Municipal Council (Buganda)



Figure 71: Health centre buildings and covered walkway at Kihuukya HC III, Hoima City (Bunyoro)



Figure 72: Binocular microscope at Kihuukya HC III, Hoima City (Bunyoro)



Figure 73: Adult weighing scale with a height meter and waiting benches at Iruhura HC III, Kabarole District (Tooro)



Figure 74: Maternity block entrance and access ramp at Kamuli HC III, Tororo District (Bukedi)

Schools also described practical gains. Musiitwa Nazigo Seed Secondary School in Kayunga used the irrigation system for teaching and food production and provided secondary education closer to surrounding communities. Kigorobya Seed Secondary School in Hoima used its classrooms, computer room and chemistry laboratory to support teaching, and at Kihanga Seed Secondary School in Ntungamo learners acquire computer skills in the equipped computer laboratory. At Rupa Seed Secondary School in Moroto, all 41 pioneer candidates scored first grade in the Uganda Certificate of Education examinations in 2024.

Other school visits showed the value of bringing teaching space closer to communities. Enrolment at Bwizi Seed Secondary School in Kamwenge grew from 204 to 1,108 students, and at Sisuni Seed Secondary School in Manafwa from 170 to 540. Gyagenda Memorial Seed Secondary School in Bujumba reported better access to secondary education about 35 kilometres from Kalangala town, and Buyende Seed Secondary School serves learners from islands in Lake Kyoga.

Sisiyi Seed Secondary School in Bulambuli recorded its buildings, furniture and ICT in use. Sibanga Seed Secondary School in Manafwa reported shorter distances for learners and less teenage pregnancy and school dropout, although full handover was still pending. Figures 75 to 77 show teaching spaces at Gyagenda Memorial, Sibanga and Sisiyi.



Figure 75: Classroom furnished with desks and a whiteboard at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)




Figure 76: Books displayed on library shelves at Sibanga Seed School, Manafwa District (Bugisu)



Figure 77: ICT laboratory block and entrance ramp at Sisiyi Seed Secondary School, Bulambuli District (Bugisu)

4.7.2 User gaps and challenges

Facilities also described what held the service back. Nearly all raised at least one gap: 272 health centres (95.8%) and 180 seed schools (93.3%), or 452 of the 477 facilities (94.8%). The figures in this section count a gap as raised when a facility named it as a challenge or asked for it as a remedy in its recommendations; a facility that asked for a fence, for example, is counted under security or fencing. Table 21 gives the counts and Figure 78 compares the two types of facility.


Power was the gap raised most often, by 200 facilities (41.9%): 44.0% of health centres and 38.9% of seed schools. Staffing followed at 32.3%, inadequate space or infrastructure at 31.7% and security or fencing at 27.3%, the last raised by 37.8% of seed schools. Repair or maintenance support was raised by 22.2% of facilities, staff housing by 22.0% and water supply by 20.1%. Two gaps belonged mainly to one type of facility: training to operate equipment was raised by 28.9% of health centres, and incomplete or delayed works by 28.0% of seed schools. Equipment not installed, not assembled or delivered incomplete was raised by 17.6% of facilities.

Table 18: User gaps and challenges raised by facilities that described service delivery

Gap or challenge raised	Health centres (n = 284)	Seed schools (n = 193)	All facilities (n = 477)
Power or electricity	125 (44.0%)	75 (38.9%)	200 (41.9%)
Staffing or manpower	102 (35.9%)	52 (26.9%)	154 (32.3%)
Inadequate space or infrastructure	85 (29.9%)	66 (34.2%)	151 (31.7%)
Security or fencing	57 (20.1%)	73 (37.8%)	130 (27.3%)
Repair or maintenance support	77 (27.1%)	29 (15.0%)	106 (22.2%)
Staff housing	66 (23.2%)	39 (20.2%)	105 (22.0%)
Water supply	51 (18.0%)	45 (23.3%)	96 (20.1%)
Training to operate equipment	82 (28.9%)	3 (1.6%)	85 (17.8%)
Equipment not installed, not assembled or delivered incomplete	46 (16.2%)	38 (19.7%)	84 (17.6%)
Works incomplete, delayed, not handed over or not commissioned	28 (9.9%)	54 (28.0%)	82 (17.2%)
Access roads or transport	39 (13.7%)	19 (9.8%)	58 (12.2%)
Accessories or consumables for supplied equipment	21 (7.4%)	8 (4.1%)	29 (6.1%)
Internet or network connectivity	5 (1.8%)	7 (3.6%)	12 (2.5%)
At least one gap raised	272 (95.8%)	180 (93.3%)	452 (94.8%)

Number of facilities and share of the facilities that described service delivery. A gap is raised when the facility named it as a challenge or asked for it as a remedy; a facility can raise several gaps.

Power, staffing and space were the gaps most often raised

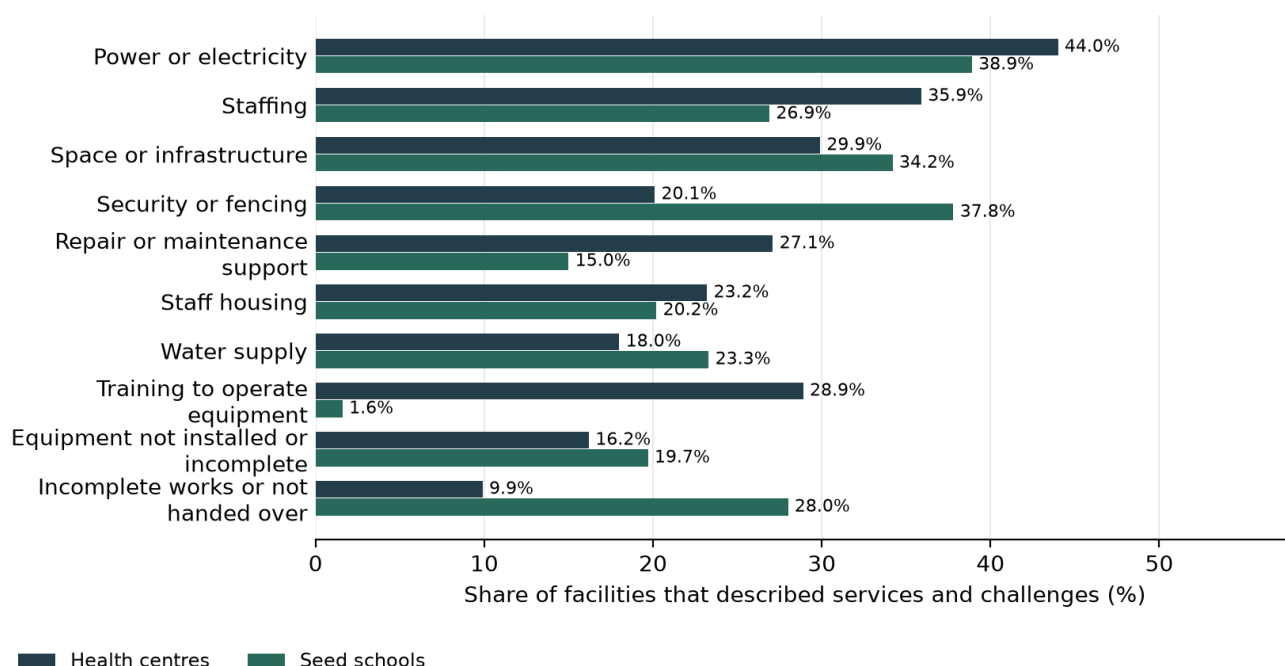

Source: Facility interviews during verification (service delivery question).

Figure 78: Power, staffing and space were the gaps most often raised

Power gaps limit the use of equipment already supplied. Loyoajonga Health Centre III in Omoro has no grid connection, so machines that need mains power cannot be used, and at Nkata Health Centre III in Buvuma weak solar batteries cannot run the equipment at the same time. Power restricted oxygen equipment at Pamaka, where the solar panel worked for only three months after commissioning. Alwi Seed Secondary School in Pakwach hires a generator to use its ICT equipment after power surges damaged some of it, and at Rupa teaching spaces served as dormitories and practical lessons depended on a hired generator.

Water and repairs were each raised by about one facility in five. Makokoto Health Centre III in Kassanda relies only on rainwater, and at Loyoajonga two of the three maternity water tanks were not connected. Nkombe Health Centre III in Mayuge reported that repairs by the regional workshop take weeks or months.

Demand also brought pressure on staff. Acii Health Centre III in Amolatar had 7 staff against 55 under the new staffing norms, and at Punuluru Health Centre III in Lira two nurses served the whole health centre. Pamaka reported too few medical personnel for its growing number of patients, and Kigorobyia reported a shortage of staff and few study materials. Mpungwe Seed Secondary School in Mayuge reported a teacher to student ratio of 1:100 against 1:60.

Space and housing gaps affect patients, learners and staff. Lakwatomer Health Centre III in Omoro attends to patients under trees for lack of space, Mpungwe hires tents at examination time for lack of classrooms, and at Kiyombya Seed Secondary School in Bunyangabu classes planned for 60 learners hold about 130. Kagumba identified needs for staff housing and for outpatient, laboratory, storage and kitchen space, and at Gyagenda Memorial 30 teachers share six housing units.

Security and access gaps affect assets and attendance. Christ the King Mpasana Seed Secondary School in Kakumiro, which has no fence, lost 20 computers from its laboratory, and Budongo Seed Secondary School in Masindi lost 16 of its 28 computers through theft. At Musiitwa Nazigo, the long distances that learners walk affected attendance.

Works, deliveries and installation also held back some services. Kigumba Town Seed Secondary School in Kiryandongo reported that construction took over two years against a six-month programme; section 4.3.1 presents the facilities whose works were outstanding at the time of the visit. At Katuugo Health Centre III in Luweero, 26 items on the delivery schedule had not yet been delivered by the supplier, and at Anamwany Health Centre III in Amolatar delivery beds had not been assembled because they arrived without their nuts. Training needs came almost entirely from health centres, where staff asked for orientation on the equipment supplied; section 4.5.2 shows how user skills kept some of it idle.

4.8 Summary of findings

At the national level, the ministries, departments and agencies held their UgIFT assets in working order and in use, with ICT equipment making up most of their holdings and value. Engraving differed widely between institutions, and none of the hospital holdings was engraved. The blood banks, presented separately, had most of their assets working, with a few broken down.

At the local governments, 590 of the 629 facilities on the programme list were verified. Most had completed works and were providing services, and the facilities with works outstanding were mainly seed schools. The reconciliation accounted for every programme-list facility, including those that were not UgIFT facilities in practice and the ten that did not exist or were not constructed under the programme.

Across the programme, 94.2% of assets were working and in use. Breakdowns and storage were the main reasons assets were not in use, and clinical equipment and school computers had the highest shares not in use.

Identification and custody need follow-up. Of the verified assets, 22.0% were engraved and 10.4% were properly engraved with the UgIFT marking; the other engraved assets carried another marking only. Some assets had moved between facilities, were held at district stores or had not yet been delivered by suppliers at the time of the visit, and where equipment stood idle the blockers were power, user skills, installation and incomplete buildings.

The assets in the UgIFT asset verification records carry a recorded value of UGX 997,840,855,042 and a net book value of UGX 812,316,492,277. Seed schools and health centres hold most of this value, mainly in buildings, while ICT equipment accounts for most of the value held by the ministries, departments and agencies.

Facilities linked the UgIFT support to better services: 83.5% of health centres and 74.6% of seed schools reported at least one benefit, led by maternity care, access and better learning environments. The same facilities raised power, staffing, space and security as their main gaps. Chapter 5 sets out the actions that follow from these findings.

5 Recommendations

The verification found that most UgIFT assets were in place and serving their purpose: 221,093 of the 234,613 assets (94.2%) were working and in use, and 590 of the 629 facilities on the programme list were verified on the ground. The next phase should turn these findings into actions that protect assets and improve care, teaching and programme administration. The recommendations in this chapter address the gaps that remain between delivery and use: the 13,520 assets (5.8%) not in use, the 115 verified facilities with works outstanding, the 78.0% of verified assets not engraved and the practices that keep assets in service. Each recommendation first sets out the finding it answers, with its figure, and then the action and the institutions responsible.

The recommendations begin with maintenance, which applies to every asset, and end with the actions for individual facilities. Where a finding differs by level, national institutions are covered first, then the blood banks and then local governments. Accounting Officers should use the priority action plan in Table 22 to assign responsibility, agree resources and check completion, and Table 23 sets out the recommended action for individual facilities where the field visits identified a specific need or a practice to sustain.

5.1 Maintenance and repairs

Maintenance keeps UgIFT assets working for the services they were bought to support. Most of the verified assets are furniture, clinical equipment and computers in daily use at health centres and seed schools, where wear and breakage are to be expected. Routine checks, a record of faults and a dependable route for repair decide whether a broken item returns to use quickly or stays out of service. During the verification, each facility was asked how it maintains, repairs, services or replaces UgIFT assets and whether it keeps a regular record of their functionality or breakdown.


Repair arrangements. Of the 469 facilities that described their maintenance arrangements, 260 (55.4%) met repairs at facility level, from their own funds or with their own staff. Health centres named Primary Health Care funds (94 of 278, 33.8%), while schools named the capitation or Universal Secondary Education grant, parents' contributions or the school budget (52 of 191, 27.2%). Busaale Health Centre III in Kayunga used Primary Health Care funds for repairs, and Kagumba Seed Secondary School in Kamuli had repaired broken furniture during the second term. A facility could describe more than one arrangement.

Support from outside the facility was cited by 151 facilities (32.2%): district offices, mainly the District Health Officer, 84 (17.9%); regional referral hospital workshops or national teams 52 (11.1%); hired technicians and artisans 27 (5.8%); and contractors or suppliers under defects liability, guarantee or warranty 12 (2.6%). Major medical equipment repairs depended on this support. Todora Health Centre III in Nwoya worked through the District Health Officer and the Gulu Regional Referral Hospital technical team, Avogera Health Centre III in Buliisa received support from Hoima Regional Referral Hospital, and Bundimulangya Health Centre III in Bundibugyo obtained a team through the District Health Officer.

In all, 97 facilities (20.7%), 59 of them schools, had not yet needed maintenance because the assets were new, not yet handed over or the buildings were still under construction, and 36 (7.7%) reported no repair arrangement, with broken items set aside or not repaired. Funds for maintenance and repair were reported as insufficient, particularly for major repairs, by 32 of the 505 facilities that described maintenance or challenges (6.3%). At Kyankaramata Health Centre III in Kyenjojo, Primary Health Care funds met minor repairs, but the cost of major repairs was a constraint.

Figure 79 compares these arrangements at health centres and seed schools. Health centres relied more on outside technical support (41.0% of health centres against 19.4% of schools), while schools more often had not yet needed maintenance (30.9% against 13.7%).

Most facilities met repairs from their own funds or staff

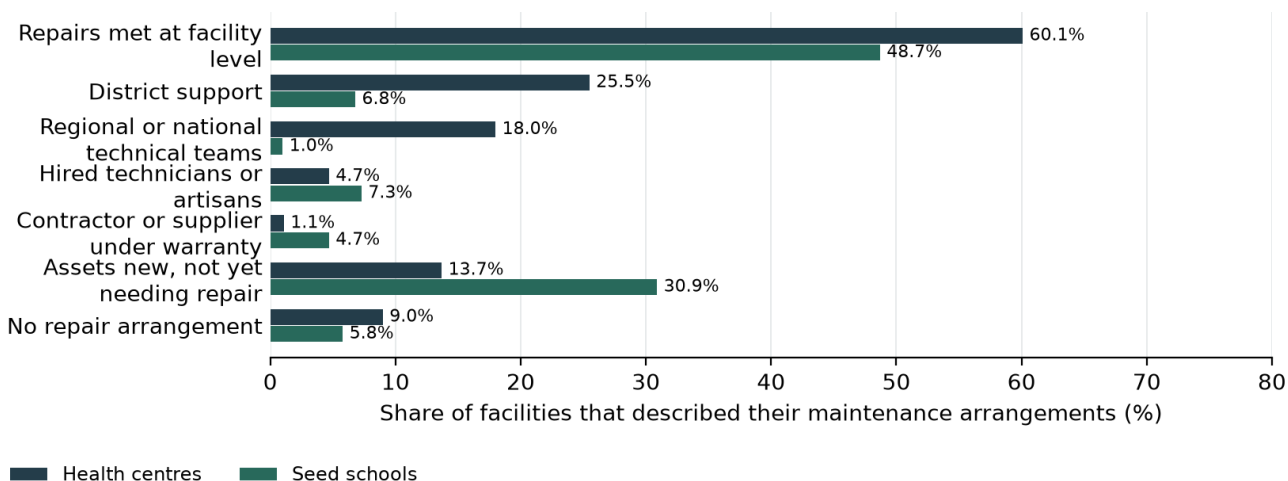


Source: Facility interviews during verification (maintenance question).

Figure 79: Most facilities met repairs from their own funds or staff

Frequency. Few facilities worked to a fixed maintenance interval. Of the 494 programme-list facilities that described how they maintain UgIFT assets or check their condition, 50 (10.1%) did so at a fixed interval. Of these 50, 14 (28.0%) worked annually, 11 (22.0%) monthly, 10 (20.0%) quarterly, 9 (18.0%) every school term, 3 (6.0%) twice a year and 3 (6.0%) weekly or daily, as Figure 80 shows. A further 18 facilities (3.6%) described routine or scheduled servicing without a set interval, mostly scheduled visits by regional referral hospital maintenance teams, and 62 (12.6%) repaired items as the need arose. Ngwedo Seed Secondary School in Buliisa engaged a caretaker every month and used the Directorate of Industrial Training for furniture repairs, while Busaale reviewed asset condition every quarter.

Annual, monthly and quarterly checks were the most common stated intervals

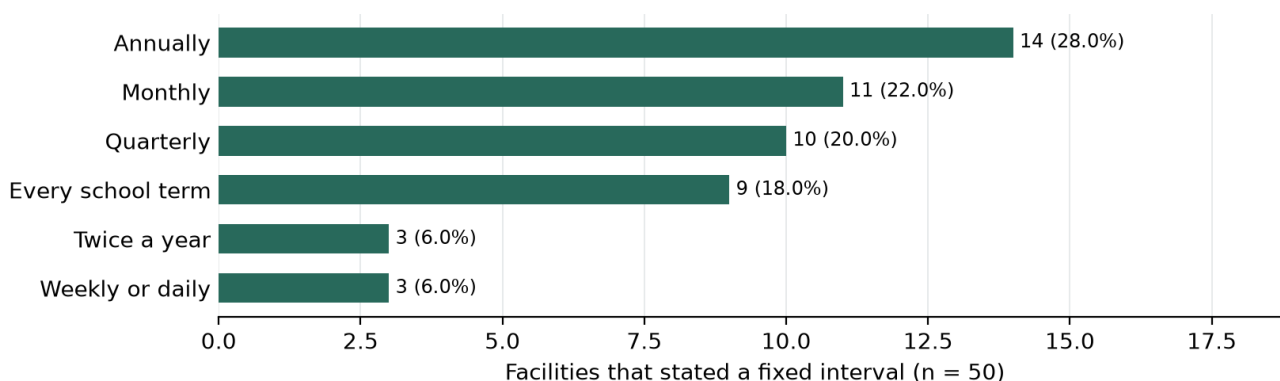

Source: Facility interviews during verification (maintenance and condition-record questions).

Figure 80: Annual, monthly and quarterly checks were the most common stated intervals

Records. Of the 463 facilities that answered, 318 (68.7%) kept a regular record of asset functionality or breakdowns, 36 (7.8%) kept a partial or informal record, 80 (17.3%) kept none and 29 (6.3%) had not yet started because the assets were new or the facility was not yet operating. Of the 478 facilities that answered, 355 (74.3%) held a record of the UgIFT assets they received, 40 (8.4%) held a partial record, such as delivery notes only or a general register that does not identify UgIFT items, and 83 (17.4%) held none. Kagumba Health Centre III in Kamuli kept an asset condition book, a simple practice that other facilities can adopt.

Recommendation. Facility managers and school governing bodies should keep the local and regional repair arrangements that already work and adopt a fixed routine: a condition check at least every school term in schools and every quarter in health centres, and a full count of UgIFT assets each year. Each facility should keep a condition book or fault list naming each item requiring action, the responsible person and the agreed completion date; the 36 facilities with no repair arrangement and the 80 with no functionality or breakdown record should set these up first.

District health and education offices should review unresolved repairs each quarter and arrange technical assistance, and regional referral hospital workshops should include UgIFT equipment in their scheduled visits. Annual maintenance plans should separate minor repairs, which facilities can meet from Primary Health Care funds or school grants, from specialist and major repairs that need district or national funding, as the experience at Kyankaramata shows, and their costs should be included in the next budget cycle. A repair should count as complete only when the item has been checked and returned to safe use, or formally assigned another outcome.

5.2 Restore safe operation

Finding. Of the 234,613 assets, 13,520 (5.8%) were not working and not in use. Of these, 3,392 (25.1%) were broken down, damaged or obsolete, at 183 facilities, and a further 1,114 (8.2%) were recorded as not functional. At national level, the ministries, departments and agencies had 20 assets (0.1%) not in use, three of them laptops at the Office of the Prime Minister recorded as damaged, and the hospitals recorded all 8,099 of their assets as working. The blood banks had 24 assets (3.8%) not in use, including six blood pressure machines at Arua Regional Blood Bank recorded as damaged or not functional. In local governments, 5,685 assets at health centres (8.9%) and 7,791 at seed schools (5.4%) were not in use. Of the assets broken down, 2,722 were at 68 seed schools and 660 at 112 health centres, and school furniture accounted for 2,462 (72.6%), mainly chairs, desks and stools.

Some damaged items remained in use or presented a risk. A cracked laboratory stool was still in use at Sikuda Seed Secondary School in Busia, a broken water-tank stand presented a threat to students at Wadelai Seed Secondary School in Pakwach, and staff at Nyamarunda Health Centre III in Kibaale raised concerns about the electrical installation. Table 23 sets out the action recommended at each of these facilities.

Recommendation. Facility managers, district health and education officers, engineers and technical teams should prioritise unsafe furniture, electrical concerns and failed equipment needed for essential services. Withdraw unsafe items, obtain technical assessments and verify safe operation after repair. The broken down and not functional assets should be assessed in order of their effect on care and teaching, beginning with clinical equipment and the school furniture that makes up most of the broken down assets; items beyond economic repair should receive a formal disposal decision. At national level, the Office of the Prime Minister should decide on repair or replacement of its three damaged laptops, and Uganda Blood Transfusion Services (UBTS) should repair or replace the six broken blood pressure machines at Arua Regional Blood Bank. Keep damaged assets separate from usable assets awaiting installation so that each receives the appropriate action.

5.3 Complete works and bring stored assets into use

Finding. Of the 590 facilities verified, 475 (80.5%) had completed works and 115 (19.5%) had works outstanding: 27 health centres (7.8% of those verified) and 88 seed schools (36.2%). Of the 115, 63 were already providing services, while 24 verified facilities, 21 of them seed schools, were not yet providing services; 22 of these 24 had works outstanding. At Ndhew and Mamba Seed Secondary Schools in Nebbi, unfinished buildings delayed installation: science equipment was held at district headquarters, and Mamba accommodated its computers in older structures.

Of the 13,520 assets not in use, 3,200 (23.7%) were in storage at 181 facilities, 164 health centres and 17 seed schools; at national level the asset records place no assets in storage, although the field teams observed furniture

left in a former MoFPED store and equipment kept in the Hoima blood bank stores (sections 4.1.1 and 4.2). Of the stored assets, 190 (5.9%) were waiting for power, 80 (2.5%) for a building or room and 141 (4.4%) were held at district stores or another facility, while 519 (16.2%) were described as new, boxed or in good condition. More widely, 1,324 assets not in use (9.8%), at 79 facilities, were waiting for power (331, 2.4% of assets not in use), a building or room (483, 3.6%), installation or assembly (493, 3.6%), trained users (16) or staff (1), and a further 97 (0.7%) lacked accessories, parts or consumables.

Facility accounts point to the same blockers. Of the 477 facilities that described services and challenges, 156 (32.7%) reported idle or unusable equipment: 71 of these (45.5%) linked it to power, 32 (20.5%) to installation and 27 (17.3%) to incomplete buildings or lack of space. Lungulu Seed Secondary School in Nwoya kept computers boxed in store pending a power connection, and at Nansanga Seed Secondary School in Budaka 27 of 28 desktop computers remained packed for lack of reliable power.

Recommendation. District Accounting Officers, engineers, health and education officers and contractors should coordinate outstanding buildings, utilities, furniture and equipment through site-specific completion plans for each of the 115 facilities with works outstanding, starting with the 22 of them that were not yet providing services. Installation should follow confirmation that rooms, power, water and security are ready. Stored assets described as new or in good condition should be issued to the rooms where they are needed, and each asset waiting for power or installation should have a named date for connection and testing. Protect services already operating during construction, and complete testing and signed handover before closing each action.

5.4 Equip staff to operate and maintain assets

Finding. Skills and staffing limited the use of equipment most at health centres. Of the 156 facilities that reported idle or unusable equipment, 52 (33.3%) linked it to staff being unable to operate the equipment; 51 of these were health centres, 45.9% of the 111 health centres reporting idle equipment. Training or skills to operate equipment was raised as a gap by 85 facilities (17.8%), 82 health centres (28.9%) and 3 seed schools (1.6%), and 61 facilities (12.8%) asked for training or orientation on the equipment. Staffing was raised by 154 facilities (32.3%), and 9 of the facilities with idle equipment (5.8%) had no personnel or specialist to use it.

At Bubago Health Centre III in Kamuli, staff needed training to operate and maintain an oxygen concentrator. At Sop Sop Health Centre III in Tororo, much of the equipment remained in store because staff did not know how to operate it, and Avogera Health Centre III asked for user orientation and technical skills.

Recommendation. District health officers, facility managers, suppliers and regional technical teams should provide practical training for staff who use specialist equipment, starting with the health centres that linked idle equipment to a lack of skills, including oxygen equipment users at Bubago and Sop Sop and staff requiring orientation at Avogera. Handover should include a demonstration, basic maintenance guidance and a named route for technical support. Future supply contracts should make on-site demonstration to the staff who will use the equipment a condition of acceptance, and staffing reviews should take account of the equipment each health centre now holds.

5.5 Strengthen identification and custody

Finding. Of the 224,705 verified assets (movable assets, excluding buildings, structures and land), 49,463 (22.0%) were engraved and 175,242 (78.0%) were not engraved. Only 23,440 (10.4% of verified assets) were properly engraved with the UgIFT marking; 26,023 (11.6%) were not properly engraved, carrying another marking only, such as a school, district or ministry code without the programme identifier. At national level, the ministries, departments and agencies had engraved 4,849 of 15,609 verified assets (31.1%) and 96.6% of their computers; the Ministry of Education and Sports accounted for 10,325 of the 10,760 MDA assets not engraved: 9,324 Teacher Effectiveness and Learners Assessment (TELA) handsets and 1,001 tablets. None of the 7,745 verified assets held

by hospitals was engraved. The blood banks had engraved 43 of 605 (7.1%), health centres 9,446 of 62,071 (15.2%) and seed schools 35,121 of 138,671 (25.3%), of which 20,260 carried a school or other marking only.

The custody findings concern assets held away from the facility or still in delivery. Of the assets not in use, 2,522 (18.7%) were in this position: 985, mainly furniture for five seed schools, had not yet been delivered by the suppliers, who were still finishing them; 703 had not yet been received at 98 facilities; 159 were held at district stores or another facility; and 675 were not at the facility at the time of the visit. The last group includes 12 desktop computers and four uninterruptible power supply (UPS) units whose location the Ministry of Works and Transport was tracing. A further 525 assets (3.9%), 515 of them at seed schools, were reported stolen, lost or missing, and 45 were kept in store because of insecurity.

Equipment from Bumunji, Buwembe and Majanji health centres in Busia had been transferred to Masafu General Hospital, and equipment intended for Todora in Nwoya had gone to Paraa during construction. Security or fencing was raised as a gap by 130 facilities (27.3%), and 42 facilities (8.8%) themselves asked for assets to be engraved and asset registers kept.

Recommendation. Institution asset managers and district finance, health and education offices should engrave verified movable assets with the UgIFT marking and confirm their locations and custodians, starting with hospital equipment, the Ministry of Education and Sports handsets and tablets, and the Lungulu holdings. Assets carrying another marking only should receive the programme identifier at their next check. Resolve the continuing allocation of equipment at Todora, Paraa and Masafu through signed transfer or receipt documentation, bring assets held at district stores to their facilities once rooms are ready, and complete delivery of the items still with suppliers.

The Ministry of Works and Transport should complete the tracing of the 12 desktop computers and four UPS units and confirm their custodians. Losses should be reported and investigated under the public finance rules, and every facility should hold a list of the UgIFT assets it received, showing each item, its engraving and its custodian. Maintain site, ownership and handover records for buildings and land.

5.6 Resolve programme-list inconsistencies

Finding. All 629 facilities on the programme list were accounted for, and 590 (93.8%) were verified on the ground. Table 12 shows that 55 programme-list entries differed from what the teams found: 10 facilities (1.6%) did not exist or were not constructed under the programme, 4 had been replaced by another facility, 30 operated under another name, 3 were not UgIFT beneficiaries, 3 had their assets relocated to another facility and 5 existed with no UgIFT assets. In all, 18 facilities (2.9% of the programme list) were not UgIFT facilities in practice, including the 10 that do not exist.

The programme list also recorded 44 facilities as complete where works were outstanding in the field, and 4 as ongoing where works were complete. Teams found a further 24 facility names outside the programme list, of which Rukoki General Hospital, Silumira Health Centre III and Bukuuku Community Seed Secondary School were confirmed as additional beneficiaries.

Recommendation. The Ministry of Finance, Planning and Economic Development, with the Ministry of Health, the Ministry of Education and Sports and the local governments concerned, should approve a corrected programme list. It should remove or annotate the 18 entries that were not UgIFT facilities in practice, with the reason for each change; link the 4 replaced and 30 renamed entries to one facility identifier, keeping the former names as aliases; record the 3 relocations with signed transfers and receipts; correct the construction status of the 48 entries that differed from the field; and add the 3 confirmed additional beneficiaries. The other 21 names found outside the programme list should be resolved through the same checks of identity, programme approval and asset custody. The corrected list should then guide decisions wherever planned locations differed from what teams found. Appendix F lists every facility concerned.

5.7 Plan for continued service delivery

Finding. The assets are supporting services: 520 of the 590 verified facilities (88.1%) were providing services. Of the 284 health centres that described the effect of UgIFT support, 237 (83.5%) reported a benefit, including improved maternity and delivery services at 117 (41.2%); of the 193 seed schools, 144 (74.6%) did so, including a better learning environment at 74 (38.3%) and improved access to secondary education at 59 (30.6%). The gaps raised most often were power (200 facilities, 41.9%), staffing (154, 32.3%), space or infrastructure (151, 31.7%), security or fencing (130, 27.3%), repair and maintenance support (106, 22.2%), staff housing (105, 22.0%) and water supply (96, 20.1%).

Kagumba Health Centre III needed staff housing and outpatient, laboratory, storage and kitchen space; Pamaka Health Centre III in Nebbi reported staffing pressure; Kigorobya Seed Secondary School in Hoima was constrained by teaching staff and study materials; and attendance at Musiitwa Nazigo Seed Secondary School in Kayunga was affected by long walking distances. Facilities also asked to take part in planning and procurement (37 facilities, 7.8%) and for quality and specifications to be checked before delivery (48, 10.1%).

Recommendation. Districts and sector ministries should review staffing, operating funds, clinical and teaching space, consumables and utilities alongside asset needs, taking power, staffing and space first as the gaps most often raised. The first round of follow-up should go to actions that restore or expand a service using assets already supplied: reliable electricity, completion of classrooms and laboratories, repair of maternity buildings, practical equipment training and return of damaged furniture to safe use. Future deliveries should follow confirmation of facility readiness, with facility managers involved in planning and in checking specifications before equipment is accepted. Managers should report progress through rooms opened, assets installed, repairs completed and staff able to operate equipment, using the proposed timeframes and evidence of completion in Table 22.

5.8 Priorities for follow-up

The first priority is to make unsafe items and installations safe and restore equipment needed for care and teaching. The next is to complete works, provide utilities and install assets that can then be used. Engraving, custody checks and routine servicing should form part of the same follow-up, with responsibility assigned to the institution and its supervising office.

Future delivery plans should confirm the room, power, water, storage and staff requirements before equipment arrives. Facility managers should take part in that planning, as recommended at Kyankaramata and Avogera. Table 22 sets out eight priority actions with proposed owners, timing and evidence of completion. The timeframes are proposed from approval of this report; Accounting Officers should assign responsible staff and track each action to completion.

Table 19: Priority actions to protect assets and restore service

Priority	Action	Responsible institution	Proposed timing	Evidence of completion
1	Withdraw damaged furniture that presents a safety concern, inspect the electrical concerns at Nyamarunda Health Centre III, and assess the failed solar and oxygen equipment arrangements at Pamaka Health Centre III. Assess the 3,392 assets recorded as broken down, damaged or obsolete, starting with essential clinical equipment and unsafe school furniture.	Facility managers, district health and education officers, district engineers and regional medical equipment technical teams	Inspect within 30 days of report approval; complete minor corrective work within 60 days.	Unsafe items withdrawn; signed technical assessment; repair record and demonstration of safe operation.

Priority	Action	Responsible institution	Proposed timing	Evidence of completion
2	Agree completion plans for Got Apwoyo, Ndheh, Mamba and Butungama seed secondary schools and the other facilities among the 115 verified with works outstanding (27 health centres and 88 seed schools). Coordinate the remaining works, utilities, furniture and equipment installation; protect ongoing equipment use at Atego Seed Secondary School.	District Accounting Officers, district engineers, district education officers, contractors and Ministry of Education and Sports, with the Ministry of Health for health centres	Agree site-specific completion plans within 30 days; track progress monthly against the approved dates.	Schedule of outstanding works; approved completion dates; inspection and handover documents; classrooms or laboratories opened for their intended use.
3	Provide the power required at Lungulu Seed Secondary School, assess and install the boxed equipment at Kalemungole Health Centre III, and assess the repair needs of stored items at Avogera Health Centre III. Review the 3,200 assets in storage at 181 facilities and the 1,324 assets waiting for power, a building, installation or trained users. Keep damaged and usable stored items on separate action lists.	District health and education officers, facility managers, electrical contractors and regional technical teams	Confirm readiness and actions within 30 days; complete installation within 90 days where rooms and utilities are ready.	Equipment location check; power and installation sign-off; named custodian; practical demonstration and date first used.
4	Repair the roof, doors and solar system at Busaale Health Centre III, arrange the major repair support needed at Kyankaramata Health Centre III, assess the three damaged laptops at the Office of the Prime Minister and repair or replace the six broken blood pressure machines at Arua Regional Blood Bank.	Facility managers, district health officers, district engineers and the responsible national institution asset managers	Agree priority work within 30 days and complete funded repairs within 90 days.	Approved repair list; work orders; repairs checked and assets returned to use or assigned a formal disposal decision.
5	Provide practical operation and basic maintenance training for oxygen equipment users at Bubago Health Centre III and Sop Sop Health Centre III and the staff requiring equipment orientation at Avogera Health Centre III, then extend it to the 52 facilities that linked idle equipment to a lack of skills.	District health officers, facility in-charges, suppliers and regional medical equipment technical teams	Complete initial training within 60 days and review use after a further 30 days.	Training attendance by role; practical demonstration of equipment use; named technical support contact.
6	Engrave the 175,242 verified assets that are not engraved (78.0%), starting with the identified Lungulu holdings and hospital equipment; add the UgiFT marking to the 26,023 assets carrying another marking only; and confirm the final allocation of transferred equipment at Todora, Paraa and Masafu.	Institution asset managers, facility managers and district finance, health and education offices	Confirm allocation within 30 days and complete priority engraving and custody checks within 90 days.	Readable engraving; item-to-custodian match; signed transfer or receipt and agreed final location.
7	Retain the functioning local and regional repair arrangements and prepare annual maintenance plans that separate minor repairs from specialist work, starting with the 36 facilities (7.7%) that reported no repair arrangement. Review unresolved faults each quarter.	Facility managers, school governing bodies, district health and education officers and national institution Accounting Officers	Prepare plans within 90 days, include costs in the next budget cycle and review quarterly.	Funded maintenance plan; fault list with responsible roles and due dates; service history and closed repair actions.
8	Review supporting clinical space and staffing at Kagumba Health Centre III and Pamaka Health Centre III, teaching staff and materials at Kigorobya Seed Secondary School, and attendance barriers at Musiitwa Nazigo Seed Secondary School. Include power, staffing and space, the gaps most often raised (41.9%, 32.3% and 31.7% of facilities), in future asset planning.	District health and education officers, facility managers and the relevant sector ministries	Complete service-needs reviews within 90 days and include agreed measures in the next planning and budget cycle.	Agreed staffing and space priorities; service or teaching plan; funded actions and periodic review of use.

5.9 Facility findings and recommended actions

Table 23 brings together the facility findings from the field visits and the action recommended for each, grouped by theme: repairs and safety, completion and utilities, installation and skills, custody, service needs, and practices to sustain. The construction cases and programme-list inconsistencies discussed in section 4.3 carry their recommended actions in those tables and are not repeated here.

Table 20: Facility findings and recommended actions

Facility and district	Finding	Recommended action
Repairs and safety		
Busaale Health Centre III, Kayunga	The facility used Primary Health Care funds for maintenance and kept a quarterly condition record, but the maternity roof leaked, door hinges were damaged and the solar battery needed replacement.	Cost and complete the roof, door and battery repairs, then confirm that the affected rooms and solar system are working.
Musiitwa Nazigo Seed Secondary School, Kayunga	The school checked furniture and fittings each term and repaired them when funds allowed; broken furniture remained out of use while funding was arranged.	Prepare a termly repair list and fund repairs in order of their effect on teaching and safety.
Sikuda Seed Secondary School, Busia	Broken desks and a cracked laboratory stool were found, and the cracked stool was still in use. In all, 23 desks were out of use, 21 of them awaiting repair.	Withdraw unsafe furniture from use and repair or replace it before returning it to classrooms or laboratories.
Nyamarunda Health Centre III, Kibaale	The facility identified and set aside broken items and referred them to the District Health Officer. Staff raised concerns about staff-quarter workmanship, electrical installation, drainage, water security and storage.	Carry out a joint engineering and health inspection, make unsafe installations safe and complete the agreed repairs.
Kijuna Health Centre III, Kassanda	The wheelchairs were not functional, and a failed water pump left the facility with inadequate water. Inadequate power also prevented full use of electronic equipment.	Kassanda District should arrange technical assessment and repair of the wheelchairs and pump, restore a dependable power supply and test the affected equipment before returning it to use.
Kyasansuwa Health Centre III, Kassanda	Three computers were completely damaged following unstable power and surges. Poor floor finishes and defective staff bathroom levels were also observed.	Kassanda District should stabilise and protect the electrical supply, assess the three computers for repair or replacement, and correct the floor and bathroom defects under technical supervision.
Alwi Seed Secondary School, Pakwach	The school reported power surges. Nine monitors and 10 system units were not working, as were the server power-backup unit and 20 other power-backup units, and only one of 13 security cameras was functional.	Pakwach District and the school should first assess the electrical supply and protection, then repair or replace failed equipment and test the whole laboratory and camera system before acceptance.
Wadelai Seed Secondary School, Pakwach	The school's 20 desktop computers were working and in use, but a solar fault interrupted use of electrical equipment. One water-tank stand was broken and presented a threat to students.	Restrict access around the damaged tank support pending an engineering assessment, repair the support, and restore and test the solar system.
Kyankaramata Health Centre III, Kyenjojo	Primary Health Care funds paid for minor repairs, but the cost of major repairs was a constraint; 57 assets were not in use, 30 of them recorded as not functional.	Prepare costed technical referrals for major repairs and agree district funding and follow-up.
Completion and utilities		
Ndhew Seed Secondary School, Nebbi	Buildings were incomplete, with computer and science equipment held at district headquarters and furniture not yet installed. Delivery of equipment had not yet produced an equipped school.	Complete the outstanding works and sanitation facilities and coordinate furniture and equipment installation with handover.
Mamba Seed Secondary School, Nebbi	Construction was incomplete. Computers were temporarily accommodated in older structures, while science equipment remained at district headquarters, so the planned laboratory and computer spaces were not ready for full installation.	Complete and commission the buildings, install the equipment and confirm safe operation before formal handover.

Facility and district	Finding	Recommended action
Atego Seed Secondary School, Nebbi	Computers were connected and working in older rooms while construction continued. Staff reported power surges, and the planned facilities were not fully commissioned.	Stabilise the power supply, protect the installed computers and finish the remaining works.
Butungama Seed Secondary School, Ntoroko	The school was still under construction at the time of the interview.	Confirm the outstanding works with the district engineer and agree the completion and handover sequence.
Muhula Seed Secondary School, Butaleja	The contractor had not handed over the school, and it was not operating. Buildings showed cracks, an air conditioner remained boxed with a missing fan and the installed water pump was not working; 120 desks and 20 desktop computers were new and not yet in use.	Butaleja District and the Ministry of Education and Sports should agree a defects and handover schedule with the contractor, rectify the works, complete the equipment and witness operational tests before handover.
Kihungya Seed Secondary School, Buliisa	The science block, computer laboratory and library were still under construction, and staff quarters were incomplete. The school reported no electricity for computer sessions, no water for sanitation and no perimeter fence; its administration block was already in use.	Buliisa District and the Ministry of Education and Sports should use one completion plan for the laboratories, staff housing, electricity, water and security, with separate testing and handover of each finished element.
Lungulu Seed Secondary School, Nwoya	The school funded minor repairs and kept breakdown information, but computers remained in storage pending power. The stored equipment included defective desktop units, and the assets were not engraved.	Provide a suitable power connection, repair defective units, install the usable equipment and engrave the assets with the UgIFT marking.
Nansanga Seed Secondary School, Budaka	The school lacked reliable power, and 27 of its 28 desktop computers remained packed.	Budaka District and the school should settle the power connection or a suitable alternative, arrange installation and testing, and confirm the number of computers available to learners.
Rupa Seed Secondary School, Moroto	The school hired a generator for practical lessons and used its library and computer laboratory block as dormitories; 58 assets, including 26 UPS units and 25 desktop sets, were not in use for lack of power.	Agree a room-use plan and power solution that restores the library and computer laboratory functions.
Pamaka Health Centre III, Nebbi	Staff reported increased attendance and community confidence, but the solar system was not working, oxygen equipment could not be used because of power constraints, and staffing was under pressure.	Restore reliable power and demonstrate oxygen equipment operation; review staffing against patient demand.
Kikandwa Health Centre III, Kassanda	Electronic equipment could not be used because reliable electricity and solar power were unavailable. Storage for damaged assets was inadequate, the facility lacked a perimeter fence, and defects were observed in flooring and skirting.	Kassanda District should agree a joint power, security and defects plan, provide secure temporary storage, and have technical staff verify repairs and equipment operation.
Installation and skills		
Kalemungole Health Centre III, Moroto	Neonatal respiratory equipment remained in an unopened carton and treatment trolleys were still wrapped, so delivered items had not been brought into routine use.	Check the equipment, confirm the room and staff requirements, and arrange installation and user orientation.
Bubago Health Centre III, Kamuli	Staff identified difficulty operating and maintaining an oxygen concentrator.	Arrange practical user training and a technical check, then demonstrate operation with the staff responsible for the equipment.
Sop Sop Health Centre III, Tororo	Much of the equipment remained in store because staff did not know how to operate it, and oxygen equipment had arrived without cylinders. Tuberculosis testing and maternity services had nevertheless improved.	Tororo District and the Ministry of Health should arrange practical training at the facility, confirm the required oxygen components, and check that trained staff can safely use each released item.
Butiaba Health Centre III, Buliisa	The hydraulic delivery bed was not in use because staff needed operating guidance, and staff had difficulty obtaining test strips for the supplied glucometers. In all, 41 assets, mostly instrument sets, kits and hollow ware, were kept in store.	Demonstrate safe operation of the delivery bed with its users, arrange a reliable supply of compatible glucometer strips and issue the stored instrument sets for use.

Facility and district	Finding	Recommended action
Avogera Health Centre III, Buliisa	The facility carried out local repairs and received technical support from Hoima Regional Referral Hospital. Items that could not be repaired remained stored, and staff identified technical skills, user orientation and storage needs.	Assess the stored items for repair, give practical user training and agree a suitable storage arrangement.
Bunamono Health Centre III, Bududa	The water tank was not working and the solar pump was not connected, leaving the staff houses without water. A supplied laboratory stand remained boxed because staff could not assemble it, and a glucometer lacked test strips.	Bududa District should complete and test the water connection, arrange assembly and user demonstration for the laboratory stand, and establish a supply of compatible glucometer strips.
Custody		
Bumunji, Buwembe and Majanji Health Centres III and Masafu General Hospital, Busia	Equipment had been transferred from the health centres to Masafu General Hospital, so allocation and custody required confirmation.	Confirm the receiving custodian, location and service need, and retain signed transfer and receipt documentation.
Todora and Paraa Health Centres III, Nwoya	Todora used the regional technical maintenance team, while some equipment originally intended for Todora remained at Paraa after redirection during construction.	Confirm the service need at both facilities, formally allocate or transfer the equipment and update the named custodians.
Kihungya Health Centre III, Buliisa	Staff reported more room for patients, easier working arrangements through staff accommodation and electricity from the new solar power house. A gas stove, electric suction apparatus, laboratory stool and electric centrifuge were held at the subcounty rather than the health centre.	Preserve the working building and solar arrangements, confirm who holds the equipment kept at the subcounty and agree whether it should be deployed to the health centre.
Service needs		
Kagumba Health Centre III, Kamuli	Staff reported increased maternity and antenatal service use. Staff housing was under pressure, and outpatient, laboratory, storage and kitchen space were identified as needs.	Assess the supporting space against patient demand and include the agreed works in the district health investment plan.
Musiitwa Nazigo Seed Secondary School, Kayunga	The school improved access to secondary education and used irrigation equipment for teaching and food production, but long walking distances and pupils' engagement in petty trade affected attendance.	Maintain the practical teaching equipment and work with parents and the district education office on attendance barriers.
Kigorobyia Seed Secondary School, Hoima	Equipped classrooms, the computer room and chemistry laboratory supported teaching, and the school and ministry shared maintenance work. Staffing and study materials constrained use of the improved facilities.	Review teaching staff and materials alongside the maintenance plan.
Practices to sustain		
Lukale Health Centre III, Buvuma	Staff reported that the maternity ward allowed women to give birth locally, instead of crossing water, and with greater privacy.	Protect the service through routine care of the maternity building and equipment.
Kagumba Seed Secondary School, Kamuli	Broken furniture had been repaired during the second term. The school also held 17 UPS units needing repair or replacement.	Continue condition checks and scheduled furniture repairs before each term, and assess the 17 UPS units for repair or replacement.
Ngwedo Seed Secondary School, Buliisa	A caretaker attended monthly for repairs, and the Directorate of Industrial Training repaired furniture.	Continue the repair schedule and record the items returned to use.
Bundimulangya Health Centre III, Bundibugyo	The District Health Officer arranged maintenance support, and staff said the power house and solar installation supported continued operation. In all, 15 items were faulty, including 10 office chairs delivered without some parts.	Keep the technical referral arrangement active, include the power and solar systems in routine servicing and follow up the incomplete chairs with the supplier.

6 Conclusion

This report brings together information on 234,613 assets verified across programme administration, health care and education, at ministries, departments and agencies, hospitals, the regional blood banks and local government health centres and seed schools. Of the 629 facilities on the programme list, 590 were verified on the ground and every facility was accounted for through verification or reconciliation. Most assets were working and in use, and facility accounts show benefits including care closer to communities, safer deliveries, improved teaching spaces and equipment supporting daily services.

The findings also show why delivery alone does not secure the intended benefit. Unfinished buildings, unreliable power and water, stored equipment, repair needs and limited user skills kept some assets from being used as intended, and most verified assets were not engraved. These findings call for coordinated action at national, district and facility levels, with clear responsibility for completion, installation, custody and maintenance.

The priority is to protect services already operating and bring the remaining assets into safe, intended use. The recommendations and the priority action plan provide a basis for that follow-up. Progress should be judged by functioning facilities, equipment in use, completed repairs and accountable custody. Sustained maintenance and provision for operating needs will help preserve the programme benefits for the communities it serves.

Appendices

Appendix A Summary count schedule

The summary schedule brings the asset counts, facility coverage and reconciliation outcomes together by institution group, following the order of the findings: ministries, departments and agencies (MDAs) and hospitals at national level, then blood banks, then the health centres and seed schools of the local governments. Each asset is counted once. Table 24 gives the full schedule; the total column covers all 234,613 assets, including four transport assets held by district offices.

Table 21: Summary count schedule by institution group

Measure	MDAs	Hospitals	Blood banks	Health centres	Seed schools	Total
Assets	16,902	8,099	626	63,606	145,376	234,613
Verified assets (engraving base)	15,609	7,745	605	62,071	138,671	224,705
Engraved	4,849	0	43	9,446	35,121	49,463
Properly engraved (UgIFT marking)	4,736	0	26	3,817	14,861	23,440
Not properly engraved (other marking only)	113	0	17	5,629	20,260	26,023
Not engraved	10,760	7,745	562	52,625	103,550	175,242
In use	16,882	8,099	602	57,921	137,585	221,093
Not in use	20	0	24	5,685	7,791	13,520
Broken down, damaged or obsolete	4	0	6	660	2,722	3,392
In storage	0	0	0	2,681	519	3,200
Working	16,882	8,099	602	57,921	137,585	221,093
Not working	20	0	24	5,685	7,791	13,520
MDAs and blood banks visited	15	-	3	-	-	18
Facilities on the programme list	-	-	-	371	258	629
Facilities verified	-	-	-	347	243	590
Facilities with works completed	-	-	-	320	155	475
Facilities with works not completed	-	-	-	27	88	115
Facilities providing services	-	-	-	327	193	520
Facilities not yet providing services	-	-	-	3	21	24
Programme-list facilities accounted for through reconciliation	-	-	-	24	15	39
Programme-list entries with an inconsistency	-	-	-	27	28	55
Does not exist or was not constructed under the programme	-	-	-	7	3	10
Replaced by another facility	-	-	-	4	0	4
Operates under another name	-	-	-	10	20	30
Not a UgIFT beneficiary	-	-	-	2	1	3
Assets relocated to another facility or held at district	-	-	-	2	1	3
Exists with no UgIFT assets	-	-	-	2	3	5
Ground-return identities outside the programme list	-	-	-	15	9	24

Working and in use coincide in the records: every working asset is in use. Assets broken down, damaged or obsolete and assets in storage are parts of the assets not in use. Facility and reconciliation rows count local government facilities on the programme list; the six rows that follow the 55 entries with an inconsistency set out those entries by outcome. A dash shows that a measure does not apply to the group.

Report-category and register-class totals continue in Appendix B. Programme-list entries that operate under another name or were replaced are counted among the facilities verified under their operating or replacing name, so the reconciliation outcomes are not additive to the facilities verified. The 590 facilities verified and the 39 accounted for through reconciliation make up the 629 facilities on the programme list.

Appendix B Asset totals by category and register class

Table 25 reconciles the report categories to the programme asset count, by institution group. School furniture, held entirely by seed schools, forms the largest category, while most assets held at national level fall under other ICT equipment and other assets.

Table 22: Assets by report category and institution group

Report category	MDAs	Hospitals	Blood banks	Health centres	Seed schools	Total
School furniture	-	-	-	-	109,713	109,713
Other assets	1,555	7,794	338	8,129	19,049	36,865
Clinical equipment	-	-	152	25,960	-	26,112
Clinical furniture	-	-	73	20,139	-	20,212
Other ICT equipment	15,159	83	21	-	587	15,850
School computers and related equipment	-	-	-	-	10,266	10,266
Maternity ward equipment	-	-	-	7,438	-	7,438
Building blocks	5	90	1	1,525	4,839	6,460
School support equipment	-	-	-	-	916	916
Health centre ICT equipment	8	-	27	410	-	445
Other furniture	99	132	11	-	-	242
Vehicles and motorcycles	76	-	3	5	6	94
Total	16,902	8,099	626	63,606	145,376	234,613

The total column includes four transport assets held by district offices. A dash shows that the group holds no assets in the category.

Table 26 preserves the register class distribution used in the government asset records alongside the report categories. Furniture and fittings, medical, laboratory and research appliances and light ICT hardware together account for 85.0% of assets.

Table 23: Assets by register class and institution group

Register class	MDAs	Hospitals	Blood banks	Health centres	Seed schools	Total
Furniture and Fittings	99	132	68	15,726	107,311	123,336
Med Lab Research Appliances	189	7,230	318	36,527	5,261	49,525
Light ICT Hardware	15,149	83	43	126	11,060	26,461
Non Residential Buildings	-	-	1	1,365	6,624	7,990
Electrical Machinery	3	209	19	516	1,699	2,446
Other Structures	5	90	1	345	825	1,266
Residential Buildings	-	-	-	475	646	1,121
Other ICT Equipment	4	-	4	234	491	733

Register class	MDAs	Hospitals	Blood banks	Health centres	Seed schools	Total
Precision Optical Instruments	-	-	-	-	532	532
Plant Machinery	4	68	-	15	351	438
Heavy ICT Hardware	14	-	1	52	214	281
Cycles	48	-	-	5	-	55
Computer Software	30	-	-	-	21	51
Light Vehicles	28	-	3	-	6	39
ICT Network Lines	-	-	-	-	33	33
Sports Equipment	-	-	-	-	30	30
Land	-	-	-	3	14	17
Water Supply Systems	-	-	-	7	6	13
Roads and Bridges	-	-	-	-	11	11
Office Equipment	7	-	-	-	-	7
Road Furniture	-	-	-	2	1	3
Musical Instruments	-	-	-	1	1	2
Other recorded items	1,322	287	168	8,207	10,239	20,223
Total	16,902	8,099	626	63,606	145,376	234,613

The total column includes four transport assets held by district offices. A dash shows that the group holds no assets in the class.

Appendix C Condition and use schedules

Condition and use follow the definitions in section 2.4: each asset is recorded as working or not working, and every working asset is in use. Table 27 supplies the data behind the condition chart in section 4.4 (Figure 28) and, because working and in use coincide, the in-use totals behind the use chart (Figure 29).

Table 24: Working and not working assets by report category

Report category	Working	Not working	Total
School furniture	104,292 (95.1%)	5,421 (4.9%)	109,713
Other assets	35,610 (96.6%)	1,255 (3.4%)	36,865
Clinical equipment	22,642 (86.7%)	3,470 (13.3%)	26,112
Clinical furniture	19,183 (94.9%)	1,029 (5.1%)	20,212
Other ICT equipment	15,807 (99.7%)	43 (0.3%)	15,850
School computers and related equipment	8,777 (85.5%)	1,489 (14.5%)	10,266
Maternity ward equipment	6,918 (93.0%)	520 (7.0%)	7,438
Building blocks	6,302 (97.6%)	158 (2.4%)	6,460
School support equipment	832 (90.8%)	84 (9.2%)	916
Health centre ICT equipment	396 (89.0%)	49 (11.0%)	445
Other furniture	242 (100.0%)	0 (0.0%)	242
Vehicles and motorcycles	92 (97.9%)	2 (2.1%)	94
Total	221,093 (94.2%)	13,520 (5.8%)	234,613

Percentages are shares of the assets in each category.

Table 28 sets out the reasons stated for assets not in use, by institution group. It covers the 13,013 assets not in use with a stated reason, and each asset is counted once under its main reason. Assets that were not at the facility at the time of the visit are shown together: the supplier had not yet delivered them, they had not yet been handed over, or they were held at the district store or elsewhere; at national level, the Ministry of Works and Transport was tracing the location of 16 assets. Hospitals recorded all their assets in use. The table supplies the data behind Figure 65 in section 4.5.2, which discusses the reasons with the utilisation blockers.

Table 25: Stated reasons for assets not in use by institution group

Main reason	MDAs	Blood banks	Health centres	Seed schools	Total	Share of assets not in use
Broken down, damaged or obsolete	4	6	660	2,722	3,392	25.1%
In storage, no other cause given	-	-	2,412	130	2,542	18.8%
Not yet delivered, handed over or held elsewhere	16	-	953	1,553	2,522	18.7%
Functional or in good condition but not in use	-	-	133	1,214	1,347	10.0%
Awaiting power, building works, installation, trained users or staff	-	-	186	1,138	1,324	9.8%
Recorded as not functional	-	-	675	439	1,114	8.2%
Stolen, lost or missing	-	-	10	515	525	3.9%
Other stated reasons	-	18	123	9	150	1.1%
Missing accessories, parts or consumables	-	-	89	8	97	0.7%
Total	20	24	5,241	7,728	13,013	96.3%

Shares are of the 13,520 assets not in use. Hospitals and district offices recorded no assets not in use.

Appendix D Recorded value and net book value schedules

The programme assets have a total recorded value of UGX 997,840,855,042, accumulated depreciation of UGX 185,538,888,776 and net book value of UGX 812,316,492,277 at 30 September 2026. These amounts support the financial handover and are presented separately from the field findings. The valuation basis is set out in section 2.5.

Table 29 gives the values by institution group behind Figure 67.

Table 26: Recorded value and net book value by institution group

Institution group	Assets	Recorded value UGX	Depreciation UGX	Net book value UGX	Share of value
MDAs	16,902	31,967,493,589	19,480,446,057	12,487,047,532	3.2%
Hospitals	8,099	26,080,242,410	22,423,146,484	3,657,095,926	2.6%
Blood banks	626	1,451,584,715	514,105,544	937,479,171	0.1%
Health centres	63,606	259,662,849,164	41,291,859,808	218,378,252,366	26.0%
Seed schools	145,376	678,247,549,426	101,549,907,057	576,704,905,370	68.0%
Local government offices	4	431,135,738	279,423,826	151,711,912	0.0%
Total	234,613	997,840,855,042	185,538,888,776	812,316,492,277	100.0%

Net book value is calculated for each asset as recorded value less accumulated depreciation, with a minimum of zero, before amounts are totalled, so for health centres and seed schools it exceeds the difference between the recorded value and depreciation shown.

Table 30 gives the national schedule: each ministry, department and agency vote, the referral and general hospitals by type, and the three regional blood banks. It supplies the data for Figure 68. Assets held at national level carry a recorded value of UGX 59,499,320,714 and a net book value of UGX 17,081,622,629.

Table 27: National value schedule: MDAs, hospitals and blood banks

Vote or institution	Assets	Recorded value UGX	Depreciation UGX	Net book value UGX
MoES	10,783	14,925,128,359	10,607,476,704	4,317,651,655
MoFPED	458	6,152,854,000	4,272,041,257	1,880,812,743
MoWE	2,939	5,000,313,297	2,089,906,834	2,910,406,463
MAAIF	2,045	2,332,681,629	984,457,129	1,348,224,500
MoH	264	1,216,859,097	463,977,008	752,882,089
MoLHUD	27	829,749,997	124,320,000	705,429,997
MoWT	88	455,932,376	326,484,882	129,447,494
OAG	20	388,773,680	111,591,545	277,182,135
MoLG	13	343,320,450	284,804,160	58,516,290
MoDVA	183	91,162,979	54,612,464	36,550,515
KCCA	51	54,024,515	53,024,515	1,000,000
OPM	10	53,535,300	48,181,770	5,353,530
NEMA	6	46,824,409	32,841,273	13,983,136
MoGLSD	10	46,180,000	13,660,000	32,520,000
PPDA	5	30,153,500	13,066,516	17,086,984
MDAs subtotal	16,902	31,967,493,589	19,480,446,057	12,487,047,532
Regional referral hospitals (17)	4,311	24,338,709,624	21,432,686,298	2,906,023,326
General hospitals (47)	2,883	1,338,616,197	736,898,458	601,717,739
National referral hospitals (4)	905	402,916,589	253,561,728	149,354,861
Hospitals subtotal (68)	8,099	26,080,242,410	22,423,146,484	3,657,095,926
Arua Regional Blood Bank	340	1,132,615,978	456,584,786	676,031,192
Hoima Regional Blood Bank	171	289,651,199	32,398,208	257,252,991
Soroti Regional Blood Bank	115	29,317,538	25,122,550	4,194,988
Blood banks subtotal	626	1,451,584,715	514,105,544	937,479,171
Total	25,627	59,499,320,714	42,417,698,085	17,081,622,629

MoDVA is the Ministry of Defence and Veteran Affairs. Figures in brackets are the number of hospitals of each type. Amounts are rounded to the nearest shilling, so rows may differ from subtotals by UGX 1.

Table 31 gives the values by report category. Building blocks carry 69.9% of the recorded value (UGX 697,270,758,260), followed by school furniture and other assets.

Table 28: Recorded value and net book value by report category

Report category	Assets	Recorded value UGX	Depreciation UGX	Net book value UGX
Building blocks	6,460	697,270,758,260	72,828,873,965	624,441,884,296
School furniture	109,713	94,352,912,507	18,031,685,755	76,328,489,752
Other assets	36,865	87,422,228,712	34,668,706,621	52,753,522,091
Clinical equipment	26,112	32,470,784,325	12,295,098,472	20,175,685,853

Report category	Assets	Recorded value UGX	Depreciation UGX	Net book value UGX
School computers and related equipment	10,266	25,434,940,136	13,385,662,572	12,049,277,564
Other ICT equipment	15,850	24,802,765,320	16,481,113,122	8,321,652,198
Clinical furniture	20,212	16,143,866,049	6,935,224,986	9,215,904,073
Vehicles and motorcycles	94	8,234,135,677	4,963,197,874	3,270,937,803
Maternity ward equipment	7,438	7,419,395,159	3,270,066,317	4,149,328,842
School support equipment	916	2,597,745,705	1,361,724,874	1,236,020,831
Health centre ICT equipment	445	971,807,133	692,463,954	279,343,179
Other furniture	242	719,516,059	625,070,264	94,445,795
Total	234,613	997,840,855,042	185,538,888,776	812,316,492,277

Net book value is calculated for each asset with a minimum of zero before amounts are totalled, so in some categories it exceeds the difference between the recorded value and depreciation shown.

Appendix E Utilisation and identification schedules

Table 32 contains the data behind the identification chart in section 4.5.1 (Figure 38). It covers the 224,705 verified assets: movable assets, excluding buildings, structures and land, which are tracked through property and site records, and excluding accessories and consumables, which were not part of the verification. Properly engraved assets carry the UgIFT marking; not properly engraved assets carry another marking only.

Table 29: Engraving of verified assets by institution group

Institution group	Verified assets	Engraved	Properly engraved	Not properly engraved	Not engraved
MDAs	15,609	4,849 (31.1%)	4,736 (30.3%)	113 (0.7%)	10,760 (68.9%)
Hospitals	7,745	0 (0.0%)	0 (0.0%)	0 (0.0%)	7,745 (100.0%)
Blood banks	605	43 (7.1%)	26 (4.3%)	17 (2.8%)	562 (92.9%)
Health centres	62,071	9,446 (15.2%)	3,817 (6.1%)	5,629 (9.1%)	52,625 (84.8%)
Seed schools	138,671	35,121 (25.3%)	14,861 (10.7%)	20,260 (14.6%)	103,550 (74.7%)
Local government offices	4	4 (100.0%)	0 (0.0%)	4 (100.0%)	0 (0.0%)
Total	224,705	49,463 (22.0%)	23,440 (10.4%)	26,023 (11.6%)	175,242 (78.0%)

Percentages are shares of the verified assets in each group.

Table 33 gives the same measures by report category. Building blocks are identified through property and site records, so engraving does not apply to them. Where a category has fewer verified assets than assets in Table 25, the difference is accessories and consumables, which were not part of the verification, and land.

Table 30: Engraving of verified assets by report category

Report category	Verified assets	Engraved	Properly engraved	Not properly engraved	Not engraved
School furniture	109,713	31,656 (28.9%)	14,405 (13.1%)	17,251 (15.7%)	78,057 (71.1%)
Other assets	33,631	1,923 (5.7%)	420 (1.2%)	1,503 (4.5%)	31,708 (94.3%)
Clinical equipment	26,112	2,824 (10.8%)	1,043 (4.0%)	1,781 (6.8%)	23,288 (89.2%)
Clinical furniture	20,212	3,953 (19.6%)	1,595 (7.9%)	2,358 (11.7%)	16,259 (80.4%)
Other ICT equipment	15,845	4,716 (29.8%)	4,650 (29.3%)	66 (0.4%)	11,129 (70.2%)
School computers and related equipment	10,059	2,445 (24.3%)	310 (3.1%)	2,135 (21.2%)	7,614 (75.7%)

Report category	Verified assets	Engraved	Properly engraved	Not properly engraved	Not engraved
Maternity ward equipment	7,438	1,510 (20.3%)	815 (11.0%)	695 (9.3%)	5,928 (79.7%)
School support equipment	916	140 (15.3%)	4 (0.4%)	136 (14.8%)	776 (84.7%)
Health centre ICT equipment	443	169 (38.1%)	135 (30.5%)	34 (7.7%)	274 (61.9%)
Other furniture	242	63 (26.0%)	63 (26.0%)	0 (0.0%)	179 (74.0%)
Vehicles and motorcycles	94	64 (68.1%)	0 (0.0%)	64 (68.1%)	30 (31.9%)
Building blocks	-	-	-	-	-
Total	224,705	49,463 (22.0%)	23,440 (10.4%)	26,023 (11.6%)	175,242 (78.0%)

Percentages are shares of the verified assets in each category.

Table 34 counts the facilities and units holding at least one asset not in use, in storage or broken down, by institution group. Assets in storage were concentrated at health centres, where 164 of the 354 facilities in the records (46.3%) held assets in storage, compared with 17 seed schools (6.7%). At national level the asset records place no assets in storage; the stored items observed at MoFPED and at the Hoima blood bank are described in sections 4.1.1 and 4.2. Assets broken down, damaged or obsolete were recorded at 183 facilities and units, among them 112 health centres (31.6%) and 68 seed schools (26.7%).

Table 31: Facilities with assets not in use, in storage or broken down by institution group

Institution group	Facilities or units	Any asset not in use	Assets in storage	Assets broken down, damaged or obsolete
MDAs	204	3 (1.5%)	0 (0.0%)	2 (1.0%)
Hospitals	75	0 (0.0%)	0 (0.0%)	0 (0.0%)
Blood banks	6	1 (16.7%)	0 (0.0%)	1 (16.7%)
Health centres	354	255 (72.0%)	164 (46.3%)	112 (31.6%)
Seed schools	255	132 (51.8%)	17 (6.7%)	68 (26.7%)
Local government offices	4	0 (0.0%)	0 (0.0%)	0 (0.0%)
Total	898	391 (43.5%)	181 (20.2%)	183 (20.4%)

Facilities or units are the facilities, hospitals, departments and blood bank entries under which assets are held in the records. Percentages are shares of those in each group.

Appendix F Programme-list reconciliation

Table 35 lists every programme-list entry with an inconsistency, 55 in all, with its local government and the outcome of the reconciliation. Each entry retains its original programme-list name, and the names used by operating and receiving facilities are shown in the outcome. Section 4.3.2 summarises these outcomes.

Table 32: Programme-list entries with an inconsistency

Programme-list entry	Local government	Outcome
Does not exist or was not constructed under the programme (10)		
H070 Busia Eastern Division	Busia MC	Does not exist under the programme
S216 Kishangara seed school	Ibanda	Does not exist under the programme
S012 Central Division	Jinja City	Does not exist under the programme
H010 Butoloogo HC II	Kassanda	Does not exist under the programme
H190 Alik HCII	Lira	Does not exist under the programme
H197 Acimi HC II	Oyam	Does not exist under the programme

Programme-list entry	Local government	Outcome
H195 Acokara HCII	Oyam	Does not exist under the programme
H200 Ariba HC II	Oyam	Does not exist under the programme
H205 Olok HC II	Pader	Not constructed under the programme
S010 Eastern Division	Tororo MC	Does not exist under the programme
Replaced by another facility (4)		
H150 Ngomoromo HC II	Lamwo	Replaced by Pangira Health Centre III
H213 Loinya HC II	Maracha	Replaced by Liko Health Centre III, which is counted under its own programme-list entry
H218 Oweko HC II	Nebbi	Replaced by Pamaka Health Centre III
H354 Musandama HC II	Ntoroko	Replaced by Butungama Health Centre III
Operates under another name (30)		
S011 Igombe	Bugweri	Operates as Mpiita Seed Secondary School
S213 Nsiika T/C	Buhweju	Operates as Ndibarema Memorial Seed Secondary School
H125 Kocheke HC II	Bukedea	Operates as Kangole / Kocheke Health Centre III
S127 Bunambutye Seed School	Bulambuli	Operates as Bumufuni Seed Secondary School
H318 Mantoroba HC II	Bundibugyo	Operates as Busanga Health Centre III
S056 Kabonero	Bunyangabu	Operates as Katugunda Seed Secondary School
S057 Kyamukube Town Council	Bunyangabu	Operates as Nsuura Seed Secondary School
H065 Dabani	Busia	Operates as Buwumba Health Centre III
S065 Maddu Seed School	Gomba	Return submitted as Kyayi Seed School
S230 Buhanika	Hoima	Operates as Kidukuru Seed Secondary School
S112 Butagaya	Jinja	Operates as Buwala Seed Secondary School
S252 Kasenda Seed School	Kabarole	Operates as St Paul Nyabweya Seed Secondary School
H329 Kidubuli HC II	Kabarole	Operates as Iruhura Health Centre III
H332 Nyabuswa HC II	Kabarole	Operates as Nyambuusa Health Centre III
S048 Kagadi	Kagadi	Operates as King Solomon Seed Secondary School
S232 Kiryanga Seed School	Kagadi	Operates as St Catherine Kicucura Seed Secondary School
S049 Ruteete	Kagadi	Operates as Kitegwa Community Seed Secondary School
H292 Kikoola	Kakumiro	Operates as Mukoora Health Centre III
S066 Bufumira Seed School	Kalangala	Operates as Nekemiya Memorial Seed Secondary School
H015 Kyakatebe HC II	Kassanda	Operates as Namabaale Health Centre III
S235 Mugarama (new facilities for St Mugagga S.S)	Kibaale	Operates as St Mugagga Vocational Seed Secondary School
H027 Kagganda HC II	Lwengo	Reconciled to the Mbirizi Seed Secondary School return
S081 Mpumudde seed school	Lyantonde	Operates as Rwamabara Seed Secondary School
S084 Kiringente Seed School	Mpigi	Operates as Wamatovu Seed Secondary School
H036 Kabbo	Mubende	Operates as Nakawala Health Centre III
S086 Kimenyedde Seed School	Mukono	Operates as St Andrews Ndwadde mutwe Seed Secondary School
S122 Mwema Seed School	Namayingo	Operates as Mutumba Seed Secondary School
S103 Pallisa	Pallisa	Operates as Akadot Seed Secondary School
S167 Kadungulu Seed School	Serere	Operates as Kagwara Seed Secondary School

Programme-list entry	Local government	Outcome
H054 Bussi HC II	Wakiso	Bussi is the village name for Zinga Health Centre III, which is counted under its own programme-list entry
Not a UgIFT beneficiary (3)		
H086 Buyinda HC II	Kaliro	Not a UgIFT beneficiary
S237 Kiziranfumbi Seed School	Kikuube	Not a UgIFT beneficiary
H193 Alira HCII	Oyam	Not a UgIFT beneficiary
Assets relocated to another facility or held at district (3)		
S208 Abanga	Zombo	UgIFT assets relocated to Kango Seed Secondary School
H231 Alangi	Zombo	UgIFT assets relocated to Amwonyo Health Centre III
H233 Ther-uru HC II	Zombo	UgIFT assets relocated to Atyak Health Centre III
Exists with no UgIFT assets (5)		
S214 Bumbaire Seed School	Bushenyi	Exists with no UgIFT assets
S215 Kyamuhunga	Bushenyi	Exists with no UgIFT assets
H149 Pandwong HC II	Kitgum MC	Exists with no UgIFT assets
S221 Kashenshero	Mitooma	Exists with no UgIFT assets
H282 Rwamujojo HC II	Sheema MC	Exists with no UgIFT assets

Entries are grouped by outcome; the number of entries in each group is shown in brackets.

Table 36 lists the 24 ground-return identities: facility names found in the field returns that are not on the programme list. They are counted separately from the 629 programme-list facilities. Three of them, marked with an asterisk, are confirmed UgIFT beneficiaries that were not on the programme list. Linked receiving facilities and the separately allocated blood banks remain in their own reconciliation accounts.

Table 33: Ground-return identities outside the programme list

Name	Local government
Arocha Health Centre III	Apac
Kabushaho Seed Secondary School	Bushenyi
Sofia Health Centre III	Busia MC
Buvuma Health Centre III	Buvuma
Bukuuku Community Seed Secondary School *	Fort Portal City
Silumira Health Centre III *	Kakumiro
Bushogye Seed Secondary School	Kanungu
Lokori Seed Secondary School	Karenga
Rukoki General Hospital *	Kasese
Onywako Health Centre III	Lira
Lwengenyi Health Centre III	Lwengo
Odupiri Health Centre III	Maracha
Kitojo Seed Secondary School	Mitooma
Rupa Seed Secondary School	Moroto
Kibuzigye Seed Secondary School	Rubanda
Bikurungu Seed Secondary School	Rukungiri

Name	Local government
Migina Health Centre III	Sheema
Simu Pondo Health Centre III	Sironko
Buloba Health Centre III	Wakiso
Ekaligo Health Centre III	Yumbe
Liko Health Centre III	Yumbe
Lobe Health Centre III	Yumbe
Nyori Health Centre III	Yumbe
Amei Seed Secondary School	Zombo

* Confirmed UgIFT beneficiary that was not on the programme list.

Table 37 lists the 89 verified facilities where works were outstanding, as confirmed in the field returns or the building records, or where services had not yet started. It supports section 4.3.1. Works were outstanding at 86 facilities, 50 of which were already providing services. The 24 facilities not yet providing services include two seed schools whose works were complete and Aleka Seed Secondary School in Oyam, recorded as ongoing on the programme list. The other 28 facilities counted as not completed in section 4.3.1 are recorded as ongoing on the programme list.

Table 34: Verified facilities with works outstanding or not yet providing services

Facility	Local government	Type	Position at the visit
Omot Health Centre III	Agago	Health centre	Main works outstanding; providing services
Bukibologoto Health Centre III	Bulambuli	Health centre	Main works outstanding; not yet providing services
Adagmon Health Centre III	Dokolo	Health centre	Main works outstanding; providing services
Mamba Health Centre III	Gomba	Health centre	Ancillary works outstanding; providing services
Ngomamene Health Centre III	Gomba	Health centre	Ancillary works outstanding; providing services
Maregamo Health Centre III	Kisoro	Health centre	Works outstanding
Benet Health Centre III	Kween	Health centre	Main works outstanding; providing services
Kaptum Health Centre III	Kween	Health centre	Main works outstanding; not yet providing services
Moyok Health Centre III	Kween	Health centre	Awaiting handover by the contractor; providing services
Mutungo Health Centre III	Makindye-Ssabagabo MC	Health centre	Ancillary works outstanding; providing services
Lama Health Centre III	Moyo	Health centre	Main works outstanding; providing services
Matugga Health Centre III	Nansana MC	Health centre	Ancillary works outstanding; providing services
Abwoch Health Centre III	Omoro	Health centre	Main works outstanding; providing services
Tekulu Health Centre III	Omoro	Health centre	Main works outstanding; providing services
Kyamwinula Health Centre III	Tororo MC	Health centre	Main works outstanding; providing services
Amanyiri Health Centre III	Yumbe	Health centre	Main works outstanding; not yet providing services
Alerek Seed Secondary School	Abim	Seed school	Awaiting handover by the contractor; providing services
Kotomor Seed Secondary School	Agago	Seed school	Main works outstanding; not yet providing services
Lamiyo Seed Secondary School	Agago	Seed school	Main works outstanding

Facility	Local government	Type	Position at the visit
Omiya Pacwa Seed Secondary School	Agago	Seed school	Main works outstanding; not yet providing services
Akwon Seed Secondary School	Amolatar	Seed school	Works outstanding; not yet providing services
Looro Seed Secondary School	Amudat	Seed school	Main works outstanding; providing services
Asamuk Seed Secondary School	Amuria	Seed school	Works outstanding
Amuru Town Seed Secondary School	Amuru	Seed school	Awaiting handover by the contractor; not yet providing services
St Peters Aroi Seed Secondary School	Arua	Seed school	Main works outstanding; providing services
Bushiribo Seed Secondary School	Bududa	Seed school	Main works outstanding; not yet providing services
Mpiita Seed Secondary School	Bugweri	Seed school	Main works outstanding; providing services
Senendet Seed Secondary School	Bukwo	Seed school	Main works outstanding; not yet providing services
Kihungya Seed Secondary School	Buliisa	Seed school	Main works outstanding; providing services
Burondo Seed Secondary School	Bundibugyo	Seed school	Main works outstanding; not yet providing services
Kabango Seed Secondary School	Bundibugyo	Seed school	Main works outstanding; providing services
Kisuba Seed Secondary School	Bundibugyo	Seed school	Works outstanding; providing services
Katugunda Seed Secondary School	Bunyangabu	Seed school	Works outstanding; providing services
Nsuura Seed Secondary School	Bunyangabu	Seed school	Main works outstanding; providing services
Muhula Seed Secondary School	Butaleja	Seed school	Main works outstanding; not yet providing services
St Luke Kibibi Seed Secondary School	Butambala	Seed school	Works complete, awaiting commissioning; not yet providing services
Patiko Seed Secondary School	Gulu	Seed school	Works outstanding; providing services
Kidukuru Seed Secondary School	Hoima	Seed school	Awaiting handover by the contractor; providing services
Sidok Seed Secondary School	Kaabong	Seed school	Main works outstanding; not yet providing services
Aperikira Seed Secondary School	Kaberamaido	Seed school	Ancillary works outstanding; providing services
Burora Seed Secondary School	Kagadi	Seed school	Awaiting handover by the contractor
King Solomon Seed Secondary School	Kagadi	Seed school	Main works outstanding; providing services
Kitegwa Community Seed Secondary School	Kagadi	Seed school	Works outstanding; providing services
St Catherine Kicucura Seed Secondary School	Kagadi	Seed school	Works outstanding; providing services
Kapedo Seed Secondary School	Karenga	Seed school	Main works outstanding
Bwesumbu Seed Secondary School	Kasese	Seed school	Main works outstanding; providing services
Lwamata Town Council Seed Secondary School	Kiboga	Seed school	Works outstanding; providing services
Kyangwali Seed Secondary School	Kikuube	Seed school	Awaiting handover by the contractor; providing services
Lake Mburo Seed Secondary School	Kiruhura	Seed school	Works outstanding
Nyakashara Seed Secondary School	Kiruhura	Seed school	Ancillary works outstanding
Kigumba Town Seed Secondary School	Kiryandongo	Seed school	Main works outstanding; providing services
Kanara Seed Secondary School	Kitagwenda	Seed school	Awaiting handover by the contractor; providing services

Facility	Local government	Type	Position at the visit
Rengen Seed Secondary School	Kotido	Seed school	Main works outstanding; not yet providing services
Kumi Seed Secondary School	Kumi	Seed school	Ancillary works outstanding; providing services
Kaptum Seed Secondary School	Kween	Seed school	Main works outstanding; not yet providing services
Kitawoi Seed Secondary School	Kween	Seed school	Main works outstanding; providing services
Moyok Seed Secondary School	Kween	Seed school	Main works outstanding; not yet providing services
Ntwetwe Seed Secondary School	Kyankwanzi	Seed school	Works outstanding; providing services
Rwentuha Seed Secondary School	Kyegegwa	Seed school	Ancillary works outstanding; providing services
Kigaraale Seed Secondary School	Kyenjojo	Seed school	Works outstanding; providing services
Kyarusizi Seed Secondary School	Kyenjojo	Seed school	Ancillary works outstanding
Kyembogo Seed Secondary School	Kyenjojo	Seed school	Ancillary works outstanding
Padibe Seed Secondary School	Lamwo	Seed school	Main works outstanding; not yet providing services
Butta Seed Secondary School	Manafwa	Seed school	Main works outstanding; not yet providing services
Khabutoola Seed Secondary School	Manafwa	Seed school	Main works outstanding; providing services
Sibanga Seed Secondary School	Manafwa	Seed school	Awaiting handover by the contractor; providing services
Sisuni Seed Secondary School	Manafwa	Seed school	Main works outstanding; providing services
Rupa Seed Secondary School	Moroto	Seed school	Ancillary works outstanding; providing services
Dufile Seed Secondary School	Moyo	Seed school	Main works outstanding
Kigando Seed Secondary School	Mubende	Seed school	Ancillary works outstanding; providing services
Moruita Seed Secondary School	Nakapiripirit	Seed school	Main works outstanding; not yet providing services
Nakapiripirit Seed Secondary School	Nakapiripirit	Seed school	Works outstanding; providing services
Mukuto Seed Secondary School	Namisindwa	Seed school	Works outstanding; providing services
Iriiri Seed Secondary School	Napak	Seed school	Awaiting handover by the contractor; not yet providing services
Lopei Seed Secondary School	Napak	Seed school	Works complete and handed over, opening the following year; not yet providing services
Atego Seed Secondary School	Nebbi	Seed school	Main works outstanding; providing services
Mamba Seed Secondary School	Nebbi	Seed school	Main works outstanding; providing services
Ndhew Seed Secondary School	Nebbi	Seed school	Main works outstanding
Ngora Seed Secondary School	Ngora	Seed school	Ancillary works outstanding
Butungama Seed Secondary School	Ntoroko	Seed school	Main works outstanding; providing services
Kibuuku Seed Secondary School	Ntoroko	Seed school	Ancillary works outstanding
Got Apwoyo Seed Secondary School	Nwoya	Seed school	Main works outstanding; not yet providing services
Okum Seed Secondary School	Otuke	Seed school	Main works outstanding; not yet providing services
Aleka Seed Secondary School	Oyam	Seed school	Works recorded as ongoing; not yet providing services
Olok Seed Secondary School	Pallisa	Seed school	Ancillary works outstanding; providing services

Facility	Local government	Type	Position at the visit
Ryakasinga Seed Secondary School	Sheema	Seed school	Main works outstanding
Kamuda Seed Secondary School	Soroti	Seed school	Works outstanding
Atyak Seed Secondary School	Zombo	Seed school	Works outstanding; providing services
Kango Seed Secondary School	Zombo	Seed school	Ancillary works outstanding; providing services

Main works are classroom, laboratory, library, ICT, administration, ward, maternity or outpatient blocks, or the whole facility; ancillary works are staff houses, latrines, toilets, kitchens, placenta pits or incinerators.

Appendix G Asset information for institutional handover

The information prepared for institutional handover covers 234,613 assets: 25,627 held at national level by MDAs, hospitals and blood banks, and 208,986 held by local governments at health centres, seed schools and district offices. Table 38 summarises the information held. It includes asset descriptions, locations, condition, use and custody details, together with available valuation and depreciation information.

Table 35: Asset information prepared for handover

Asset scope	Assets	Information held	Handover purpose
Whole programme	234,613	Identification, location, condition, use, custody and available valuation details.	Institutional accountability, maintenance planning and financial reporting.

Asset identifiers, classifications, identification marks, use and custody details, and available cost and depreciation values support institutional accountability, maintenance planning and financial reporting.

Appendix H Evidence supporting the findings

The findings draw on physical inspection, discussions with facility managers and technical officers, photographs, asset inventories and supervisor reconciliation. Facility examples identify the location, the issue requiring action and its effect on services. Photographs document the condition of selected facilities and assets at the time of the visits.

Service benefits described by facility managers are presented as their experience of the programme. The action plan sets out the recommended next steps and proposed responsibilities.

Appendix I Photographic record of verified assets

The photographs in this appendix record assets verified at health centres and seed schools during the local government fieldwork, and show their condition at the time of the visits. Photographs of works in progress, engraving, storage, damage and services appear with the related findings in chapter 4.

Health centres

Figures 81 to 100 show clinical, maternity and laboratory equipment and furniture at health centres, including an infant radiant warmer, oxygen concentrators and cylinders, delivery beds, autoclaves, a binocular microscope, weighing scales and kangaroo care chairs.



Figure 81: Infant radiant warmer at a health centre, Makindye-Ssabagabo Municipal Council (Buganda)



Figure 82: Oxygen cylinders marked KIBIRI HCIII at Kibiri HC III, Makindye-Ssabagabo Municipal Council (Buganda)



Figure 83: Wooden waiting bench at Kibiri HC III, Makindye-Ssabagabo Municipal Council (Buganda)



Figure 84: Delivery bed and clinical furniture at a health centre, Kabarole District (Tooro)



Figure 85: Oxygen concentrator at Kalemungole HC III, Moroto District (Karamoja)



Figure 86: Suction apparatus at Kalemungole HC III, Moroto District (Karamoja)



Figure 87: Oxygen concentrator at Kamoru HC III, Kotido District (Karamoja)



Figure 88: Instrument trolley with delivery instruments at Kamoru HC III, Kotido District (Karamoja)



Figure 89: Medical-waste bins and ward beds at Butiaba HC III, Buliisa District (Bunyoro)



Figure 90: Laboratory centrifuge at Butiaba HC III, Buliisa District (Bunyoro)



Figure 91: Blood pressure apparatus on a mobile stand at Butiaba HC III, Buliisa District (Bunyoro)



Figure 92: Office chairs at Butiaba HC III, Buliisa District (Bunyoro)



Figure 93: Kangaroo care chair at Kyabasara HC III, Kagadi District (Bunyoro)



Figure 94: Infant weighing scale at Buwembe HC III, Busia District (Bukedi)



Figure 95: Autoclave above a gas cylinder at Buwembe HC III, Busia District (Bukedi)

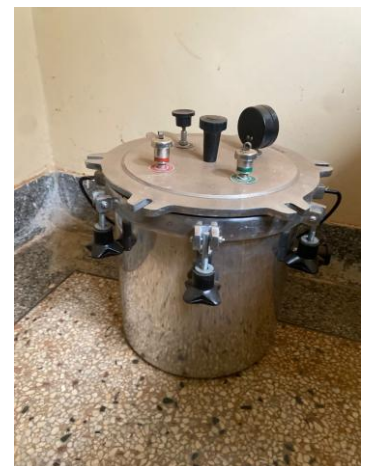


Figure 96: Autoclave at Atar HC III, Kween District (Sebei)



Figure 97: Kangaroo care chair at Atar HC III, Kween District (Sebei)



Figure 98: Binocular microscope on a trolley at Namusita HC III, Budaka District (Bukedi)



Figure 99: Infant weighing scales at Namusita HC III, Budaka District (Bukedi)

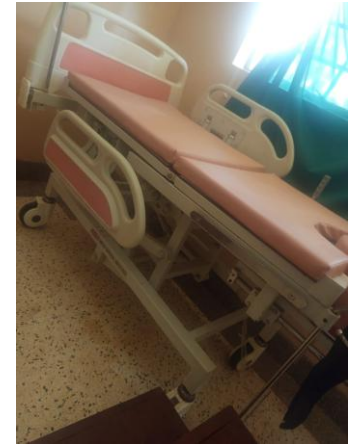


Figure 100: Delivery bed with side rails at Kabweri HC III, Kibuku District (Bukedi)

Figures 101 to 110 show health centre buildings and the power, water and sanitation installations that serve them, including solar panels and batteries, a power house, latrine and sanitation blocks, a waste disposal structure and water tanks.



Figure 101: Health centre building, Nwoya District (Acholi)



Figure 102: Solar panels at Kalemungole HC III, Moroto District (Karamoja)



Figure 103: Patient toilet block at Kalemungole HC III, Moroto District (Karamoja)



Figure 104: Power house at Kyabasara HC III, Kagadi District (Bunyoro)



Figure 105: Latrine block and paved access at Kyabasara HC III, Kagadi District (Bunyoro)



Figure 106: Solar batteries at Bunangaka HC III, Bulambuli District (Bugisu)



Figure 107: Solar batteries and control equipment at Atar HC III, Kween District (Sebei)



Figure 108: Sanitation block with external handwashing basins at Kibiri HC III, Makindye-Ssabagabo Municipal Council (Buganda)



Figure 109: Waste disposal structure at Kibiri HC III, Makindye-Ssabagabo Municipal Council (Buganda)



Figure 110: Water tanks on a steel tower at Kabweri HC III, Kibuku District (Bukedi)

Seed schools

Figures 111 to 128 show furniture and teaching equipment at seed schools, including laboratory benches and stools, laboratory glassware, anatomical teaching models, classroom desks, library shelving and computer equipment.



Figure 111: Science laboratory tables and stools at a seed secondary school, Kalangala District (Buganda)



Figure 112: Library shelves and reading tables at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)

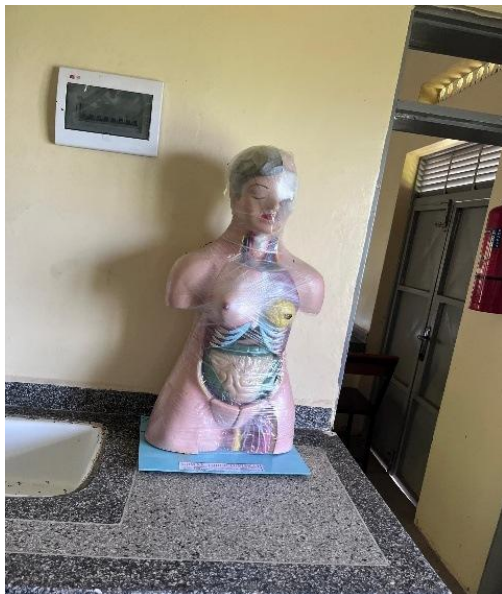


Figure 113: Anatomical teaching model at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)



Figure 114: Laboratory glassware and equipment at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)



Figure 115: Desktop computers and classroom furniture at a seed secondary school, Busia District (Bukedi)



Figure 116: Classroom desks at a seed secondary school, Ntoroko District (Tooro)



Figure 117: Classroom desks at King Solomon Seed Secondary School, Kagadi District (Bunyoro)



Figure 118: Laboratory benches and sinks at Bweema Seed Secondary School, Buvuma District (Buganda)



Figure 119: Classroom desks at Bweema Seed Secondary School, Buvuma District (Buganda)



Figure 120: Laboratory supplies and an anatomical teaching model at Rupa Seed School, Moroto District (Karamoja)



Figure 121: Computer equipment in the school ICT room at Kabeywa Seed Secondary School, Kapchorwa District (Sebei)



Figure 122: Library shelving and tables at Kabeywa Seed Secondary School, Kapchorwa District (Sebei)



Figure 123: Office desk and other furniture at Lwamata Town Council Seed Secondary School, Kiboga District (Buganda)



Figure 124: Laboratory tables at Lwamata Town Council Seed Secondary School, Kiboga District (Buganda)



Figure 125: Library shelving at Lwamata Town Council Seed Secondary School, Kiboga District (Buganda)

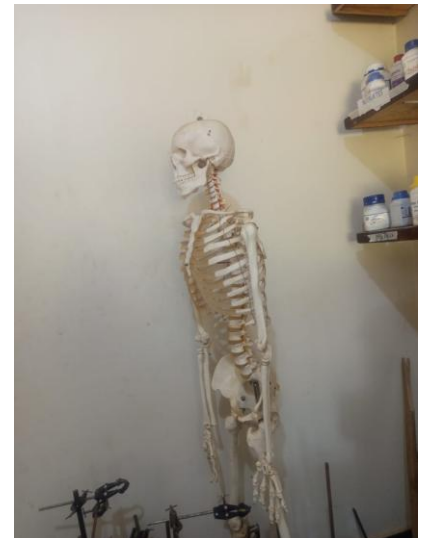


Figure 126: Anatomical skeleton teaching model at Kamankoli Seed Secondary School, Budaka District (Bukedi)



Figure 127: Laboratory benches, stools and sinks at Nansanga Seed Secondary School, Budaka District (Bukedi)



Figure 128: Library shelving with books at Nansanga Seed Secondary School, Budaka District (Bukedi)

Figures 129 to 144 show seed school buildings and the water, sanitation and gas installations that serve them, including school blocks, a science laboratory, a computer and library block, water storage tanks, a borehole, a sanitation block and gas cylinders with their pipework.



Figure 129: Buildings at a seed secondary school, Nwoya District (Acholi)



Figure 130: School blocks at Gyagenda Memorial Seed Secondary School, Kalangala District (Buganda)



Figure 131: School buildings and courtyard at a seed secondary school, Buvuma District (Buganda)



Figure 132: Raised water storage tank at a seed secondary school, Buvuma District (Buganda)



Figure 133: Sanitation block at Bweema Seed Secondary School, Buvuma District (Buganda)



Figure 134: Water tank and enclosed service structures at Bweema Seed Secondary School, Buvuma District (Buganda)



Figure 135: Borehole apron and pipework at Katikekire Seed School, Moroto District (Karamoja)



Figure 136: Section of the science laboratory exterior at Iriiri Seed Secondary School, Napak District (Karamoja)



Figure 137: Water storage tanks at Lopei Seed Secondary School, Napak District (Karamoja)



Figure 138: Computer and library block at Lopei Seed Secondary School, Napak District (Karamoja)



Figure 139: Water tanks on a rendered plinth and steel tower at Alerek Seed Secondary School, Abim District (Karamoja)



Figure 140: Water storage tanks at Rengen Seed School, Kotido District (Karamoja)



Figure 141: Gas cylinders and pipework at King Solomon Seed Secondary School, Kagadi District (Bunyoro)



Figure 142: Water tank on a masonry support at King Solomon Seed Secondary School, Kagadi District (Bunyoro)



Figure 143: Elevated water tank on a steel tower at King Solomon Seed Secondary School, Kagadi District (Bunyoro)



Figure 144: Rainwater tank beside a staff house at Rupa Seed School, Moroto District (Karamoja)
